

Airport Projects Update

As of November 18, 2020

T-Hangar Row E Construction

Construction is underway, contractor has been on-site since October 26. Erosion controls have been installed and site has been stripped. Construction of the building foundation is underway with excavation and fill of select material as a base for the building foundation. Formwork and installation of reinforcing steel is next. Concrete pour of the slab is scheduled for the week of November 30.

Photos of the work



Figure 1- Installation of Filter Dam



Figure 2 - Stripping topsoil for grading



Figure 3- Folding Sand into Existing Fill



Figure 4 - Select fill mixing on the building foundation

Rates and Charges Study / Update of Airport Fees

Analysis of existing airport rates and charges has been completed and provide to the airport as guidance for setting new fees. The analysis also include documenting fee analysis for future needs like ground leases and Customs and Border Patrol services should the airport initiate agreements to accept international flights.

Taxiway A Design

Survey of the airfield is underway, while field investigation of the soil for the relocated taxiway was completed on October 10. Preliminary Engineering is underway, with the engineering report that will define the project scope and estimate the project construction cost scheduled for completion in early March. An exhibit showing possible exit taxiway locations is on display at the airport to gather stakeholder input on preferences of the proposed configuration.

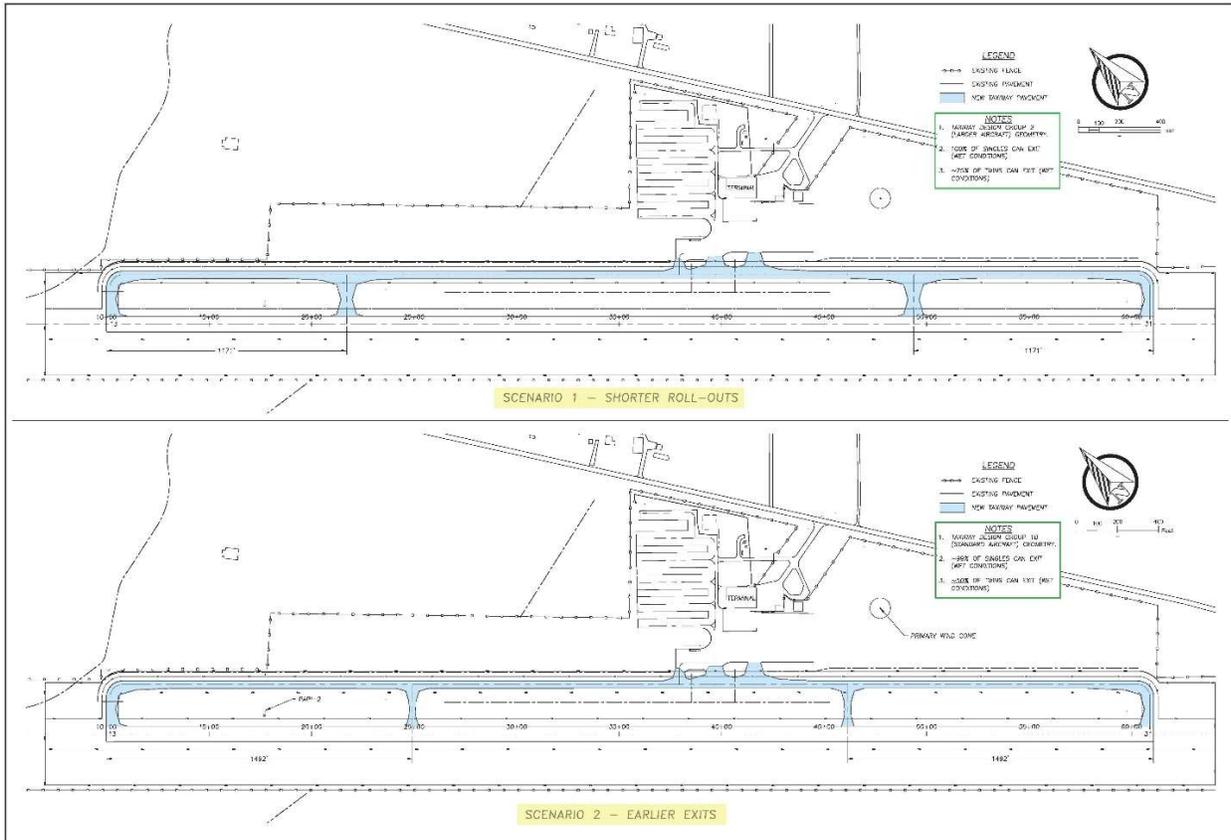


Figure 5 - Exit taxiway optional geometry
