

# Biweekly Construction Summary City of Bonifay



**Project Title:** Bonifay Southside Drainage Improvements

DHM Project ID # BON25CD


**Work performed the week of:** October 20, 2025 Through November 2, 2025

Holmes County Contact: <u>Sierra Smith, Grants Coordinator</u>	Design Engineer: <u>Rod Adams, P.E., DHM</u>
Contractor Project Mgr: <u>Kenneth Jenkins, GCUC</u>	CEI Project Mgr: <u>Jake Mathis, DHM</u>
Distribute To: <u>Larry Cook, Mayor of Bonifay</u> <u>Sierra Smith, City of Bonifay</u> <u>Kenneth Jenkins, GCUC</u> <u>Chris Corbin, GCUC</u>	Senior Inspector: <u>Sandra Toole, DHM</u> <u>David Melvin, DHM Engineering</u> <u>Brent E. Melvin, P.E., DHM Engineering</u> <u>Rod Adams, DHM Engineering</u> <u>Jake Mathis, DHM Engineering</u>

Notice To Proceed Date: <u>June 16, 2025</u>	
Substantial Completion Date: <u>November 26, 2025</u>	
Final Completion Date: <u>December 26, 2025</u>	
Previous Contract Amount: <u>\$915,008.25</u>	
Current Contract Amount: <u>\$1,023,292.63</u>	
SA / WCO's Approved No. <u>2</u>	<u>41%</u>
Pay Estimate Approved No. <u>4</u>	<u>43%</u>
Estimated Constr. Complete: _____	<u>72%</u>
Contract Time Used: _____	

Total Contract Days:	<u>194</u>
Previous Contract Days:	<u>150</u>
Contract Day:	<u>140</u>
Substantial Days Remaining:	<u>24</u>
Final Days Remaining:	<u>54</u>
Total Weather Days:	<u>3</u>
Total Holidays:	<u>1</u>

Project is on Schedule?     X     Yes      No



**Description of Work:**

**Accomplishments:**

Clifford St, Jernigan Ave, and Hightower Ave, all work completed.  
Walk-Thru conducted on 10/10/25 for Clifford St, Jernigan Ave, & Hightower Ave.  
Subcontractor completed 4" sewer and 8" waterline bores on St. Johns Rd.  
Subcontractor completed all utility tie-ins located on St. Johns Rd.  
Contractor began Road Closure on St. Johns Road on 10/16/2025.  
Message Boards placed for St. Johns Rd 10/10/2025.  
Contractor installed S-1 and S-3 Box Culverts

**Current Activities:**

**GCUC**  
Maintained Message Boards and set up Detour Signs and Road Closure for St. Johns Rd.  
Contractor remove remaining existing guardrail post on St. Johns Rd.  
Contractor completed punch list items for Hightower Ave. and Jernigan Ave.  
Contractor installed S-1 and S-3 Box Culverts.  
Contractor primed and placed joint sealant on all Box Culvert joints.  
Contractor grouted joints and lift holes.

**A & W Contracting**

No Work This Period.

**Holiday & Weather Days**

Holiday's = Sept. 1, 2025  
Weather days = August 4, 13, October 27, 2025

**Pending Issues:**

NONE

**Potential Problems:**

NONE

**Project Changes:**

Work Change #1 added 30 days for utility issues on St. Johns Rd.  
Work Change #2 Added 14 days for work change #3 and #4 for equipment and labor on utility issues for St. Johns Rd. and Hightower Ave.  
Work Change added two concrete driveway aprons in exchange for Mr. Fisher signing the easement for lateral ditch excavation.

**Future:**

Tightline, Subcontractor to begin existing S-2 Box Culvert footings, Culvert extensions and forming endwalls.

Jake Mathis  
Construction Project Manager




City of Bonifay / Bonifay Drainage Improvements  
Construction Photos



St. Johns Rd  
Contractor excavated for S-1 Box Culverts and installed 1 LF thick rock bed & checking grades



St. Johns Rd  
Contractor setting Box Culverts for S-1

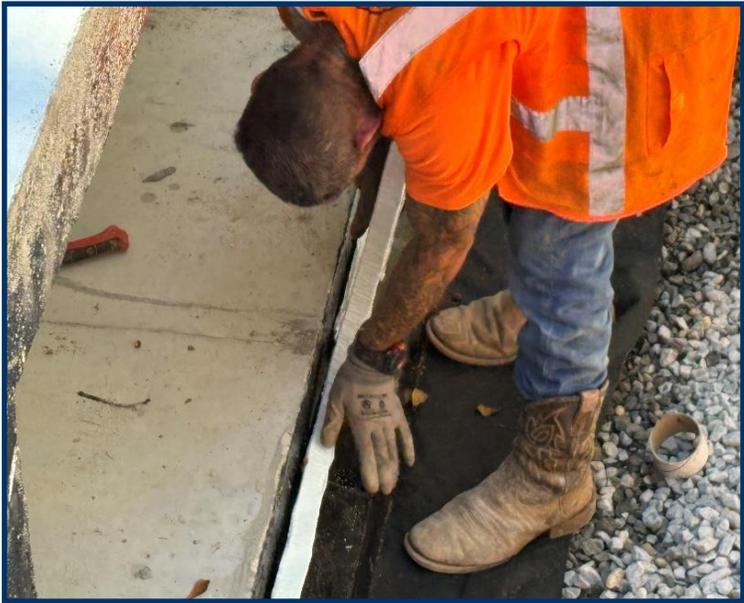

St. Johns Rd  
Contractor installing joint seal on primed tongue and grooves of Box Culverts



St. Johns Rd.  
Contractor grouting all outside joints and lift holes on S-1 Box Culverts



City of Bonifay / Bonifay Drainage Improvements  
Construction Photos



St. Johns Rd  
Contractor completed S-1 Box Culverts  
All joints wrapped with filter fabric



St. Johns Rd  
J & M testing compacted lifts of backfill West side of S-1



St. Johns Rd  
J & M testing compacted lifts of backfill between  
S-1 and existing S-2 Box Culverts



St. Johns Rd.  
Contractor installing S-3 East Side of existing S-2  
Box Culverts



City of Bonifay / Bonifay Drainage Improvements  
Construction Photos



St. Johns Rd  
Contractor setting up box culvert puller in S-3 Box Culverts



St. Johns Rd  
Contractor installing S-3 Box Culverts



St. Johns Rd  
View inside S-3 Box Culverts



St. Johns Rd.  
Contractor grouting joints and lift holes for S-3 Box Culverts inside and outside

