

Biweekly Construction Summary

City of Bonifay



Project Title: City of Bonifay Resilient Stormwater Park

Grant #23FRP18

DHM Project ID # BON23RE


Work performed the week of: April 7, 2025 Through April 20, 2025

Holmes County Contact:	<u>Ricky Callahan, City Clerk</u>	Design Engineer:	<u>Brent E. Melvin, P.E., DHM</u>
Contractor Project Mgr:	<u>Adam Albritton, ECSC, LLC</u>	CEI Project Mgr:	<u>Jake Mathis, DHM</u>
Distribute To:	<u>Larry Cook, Mayor of Bonifay</u> <u>Ricky Callahan, City of Bonifay</u> <u>Sierra Smith, City of Bonifay</u> <u>Adam Albritton, ECSC, LLC</u>	Inspector :	<u>Tommy Hays, DHM</u>
			<u>David Melvin, DHM Engineering</u> <u>Brent E. Melvin, P.E., DHM Engineering</u> <u>Jake Mathis, DHM Engineering</u>

Notice To Proceed Date:	<u>March 24, 2025</u>
Substantial Completion Date:	<u>October 19, 2025</u>
Final Completion Date:	<u>November 18, 2025</u>
Contract Amount:	<u>\$1,988,938.94</u>
Current Contract Amount:	<u>\$1,935,890.39</u>
SA / WCO's Approved No.	<u>1</u>
Pay Estimate Approved No.	<u>0</u>
Estimated Constr. Complete:	<u>15%</u>
Contract Time Used:	<u>11%</u>

Project is on Schedule? X Yes No

Total Contract Days:	<u>240</u>
Contract Day:	<u>28</u>
Substantial Days Remaining:	<u>182</u>
Final Days Remaining:	<u>212</u>
Total Weather Days:	<u>4</u>
Total Holidays:	<u>0</u>

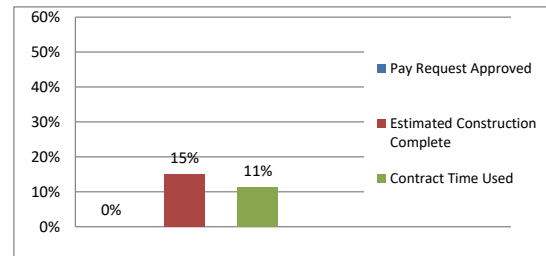

Description of Work:

Accomplishments:

Contractor installed advanced warning road signs.
Contractor removed and hauled off 98% of existing concrete.
Contractor installed 100% of silt fence and with staked hay bales as needed per plans.
Contractor loaded and hauled off 3240 CY of fill dirt.
Contractor cleared and grubbed existing trees per plans.

Current Activities:

ECSC

Contractor removed existing guardrail and box culvert on Moody Street per plans.
Contractor milled up 1" of existing asphalt pavement on Depot and Moody Street and Banfil Ave.
Contractor removed and hauled off 73.3 SY of existing concrete.
Contractor cutting and removing existing dirt out to set grades for stormwater pond.

Corbin Contracting & Underground

No work This Period

Extreme Land Restoration

No work This Period

Highway Specialties

No work This Period

Holiday & Weather Days

Holiday's = 0

Weather days = March 31, 2025, April 1,7, 8 2025

Pending Issues:

NONE

Potential Problems:

NONE

Project Changes:

Future:

Contractor to continue to remove dirt to set grades for stormwater pond.
Contractor to install 60" Pipe w/60" MES.

Jake Mathis
Construction Project Manager

DHM Melvin
Engineering

City of Bonifay / Resilient Stormwater Park
Construction Photos



Resilient Stormwater Park
Contractor removing guardrails on Moody Street.



Resilient Stormwater Park
Contractor demoing concrete pad on Moody Street.



Resilient Stormwater Park
Contractor removing existing box culvert on Moody Street.



Resilient Stormwater Park
Contractor grading and shaping slope for Stormwater Pond per plans.



City of Bonifay / Resilient Stormwater Park
Construction Photos



Resilient Stormwater Park
Contractor milled up existing asphalt on Banfil Ave.



Resilient Stormwater Park
Contractor milled up existing asphalt on Moody Street



Resilient Stormwater Park
VT-Verifying asphalt thickness.



Resilient Stormwater Park
Contractor loading and hauling off material from job site.

