

Deschutes County Courthouse Expansion Update

Board of County Commissioners Meeting

September 29, 2025



Courthouse Expansion Update



- Recently completed and ongoing work
- Construction schedule
- Project budget



Completed: Tower Crane Removal



Completed: Tower Crane Removal



Completed: Tower Crane Removal



Completed: Stair 2



Completed: Mechanical Curbs & Pads



Ongoing: Remodel Phase 1



Ongoing: Mechanical, Electrical, Plumbing



Ongoing: Interior Wall Framing



Ongoing: Exterior Wall Mock-Up



Ongoing: Exterior Wall Construction



Ongoing: Roof Parapet & Screening



Ongoing: Lobby Construction



Ongoing: Main Entry




Upcoming Work

In the coming 4 - 6 weeks...

- **Main Roof Parapet and Penthouse Construction**
- **Exterior Wall Construction**
- **Mechanical, Electrical, and Plumbing Rough-In**
- **Interior Walls and Door Frames**
- **Main Lobby Slab on Grade and Structural Steel**
- **Existing Building Renovation: offices and hearing room**



CONSTRUCTION TIMELINE

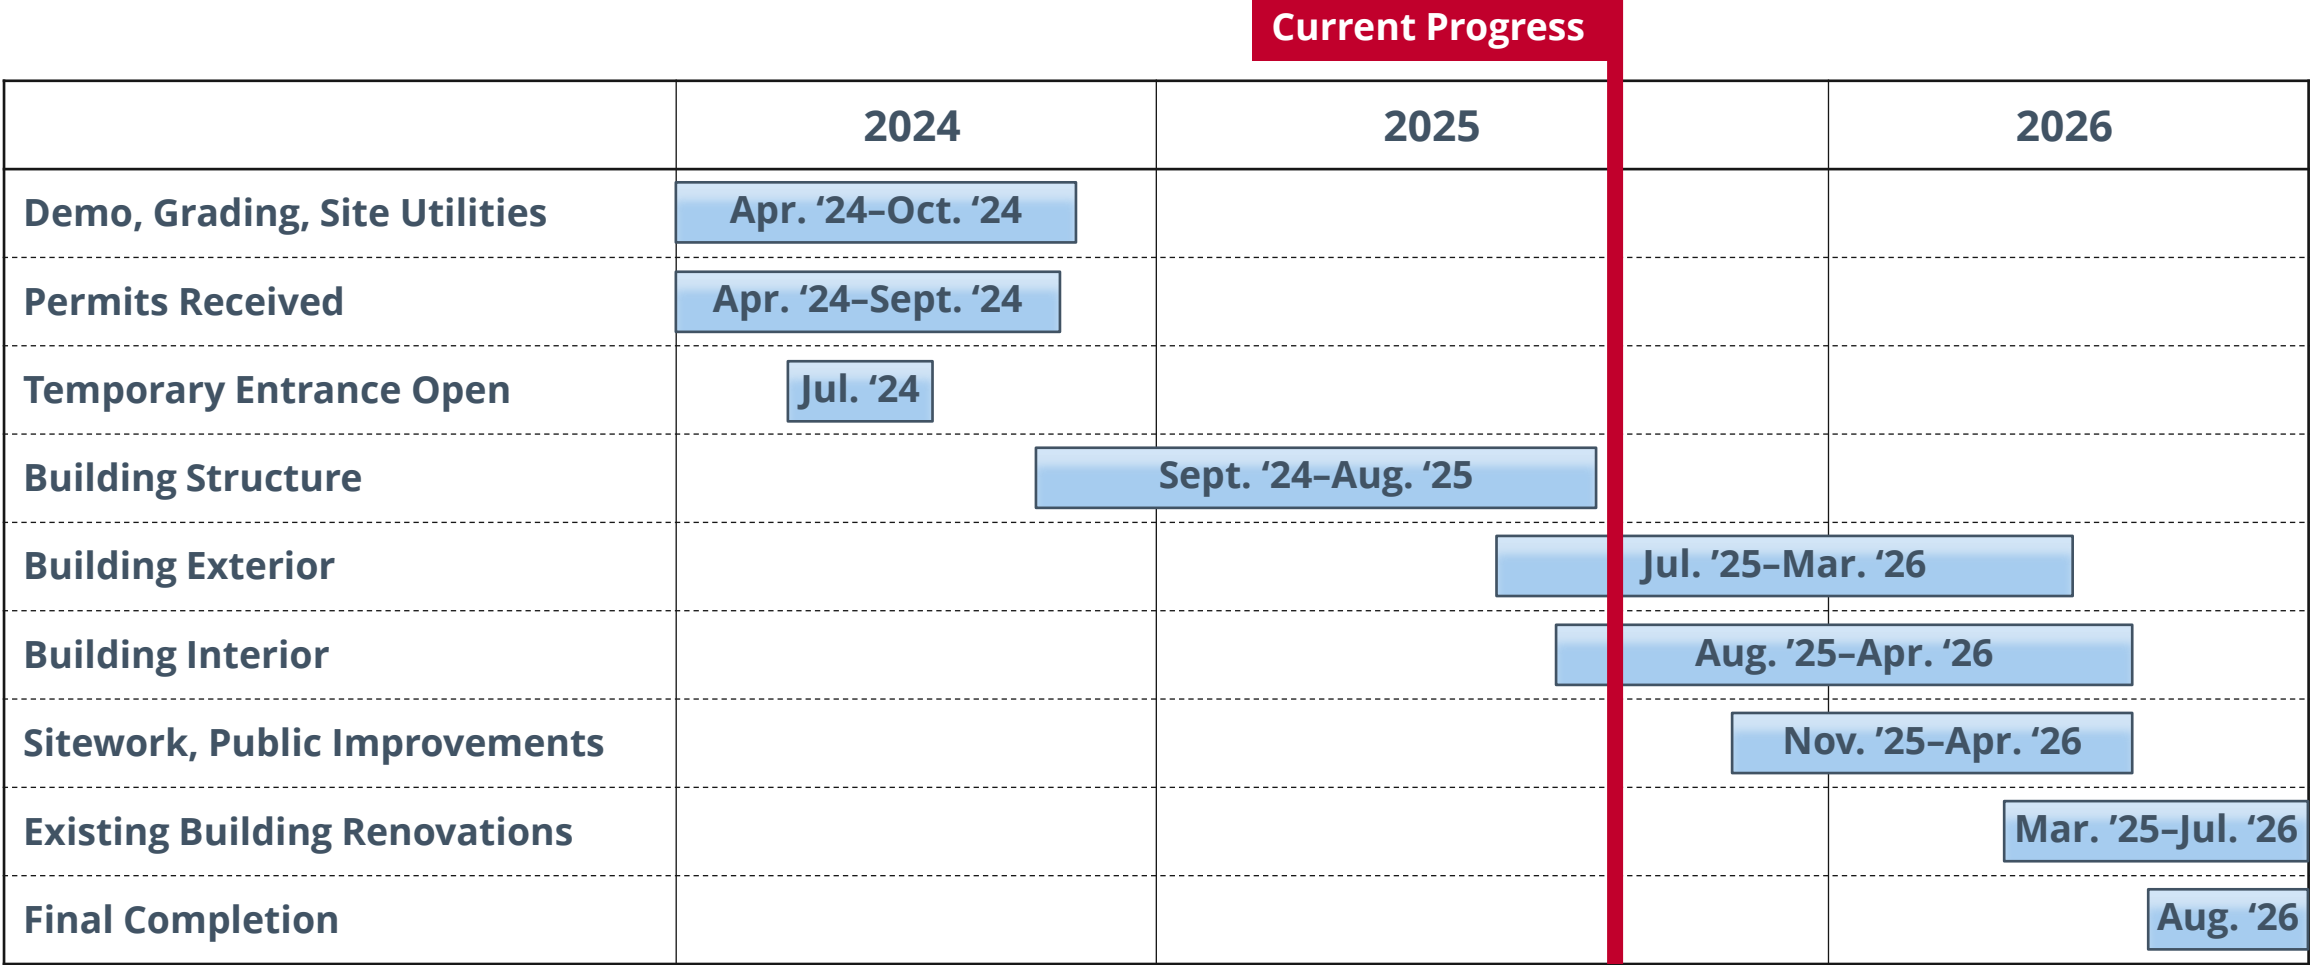

Questions?



Budget Update
