



02 634501 Harrison Fire Rescue Station 70 - Monthly Report (October 2025).xlsx

PROJECT SNAPSHOT



PROJECT NAME & LOCATION:	
Project Name:	Village of Harrison Fire Rescue Station 70
Project Address:	W5662 Manitowoc Road Harrison, WI 54952
Contact:	Chad Pelishek

CONSTRUCTION STATUS	
Actual Start Date:	09/08/25
% Complete to Date:	25%
Target Substantial Comp:	07/16/26
Target Final Completion:	07/30/26

PROJECT SUMMARY:
The Project consists of a 21,110 sf new fire station facility located at W5662 Manitowoc Rd. Harrison, WI 54915

UPCOMING MEETINGS AND SITE VISITS:	
Weekly	Construction Meeting Tues 10/21/2025
Weekly	Construction Meeting Tues 10/28/2025
Weekly	Construction Meeting Tues 11/4/2025
Notes:	Owner Meeting Tues 10/28/2025 (Bi-Weekly)

4 WEEK OUTLOOK:	
WEEK 1 09.29.25	Masonry continue, under ground utilities, footings and foundation walls. Electrical install in CMU.
WEEK 2 10.06.25	Underslab Mechanical, Electrical and Plumbing utilities, CMU at Training Tower,
WEEK 3 10.13.25	CMU Bearing walls at mezzanine/Low Roof/ Apparatus Bay
WEEK 4 10.20.25	Exterior Wall Framing


CONTRACTOR FINANCIAL COMPLETION STATUS					
ID	COMPANY	% TO DATE	ON TRACK	PLAN OF ACTION	ACTION ITEMS
EOR	Wendel	70	Yes		
GC	Miron Construction	7	Yes		
FP	Pace Corporation Fire	0	Yes		
PC	IKM Project Solutions	23	Yes		
MC	Johnson and Jonet	1	Yes		
EC	VOE Power Systems	12	Yes		

WORK COMPLETED THIS MONTH

Harrison Fire-Rescue Station #70 Update 10/20/2025

- 9/29-10/03 Continue Foundations for Main Building and began the installation of the CMU block
- 10/06-10/24 Contractors continued to install the underground utilities for the MEP systems.
- 10/01/-10/10 Installation of the CMU at the Training Tower
- 10/13-10/27 Installation of the bearing walls at the Mezzanine, Low Roof and Apparatus Bay areas
- 10/20 Begain the installation of the exterior wall framing.
- 9/29-10/24 Grade & Rock North Driveway



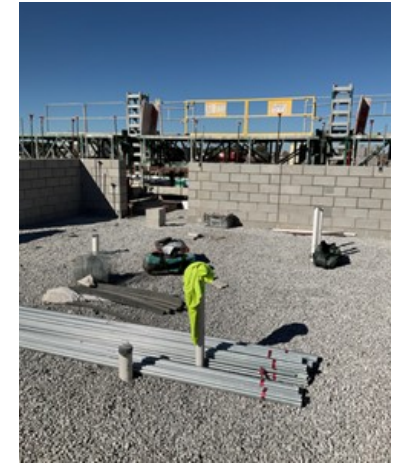



02 634501 Harrison Fire Rescue Station 70 - Monthly Report (October 2025).xlsx
PROJECT BUDGET

CONTRACTOR CONSTRUCTION COST

REF	DESCRIPTION	ORIGINAL CONTRACT	APPROVED CO to DATE	PENDING CO to DATE	TOTAL EST CONTRACT	BILLED PREVIOUSLY	BILLED THIS CYCLE	COST COMPLETE	% COMP	REMAINING BALANCE
GC SC	Miron Construction	6,868,866.00	-	-	6,868,866.00	-	450,188.85	450,188.85	7	6,418,677.15
FP	Pace Corporation Fire Protection	110,544.00	-	-	110,544.00	-	-	-	0	110,544.00
PC	IKM Building Solutions	662,001.00	-	-	662,001.00	-	154,128.00	154,128.00	23	507,873.00
MC	Johnson & Jonet	1,062,700.00	-	-	1,062,700.00	-	9,357.50	9,357.50	1	1,053,342.50
EC	VOE Power Systems	894,129.00	-	-	894,129.00	-	106,211.90	106,211.90	12	787,917.10
Total Contractor Cost		9,598,240.00	-	-	9,598,240.00	-	719,886.25	719,886.25	9	8,878,353.75

PROFESSIONAL SERVICE COST

REF	DESCRIPTION	ORIGINAL CONTRACT	APPROVED CO to DATE	PENDING CO to DATE	TOTAL EST CONTRACT	BILLED PREVIOUSLY	BILLED THIS CYCLE	COST COMPLETE	% COMP	REMAINING BALANCE
Design Contract								-		-
10	Study	18,500.00	-	-	18,500.00	18,500.00		18,500.00	100	-
20	Schematic Design	112,000.00			112,000.00	112,000.00		112,000.00	100	-
30	Design Development	112,000.00			112,000.00	112,000.00		112,000.00	100	-
50	Construction Documents	196,000.00			196,000.00	196,000.00		196,000.00	100	-
60	Bidding	28,000.00			28,000.00	28,000.00		28,000.00	100	-
70	Construction Administration	112,000.00			112,000.00	22,400.00	11,200.00	33,600.00	30	78,400.00
95	Cost of Work Fee Alteration	115,030.00			115,030.00	92,024.00		92,024.00	80	23,006.00
R40	Reimbursable Expenses	500.00	-	-	500.00	500.00		500.00	100	-
R41	Expenses SD-CA	10,000.00			10,000.00	6,697.93	833.61	7,531.54	75	2,468.46
Construction Contract								-		-
52	PreConstruction	30,000.00	-	-	30,000.00	30,000.00		30,000.00	100	-
80	CM Labor	456,000.00	-	-	456,000.00	19,045.00	37,957.50	57,002.50	13	398,997.50
84	CM Fee	289,298.49	-	-	289,298.49			-	0	289,298.49
R40	Expenses	72,000.00	-	-	72,000.00		4,268.90	4,268.90	6	67,731.10
Total Professional Service Cost		1,551,328.49	-	-	1,551,328.49	637,166.93	54,260.01	691,426.94	70	859,901.55



OWNER COSTS

REF	DESCRIPTION	ORIGINAL CONTRACT	APPROVED CO to DATE	PENDING CO to DATE	TOTAL EST CONTRACT	BILLED PREVIOUSLY	BILLED THIS CYCLE	COST COMPLETE	% COMP	REMAINING BALANCE
1	PSI - 3rd Party Inspection	24,350.00	-	-	24,350.00	-	-	-	0	24,350.00
Total Owner Cost		24,350.00			24,350.00				0	24,350.00
Total Contractor Cost		9,598,240.00	-	-	9,598,240.00	-	719,886.25	719,886.25	8.52	8,878,353.75
Total Professional Service Cost		1,551,328.49	-	-	1,551,328.49	637,166.93	54,260.01	691,426.94	70	859,901.55
Total Owner Cost		24,350.00	-	-	24,350.00	-	-	-	-	24,350.00
TOTAL PROJECT BUDGET		11,173,918.49	-	-	11,173,918.49	637,166.93	774,146.26	1,411,313.19	78	9,762,605.30

Note: All Billings are thru September 30, 2025



02 634501 Harrison Fire Rescue Station 70 - Monthly Report (October 2025).xlsx
CHANGE ORDER LOG

PROJECT INFORMATION:		
Project Name: Village of Harrison Fire Rescue Station 70	Original Contract Cost: \$ 9,598,240.00	Type/Reason
Project Address: W5662 Manitowoc Road Harrison, WI 54952	Approved Work: \$ -	CR = Customer request
Contact: Chad Pelishek	Revised Total Contract Cost: \$ 9,598,240.00	UC = Unforeseen cond DO = Design omission FO = Field order

CE No.	Contractor	Description of Work	Type/Reason	Proposal No	Proposal Amount	Amount Approved	Date Received	Date to Owner	Owner Reviewed	Status	Contractor CO No.
01.0											
02.0											
Total					-	-					
