



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/05/2026

Weather: sunny/clear

Temp	
High	Low
75	54

Report No.: 1
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
<p>Contractor mobilized equipment to site, including one mini-excavator, one skid steer, and steel trench protection. Project engineer Ibraheem Aburumman met with the crew on site to review scope and discuss the planned setup for the directional bore. Also completed layout for the work area.</p>	<p>Project engineer Ibraheem Aburumman discussed equipment positioning and the required excavation area to accommodate drilling operations as well as personnel access for pipe and fitting connections. Ibraheem also spoke with nearby homeowners to communicate upcoming work activities</p>

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	1
Clear			No. Days Left	209

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	1	8
Laborer	10	8


Equipment				
Equipment	Model No.	No.	Hours	Stand-by



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

Backhoe	CAT 302.7	1		8
Skid Steer	CAT 236D3	1		8

Pay Items			
Pay Item Desc.	Location	Quantity	
1-Mobilization (max 3% of contract price), complete in place, the sum of:	Ridgeley Dr and Hickory Shadows Dr	0.5	Lump sum

HDR Site Representative 	Supervisor 	Contractor 
---	--	--



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/06/2026

Weather: Sunny/Clear

Temp	
High	Low
80	65

Report No.: 2
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Contractor returned to site to lay out inlet protection barriers and tree protection fencing. Also installed traffic control cones at Ridgley Station. No additional construction activities performed this day.	

Materials Testing - Test Taken & Results	Time Charges		
		Day Charged?	Yes
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used
clear			No. Days Left
			210
			2
			208

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	1	4
Laborer	5	4


Equipment				
Equipment	Model No.	No.	Hours	Stand-by
Backhoe	CAT 302.7	1		8
Skid Steer	CAT 263D3	1		8



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

--	--	--	--	--

Pay Items			
Pay Item Desc.	Location	Quantity	
4-Storm Water Pollution Prevention Plan, complete in place, the sum of:	Hickory Shadows Drive	0.5	Lump sum
44-Install Tree Protection fence (up to 5,000 L.F.), complete in place, the sum of:	Hickory Shadows Dr	1,400	Linear feet

HDR Site Representative	Supervisor	Contractor
		



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/07/2026

Weather: Sunny/Clear

Temp	
High	Low
79	66

Report No.: 3
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Contractor begin & completed demolition of driveway for 1027 Ridgeley for bore pit. Concrete was removed (26'x16') for bore pit at sta: 3+00. Contractor also excavated bore pit for water line installation at sta: 4+73.71. Drilling was completed from sta: 3+00 - 4+73.71. No 8" PVC C-900 installed this day. Only drilling.	Met the owner of Arnold & Co (Randy Arnold) & project engineer (Ibraheem Aburumman). I was explained planned work activities for the day. Myself, Randy, & Ibraheem also met with Cassie Stephens at City Hall to discuss work activities. Cassie instructed us that if any issues occurred involving residents to contact Hilshire Village police department and that they have been notified of on going construction activities.

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	3
clear			No. Days Left	207

Manpower		
Labor Force/Sub	No.	Hours
Laborer	9	10
Supervisor	1	10
Operator	1	10
Other Flagger	1	10
Foreman	1	10

Equipment				
Equipment	Model No.	No.	Hours	Stand-by



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

Skid Steer	CAT 236D3	1	10	
Backhoe	CAT 302.7	1	10	
Other Directional drilling rig	Vermeer D7x11	1	10	

Pay Items			
Pay Item Desc.	Location	Quantity	

HDR Site Representative 	Supervisor 	Contractor 
---	--	--

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Bore pit at 1027 Ridgely
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Boring sub-contractor
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Bore pit on Ridgeley at sta: 4+73.71
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



8" C-900 waterline
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Drilling at sta: 4+73.71



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/08/2026

Weather: sunny/clear

Temp	
High	Low
77	68

Report No.: 4
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Contractor removed concrete from driveway at 12 Hickory Shadows Dr. 13'x17' was removed. Contractor also continued drilling/boring from sta: 3+00 - 4+73.71. During drilling excessive ground force was encountered and as a result contractor moved drilling over approx 5' and redrilled/bored. No C-900 was installed.	Sanitray service line was hit during drilling at approx. sta 3+50. Contractor removed additional concrete driveway and repaired service line

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	4
clear			No. Days Left	206

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	1	10
Foreman	1	10
Operator	1	10
Laborer	10	10

Equipment				
Equipment	Model No.	No.	Hours	Stand-by



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

Backhoe	CAT 302.7	1	10	
Skid Steer	CAT 236D3	1	10	
Other Directional drilling rig	Vermeer D7x11	1	10	

Pay Items			
Pay Item Desc.	Location	Quantity	

HDR Site Representative 	Supervisor 	Contractor 
---	--	--

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Drilling/boring from sta: 3+00 - 4+73.71

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Removing concrete driveway at 12 Hickory Shadows Dr



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/09/2026

Weather: sunny/clear

Temp	
High	Low
81	55

Report No.: 5
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Contractor continued drilling/boring from sta: 3+00 - 4+73.71. No C-900 was installed.	Teams meeting with Efrain, Ngoc, Randy, & Ibrahim to discuss existing ductile iron at sta: 4+73. Efrain instructed contractor to connect the new 8-inch water line from Hickory Shadows to the Ridgeley Drive 8-inch water line by reconnecting to the same tee, replacing the existing 8-inch gate valve and performing the offset, in lieu of the proposed 8-inch x 8-inch TS&V. Inspector walked and took pictures for potential relocation of fire hydrant at sta: 2+53

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	5
clear			No. Days Left	205

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	1	10
Foreman	1	10
Laborer	8	10

Equipment				
Equipment	Model No.	No.	Hours	Stand-by



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

Backhoe	CAT 302.7	1	10	
Skid Steer	CAT 236D3	1	10	
Other directional drilling rig	Vermeer D7x11	1	10	

Pay Items			
Pay Item Desc.	Location	Quantity	

HDR Site Representative 	Supervisor 	Contractor 
---	--	--

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Contractor performing investigating excavation to find reason for excessive force during boring/drilling
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Repair of damaged sanitary service line for 1027 Ridgeley



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/10/2026

Weather: sunny/clear

Temp	
High	Low
57	39

Report No.: 6
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
No work this day - Saturday	

Materials Testing - Test Taken & Results	Time Charges			
		Day Charged?	Yes	No. Contract Days
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	6
sunny/clear			No. Days Left	204

Manpower		
Labor Force/Sub	No.	Hours

Equipment				
Equipment	Model No.	No.	Hours	Stand-by

Pay Items		
Pay Item Desc.	Location	Quantity

HDR Site Representative	Supervisor	Contractor



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/11/2026

Weather: sunny/clear

Temp	
High	Low
66	43

Report No.: 7
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
No work this day - Sunday	

Materials Testing - Test Taken & Results	Time Charges			
		Day Charged?	Yes	No. Contract Days
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	7
sunny/clear			No. Days Left	203

Manpower		
Labor Force/Sub	No.	Hours

Equipment				
Equipment	Model No.	No.	Hours	Stand-by

Pay Items		
Pay Item Desc.	Location	Quantity

HDR Site Representative	Supervisor	Contractor



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/12/2026

Weather: sunny/clear

Temp	
High	Low
62	46

Report No.: 8
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Contractor continued drilling/boring from sta: 3+00 - 4+73.71. 154.72 LF C-900 was installed.	Inspector Montreal Bailey not onsite this day (family emergency). Cole Quake covered daily observations.

Materials Testing - Test Taken & Results	Time Charges		
		Day Charged?	Yes
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used
clear			No. Days Left
			210
			8
			202

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	1	10
Foreman	1	10
Operator	1	10
Laborer	8	10

Equipment				
Equipment	Model No.	No.	Hours	Stand-by
Backhoe	CAT 302.7	1	10	
Skid Steer	CAT 263D3	1	10	
Other directional drilling rig	Vermeer D7X11	1	10	



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

Pay Items			
Pay Item Desc.	Location	Quantity	
25-Furnish and Install 8" PVC C-900, DR 18 Water Line & Fittings, including restrained joints, by Auger Construction, complete in place, the sum of:	sta: 3+00 - 4+73.71	154.72	Linear feet
39-Trench Protection for Water Line, complete in place, the sum of:	Ridgley	100	Linear feet

HDR Site Representative	Supervisor	Contractor
		

Photo(s) of day's work




Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



8" PVC C-900 waterline being installed
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements

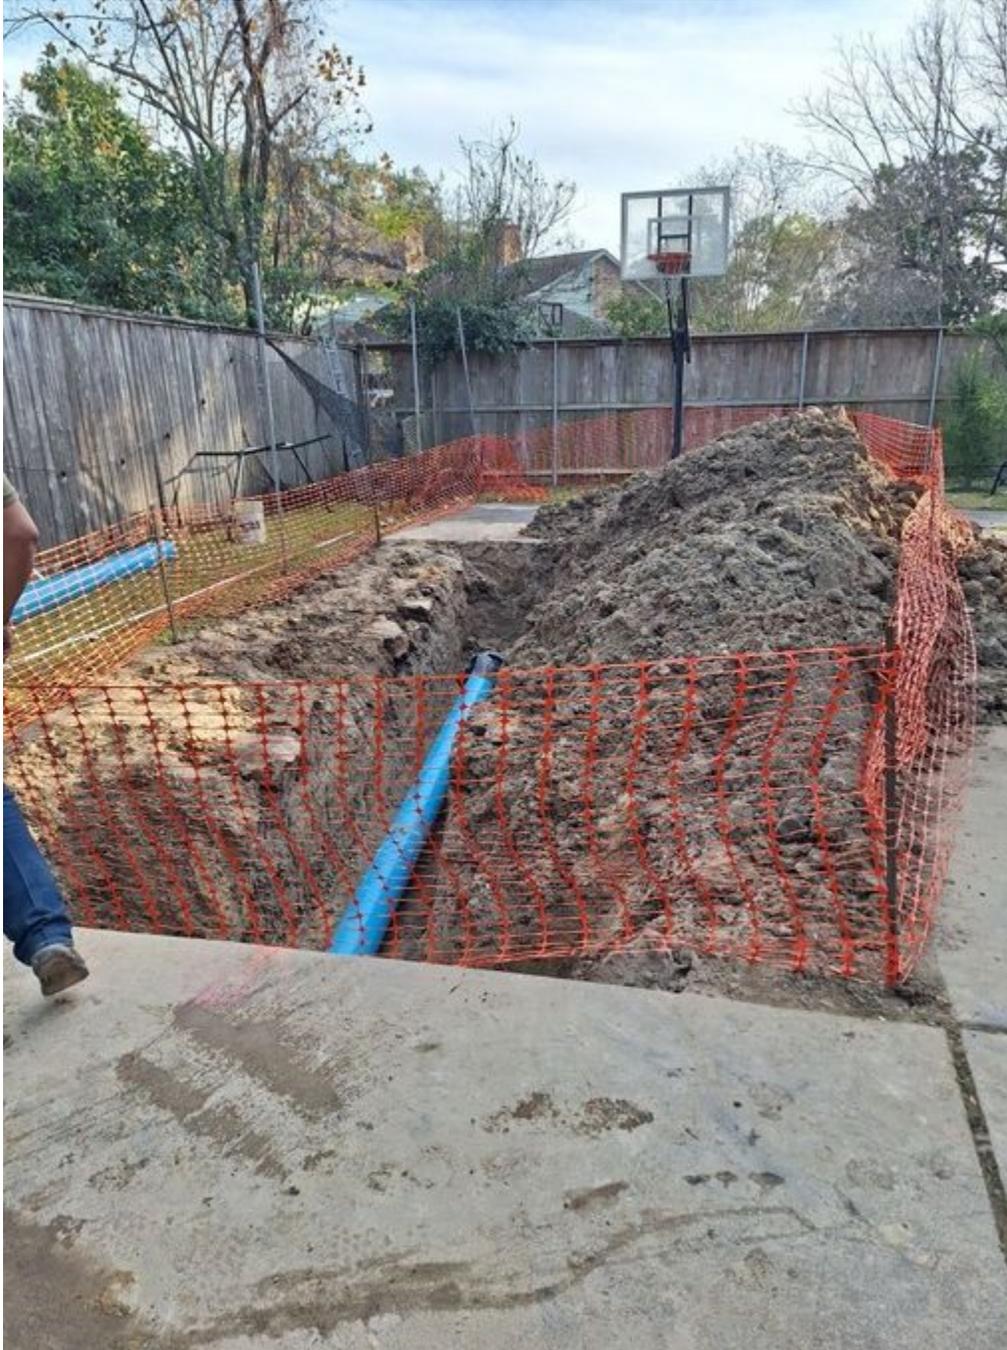

8" PVC C-900 waterline being installed
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Temporary concrete patch placed back in driveway for 1027 Ridgeley Rd



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/13/2026

Weather: cloudy/rain

Temp	
High	Low
56	46

Report No.: 9
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
<p>Contractor continued installation of 8" PVC C-900 from sta: 3+00 - 4+73.71. Pipe was backfilled. Contractor then begin excavating at 12 Hickory Shadow for bore pit for continued drilling/boring from sta: 1+18.23 - 3+00.</p>	<p>Inspector Montreal Bailey not onsite this day (First Aid/CPR training). Cole Quake covered daily observations. Contractor damaged underground power lines at 12 Hickory shaddows at 1:00PM and as a result residents lost electricity. Electricity was repaired by Centerpoint and all residents had working power at 10:00PM.</p>

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	9
clear			No. Days Left	201

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	1	10
Foreman	1	10
Operator	1	10
Laborer	8	10

Equipment				
Equipment	Model No.	No.	Hours	Stand-by
Backhoe	CAT 302.7	1	10	
Skid Steer	CAT 236D3	1	10	



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

Other Directional drilling rig	Vermeer D7x11	1	10	
--------------------------------	---------------	---	----	--

Pay Items			
Pay Item Desc.	Location	Quantity	

HDR Site Representative 	Supervisor 	Contractor 
---	--	--

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Backfilling of waterline at 1027 Ridgeley
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Excavating & drilling at 12 Hickory Shadows (sta: 1+18)



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/14/2026

Weather: sunny/clear

Temp	
High	Low
69	39

Report No.: 10
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Contractor continued drilling/boring from sta: 1+18.23 - 3+00. 171.28 LF C-900 was installed. Contractor then begin excavating at 19 Hickory Shadow for bore pit for drilling/boring from sta: 4+00 - 6+23. Also removed trees 38, 40, 41, 52, 53, 54, 56, 57, 58 per tree protection plan.	

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	10
clear			No. Days Left	200

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	1	10
Foreman	1	10
Operator	1	10
Laborer	7	10

Equipment				
Equipment	Model No.	No.	Hours	Stand-by
Backhoe	CAT 302.7	1	10	



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

Skid Steer	CAT 236D3	1	10	
Other directional drilling rig	Ditch Witch 3020	1	10	

Pay Items			
Pay Item Desc.	Location	Quantity	
25-Furnish and Install 8" PVC C-900, DR 18 Water Line & Fittings, including restrained joints, by Auger Construction, complete in place, the sum of:	sta: 1+18.23 - 3+00 (Ridgley to Hickory Shadows rd)	171.28	Linear feet
41-Remove Tree 0" to 11.99" (or Palm tree), complete in place, the sum of:	40, 41, 52, 54, 56, 57, 58 per tree protection plan	7	Each
42-Remove Tree 12" to 29.99", complete in place, the sum of:	38 & 53 per tree protection plan	2	Each
45-Install Root Pruning Trench, complete in place, the sum of:	sta 4+00 - 6+00	125	Linear feet
43-Clearance Prune Tree, complete in place, the sum of:	sta 4+00 - 6+00	12	Each
39-Trench Protection for Water Line, complete in place, the sum of:	sta: 1+18.23 - 3+00 (Ridgley to Hickory Shadows rd)	219	Linear feet

HDR Site Representative	Supervisor	Contractor
--------------------------------	-------------------	-------------------



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements

		
---	--	---

Photo(s) of day's work



Contractor drilling/boring from sta: 1+18.23 - 3+00 (Ridgley to Hickory Shadows rd)
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Contractor drilling/boring from sta: 1+18.23 - 3+00 (Ridgley to Hickory Shadows rd)
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Contractor installed 8" PVC C-900 waterline from sta: 1+18.23 - 3+00 (Ridgely to Hickory Shadows rd)



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/15/2026

Weather: sunny/clear

Temp	
High	Low
61	46

Report No.: 11
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Contractor continued drilling/boring from sta: 4+00 - 6+23. No waterline was installed.	During drilling/boring from sta: 4+00 - 6+23 excessive water as a result of existing waterline collapse occurred. Inframark was contacted and arrived onsite and turned off water. Contractor then begin excavating to locate and repair damaged waterline. Waterline was located below existing inlet at sta 4+08. Waterline was AC pipe and contractor was unable to perform repair due to pipe damaged location being under existing inlet. Inframark performed waterline repair after hours.

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	11
clear			No. Days Left	199

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	1	15
Foreman	1	15
Operator	1	15
Laborer	7	15

	Equipment



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

Equipment	Model No.	No.	Hours	Stand-by
Backhoe	CAT 302.7	1	10	
Skid Steer	CAT 236D3	1	10	
Other Directional drilling rig	Ditch Witch 3020	1	10	

Pay Items			
Pay Item Desc.	Location	Quantity	
53-Extra Hand Excavation, complete in place, the sum of:	Sta 4+08 (19 Hickory Shadows)	75	Cubic yards
39-Trench Protection for Water Line, complete in place, the sum of:	sta 4+00 - 6+00	219	Linear feet

HDR Site Representative	Supervisor	Contractor
		

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Contractor drilling/boring from sta: 4+00 - 6+23.
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Centerpoint repair of gas service line for 19 Hickory Shadows



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/16/2026

Weather: sunny/clear

Temp	
High	Low
77	51

Report No.: 12
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Contractor continued drilling/boring from sta: 4+00 - 6+23. 421 LF C-900 was installed.	

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	12
clear			No. Days Left	198

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	1	10
Foreman	1	10
Operator	1	10
Laborer	5	10

Equipment				
Equipment	Model No.	No.	Hours	Stand-by
Backhoe	CAT 302.7	1	10	
Backhoe	CAT 306	1	10	
Skid Steer	CAT 299D	1	10	
Other Directional drilling rig	Ditch Witch 3020	1	10	



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

--	--	--	--	--

Pay Items			
Pay Item Desc.	Location	Quantity	
25-Furnish and Install 8" PVC C-900, DR 18 Water Line & Fittings, including restrained joints, by Auger Construction, complete in place, the sum of:	sta: 4+00 - 6+23	421	Linear feet
39-Trench Protection for Water Line, complete in place, the sum of:	sta: 4+00 - 6+23	219	Linear feet

HDR Site Representative	Supervisor	Contractor
		

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



drilling/boring from sta: 4+00 - 6+23



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/17/2026

Weather: sunny/clear

Temp	
High	Low
57	30

Report No.: 13
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
No work this day - Saturday	

Materials Testing - Test Taken & Results	Time Charges			
		Day Charged?	Yes	No. Contract Days
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	13
clear			No. Days Left	197

Manpower		
Labor Force/Sub	No.	Hours

Equipment				
Equipment	Model No.	No.	Hours	Stand-by

Pay Items		
Pay Item Desc.	Location	Quantity

HDR Site Representative	Supervisor	Contractor



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/18/2026

Weather: sunny/clear

Temp	
High	Low
58	34

Report No.: 14
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
No work this day - Sunday	

Materials Testing - Test Taken & Results	Time Charges			
		Day Charged?	Yes	No. Contract Days
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	14
clear			No. Days Left	196

Manpower		
Labor Force/Sub	No.	Hours

Equipment				
Equipment	Model No.	No.	Hours	Stand-by

Pay Items		
Pay Item Desc.	Location	Quantity

HDR Site Representative	Supervisor	Contractor



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/19/2026

Weather: Sunny

Temp	
High	Low
67	37

Report No.: 15
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Bore pits were dug in preparation for water line installation.	

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	15
Clean site with material stored near park. Bore pits are open awaiting water line installation.			No. Days Left	195

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	3	
Operator	4	
Laborer	4	

Equipment				
Equipment	Model No.	No.	Hours	Stand-by
Excavator		2		
Skid Steer		2		

Pay Items			
Pay Item Desc.	Location	Quantity	



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements

HDR Site Representative	Supervisor	Contractor
		

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Water line pipe
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Equipment and material stored near park.
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Bore pit outside of 24 Hickory Shadows Drive
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Bore pit outside of 12 Hickory Shadows Drive



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/20/2026

Weather: Cloudy

Temp	
High	Low
63	48

Report No.: 16
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Continued excavating/hand digging for bore pits, began directional drilling, water line installation, and installed temporary storm sewer pipe	

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	16
			No. Days Left	194

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	2	
Foreman	2	
Laborer	12	

Equipment				
Equipment	Model No.	No.	Hours	Stand-by
Other Directional drill		1		
Excavator		1		
Dump Truck		1		



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

Pay Items			
Pay Item Desc.	Location	Quantity	
25-Furnish and Install 8" PVC C-900, DR 18 Water Line & Fittings, including restrained joints, by Auger Construction, complete in place, the sum of:		340	Linear feet

HDR Site Representative	Supervisor	Contractor
		

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Water line at bore pit outside of 12 Hickory Shadows Drive
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Temporary storm sewer outside of 19 Hickory Shadows Drive
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Directional drilling equipment
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Water line pipe



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/21/2026

Weather: rain/cloudy

Temp	
High	Low
69	60

Report No.: 17
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
No work this day due to rain	

Materials Testing - Test Taken & Results	Time Charges			
		Day Charged?	Yes	No. Contract Days
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	17
			No. Days Left	193

Manpower		
Labor Force/Sub	No.	Hours

Equipment				
Equipment	Model No.	No.	Hours	Stand-by

Pay Items		
Pay Item Desc.	Location	Quantity

HDR Site Representative	Supervisor	Contractor



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/22/2026

Weather: Cloudy

Temp	
High	Low
69	61

Report No.: 18
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Excavation for water line began along north side of Hickory Shadows Drive, service line was struck during excavation and repaired by Inframark	

Materials Testing - Test Taken & Results	Time Charges		
		Day Charged?	Yes
			210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used
			18
			No. Days Left
			192

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	1	
Foreman	2	
Operator	2	
Laborer	4	

Equipment				
Equipment	Model No.	No.	Hours	Stand-by
Excavator		2		
Loader		1		

Pay Items		
Pay Item Desc.	Location	Quantity



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements

--	--	--	--

HDR Site Representative	Supervisor	Contractor
TE	NLL	D

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Equipment outside of 12 Hickory Shadows Drive
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Excavation and location of service line repair
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Repaired service line location
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Excavation on north side of Hickory Shadows Drive



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/23/2026

Weather: Cloudy

Temp	
High	Low
67	60

Report No.: 19
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Excavation continuing for water line, service line was struck and repair was made, 8" water line installation	

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	19
			No. Days Left	191

Manpower		
Labor Force/Sub	No.	Hours
Operator	4	
Supervisor	2	
Foreman	2	
Laborer	5	

Equipment				
Equipment	Model No.	No.	Hours	Stand-by
Excavator		2		
Other Directional drilling machine				
Dump Truck		1		



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

Pay Items			
Pay Item Desc.	Location	Quantity	
25-Furnish and Install 8" PVC C-900, DR 18 Water Line & Fittings, including restrained joints, by Auger Construction, complete in place, the sum of:		200	Linear feet

HDR Site Representative	Supervisor	Contractor
		

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Excavation for water line and directional drilling equipment
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Pit to the right of 18 Hickory Shadows Drive
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Pit near 24 Hickory Shadows Drive
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Pit to the right of 17 Hickory Shadows Drive
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Pit to the right of 19 Hickory Shadows Drive (location of proposed C-2 inlet)
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Pit to the left of 12 Hickory Shadows Drive
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Pit in front of 12 Hickory Shadows Drive
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Pit to the left of 7 Hickory Shadows Drive
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



P5 Hickory Shadows Drive (the object pictured is not a pipe, it's a device for drilling a hole for the trenchless pipe)
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Pit located near north side exit of Hickory Shadows Drive
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Small pit located to the right of 6 Hickory Shadows Drive
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Pit to the left of 7 Hickory Shadows Drive
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Excavation outside of 5 Hickory Shadows Drive



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/24/2026

Weather: rain/cloudy

Temp	
High	Low
54	31

Report No.: 20
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
No work this day - Saturday	

Materials Testing - Test Taken & Results	Time Charges			
		Day Charged?	Yes	No. Contract Days
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	20
clear			No. Days Left	190

Manpower		
Labor Force/Sub	No.	Hours

Equipment				
Equipment	Model No.	No.	Hours	Stand-by

Pay Items		
Pay Item Desc.	Location	Quantity

HDR Site Representative	Supervisor	Contractor



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/25/2026

Weather: rain/cloudy	Temp		Report No.: 21
	High	Low	
	33	22	Contractor: Arnold & Co. LLC

Description Of Work:	Conversation
No work this day - Sunday	

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	21
clear			No. Days Left	189

Manpower		
Labor Force/Sub	No.	Hours

Equipment				
Equipment	Model No.	No.	Hours	Stand-by

Pay Items		
Pay Item Desc.	Location	Quantity

HDR Site Representative	Supervisor	Contractor
		



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/26/2026

Weather: sunny/clear

Temp	
High	Low
40	23

Report No.: 22
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Contractor performed prep work for boring from sta: 6+50 - 9+70 and making connection at sta: 6+00 (12 Hickory Shadows).	Spoke with project engineer Ngoc Le and was instructed that contractor should not be working due to city being closed as a result of extreme winter weather. Contractor was notified and worked half shift prior to de mobilizing for the day.

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	22
clear			No. Days Left	188

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	1	4
Foreman	1	4
Operator	1	4
Laborer	3	4

Equipment				
Equipment	Model No.	No.	Hours	Stand-by
Backhoe	CAT 302.7	1	4	
Backhoe	CAT 306	1	4	
Skid Steer	CAT 299D	1	4	



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements

Pay Items		
Pay Item Desc.	Location	Quantity

HDR Site Representative	Supervisor	Contractor
		

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



prep work for making connection at sta: 6+00 (12 Hickory Shadows).



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/27/2026

Weather: sunny/clear

Temp	
High	Low
52	31

Report No.: 23
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
No work this day - site shut down due to city closure as a result of extreme winter weather	

Materials Testing - Test Taken & Results	Time Charges		
	Day Charged?	Yes	No. Contract Days
			210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used
clear			23
			No. Days Left
			187

Manpower		
Labor Force/Sub	No.	Hours

Equipment				
Equipment	Model No.	No.	Hours	Stand-by

Pay Items		
Pay Item Desc.	Location	Quantity

HDR Site Representative	Supervisor	Contractor



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements

	NLL	
--	-----	--



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/28/2026

Weather: sunny/clear

Temp	
High	Low
61	34

Report No.: 24
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
<p>Contractor installed waterline and waterline bends from sta: 6+13 - 6+23 (12 Hickory Shadows). Also installed waterline and 21 LF of 16" steel casing at sta 6+15. Waterline bend encased in cement stabalized at sta 6+19 and sanitary sewer crossing. Bank sand placed over waterline in remaining locations. Temporary crushed concrete base placed for paving.</p>	

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	24
clear			No. Days Left	186

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	1	10
Foreman	1	10
Operator	1	10
Laborer	8	10

Equipment				
Equipment	Model No.	No.	Hours	Stand-by



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

Backhoe	CAT 302.7	1	10	
Backhoe	CAT 306	1	10	
Skid Steer	CAT 299D	1	10	

Pay Items			
Pay Item Desc.	Location	Quantity	
56-Cement Stabilized Sand, complete in place, the sum of:	waterline bend at sta: 6+18 and sewer line crossing at sta: 6+15	3	Cubic yards
38-16" Steel Casing for 8" Water Line, complete in place, the sum of:	waterline crossing at sta: 6+15	25	Linear feet
39-Trench Protection for Water Line, complete in place, the sum of:	waterline crossing at sta: 6+15	28	Linear feet
58-Extra Crushed Concrete Base Material, complete in place, the sum of:	paving patch for waterline crossing at sta: 6+15	7	Tons
25-Furnish and Install 8" PVC C-900, DR 18 Water Line & Fittings, including restrained joints, by Auger Construction, complete in place, the sum of:	waterline crossing at sta: 6+15	28	Linear feet

HDR Site Representative	Supervisor	Contractor
--------------------------------	-------------------	-------------------



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements

		
---	--	---

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Contractor installed waterline and waterline bends from sta: 6+13 - 6+23 (12 Hickory Shadows).

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Bank sand placed over waterline and waterline bends from sta: 6+13 - 6+23 (12 Hickory Shadows)
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Contractor installed waterline and 21 LF of 16" steel casing at sta 6+15.
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Bank sand placed over waterline and 21 LF of 16" steel casing at sta 6+15.



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/29/2026

Weather: sunny/clear

Temp	
High	Low
71	39

Report No.: 25
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Contractor installed waterline and 12 LF of 16" steel casing at sta 3+33. Also installed 25 LF of waterline from bend at sta: 3+33. Waterline encased in cement stabilized at sanitary sewer crossing. Bank sand placed over waterline in remaining locations. Temporary crushed concrete base placed for paving. Contractor placed concrete for 1027 Ridgeley.	Attended progress meeting at City Hall

Materials Testing - Test Taken & Results	Time Charges			
Geotest technician onsite to sample and test concrete for driveway	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	25
clear			No. Days Left	185

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	1	10
Foreman	1	10
Operator	1	10
Laborer	8	10

Equipment				
Equipment	Model No.	No.	Hours	Stand-by



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

Backhoe	CAT 302.7	1	10	
Backhoe	CAT 306	1	10	
Skid Steer	CAT 299D	1	10	


Pay Items			
Pay Item Desc.	Location	Quantity	
14-Full Depth Concrete Point Repair, complete in place, the sum of:	1027 driveway (25' x 15')	42	Square Yards
25-Furnish and Install 8" PVC C-900, DR 18 Water Line & Fittings, including restrained joints, by Auger Construction, complete in place, the sum of:	waterline crossing from bend at sta: 3+33.	25	Linear feet
38-16" Steel Casing for 8" Water Line, complete in place, the sum of:	Waterline crossing from bend at sta: 3+33.	15	Linear feet
56-Cement Stabilized Sand, complete in place, the sum of:	Waterline/sewer line crossing from bend at sta: 3+33.	2	Cubic yards
39-Trench Protection for Water Line, complete in place, the sum of:	Waterline crossing from bend at sta: 3+33.	25	Linear feet
58-Extra Crushed Concrete Base Material, complete in place, the sum of:	Waterline crossing from bend at sta: 3+33.	3	Tons

HDR Site Representative 	Supervisor 	Contractor 
---	--	--



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements

Photo(s) of day's work

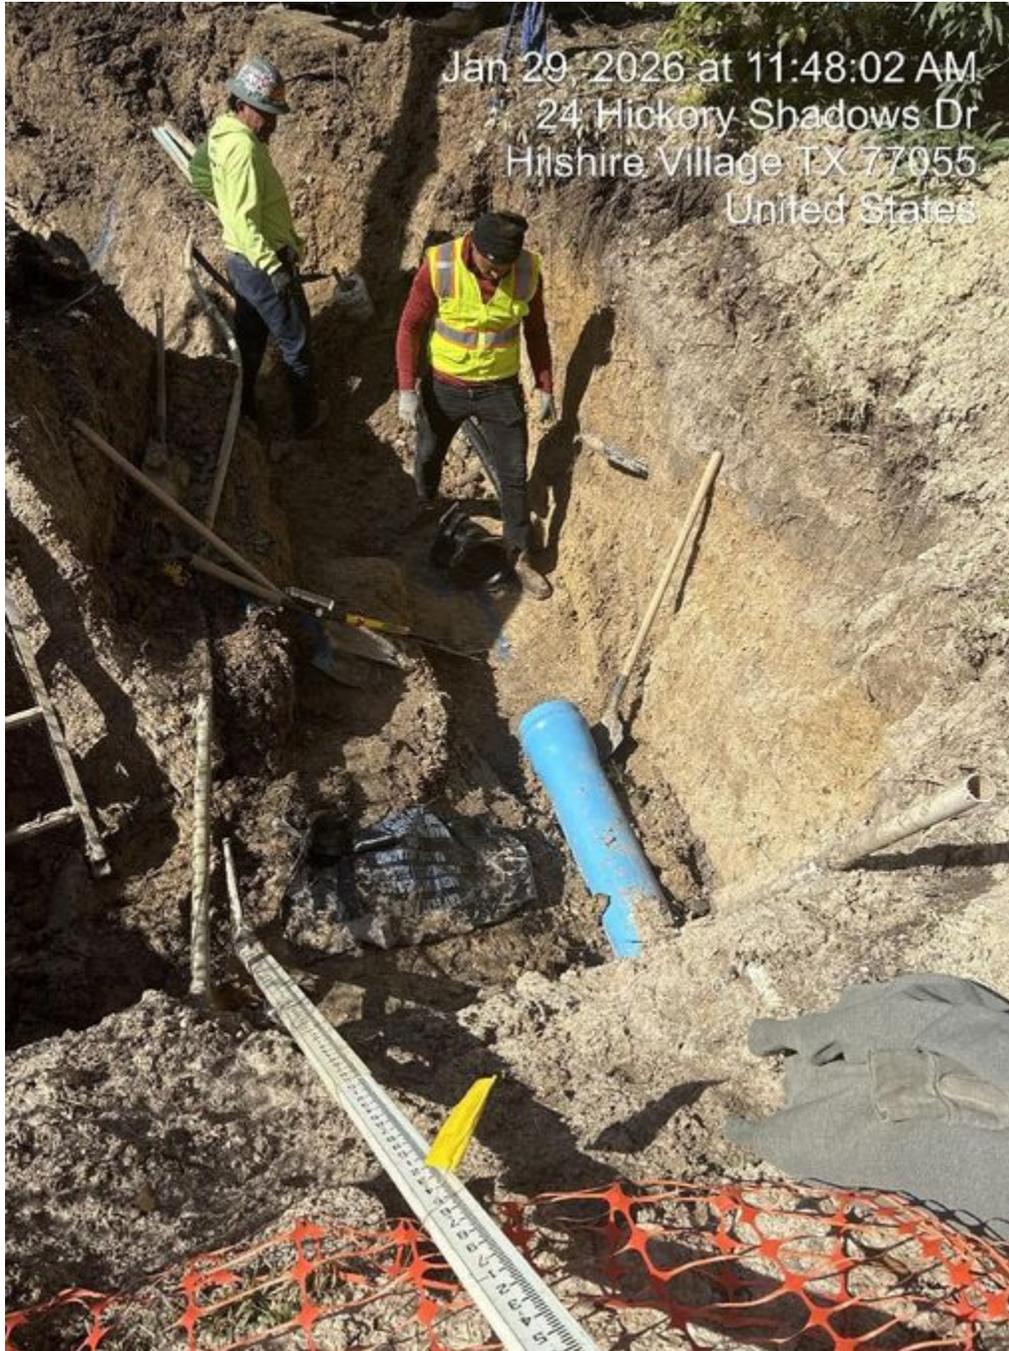

Contractor installing waterline and 12 LF of 16" steel casing at sta 3+33.

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Contractor installing waterline and 12 LF of 16" steel casing at sta 3+33.
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Contractor installing waterline and 12 LF of 16" steel casing at sta 3+33.
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



1027 Ridgeley driveway
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



1027 Ridgeley driveway



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/30/2026

Weather: sunny/clear

Temp	
High	Low
55	36

Report No.: 26
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
Contractor performed saw cutting of road in various locations for water line services. Also jack hammered and removed concrete at sta: 4+00 for installation of waterline. No waterline installed	Contacted Ngoc & Efrain to explain existing AC pipe at sta: 9+70 (Wirt Rd).

Materials Testing - Test Taken & Results	Time Charges			
	Day Charged?	Yes	No. Contract Days	210
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	26
clear			No. Days Left	184

Manpower		
Labor Force/Sub	No.	Hours
Supervisor	1	10
Foreman	1	10
Operator	1	10
Laborer	7	10

Equipment				
Equipment	Model No.	No.	Hours	Stand-by
Backhoe	CAT 302.7	1	10	
Backhoe	CAT 306	1	10	
Skid Steer	CAT 299D	1	10	



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**

Pay Items			
Pay Item Desc.	Location	Quantity	
64-Construction Material Testing Services, complete in place, the sum of:	Geotest Invoice	0.051473125	Lump sum
2-Traffic Control and Regulation, including flagmen, complete in place, the sum of:	Hickory Shadows Rd	0.22	Lump sum

HDR Site Representative	Supervisor	Contractor
		

Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Contractor saw cutting road
Photo(s) of day's work



Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements



Contractor jack hammering and removing concrete at sta: 4+00 for installation of waterline.



Construction Daily Report For

Hickory Shadows Drive Paving, Drainage & Utility Improvements

Job: Hickory Shadows Drive
Paving, Drainage & Utility
Improvements

Date: 01/31/2026

Weather: sunny/clear

Temp	
High	Low
47	29

Report No.: 27
Project No.: 10418041
Contractor: Arnold & Co.
LLC

Description Of Work:	Conversation
No work this day - Saturday	

Materials Testing - Test Taken & Results	Time Charges			
		Day Charged?	Yes	No. Contract Days
Project Site Conditions (Describe):	Reason if Day Not Charged		No. Days Used	27
clear			No. Days Left	183

Manpower		
Labor Force/Sub	No.	Hours

Equipment				
Equipment	Model No.	No.	Hours	Stand-by

Pay Items		
Pay Item Desc.	Location	Quantity

HDR Site Representative	Supervisor	Contractor



**Construction Daily Report For
Hickory Shadows Drive Paving, Drainage & Utility Improvements**
