

Homer Public Safety Building


Grubstake Avenue Homer, Alaska 99603



Date Fri 12/06/2019

Job # 1809-2

Prepared By Carl Brinkerhoff

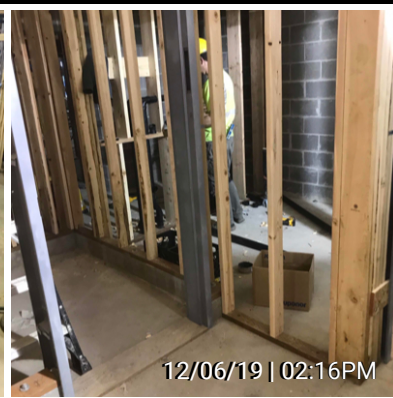

Weather

6:00 AM

27°

Overcast

Wind: 8 MPH | Precipitation: .0" | Humidity: 75%

12:00 PM

30°

Mostly Cloudy

Wind: 9 MPH | Precipitation: .01" | Humidity: 77%

4:00 PM

34°

Mostly Cloudy

Wind: 10 MPH | Precipitation: .01" | Humidity: 79%

Work Logs

Name	Description	Quantity	Hours	Hours To Date
Consolidated Roofing		0	0	477
Duct or Sheet Metal		0	0	12
East Road Services		0	0	944
Eayrs Plumbing	Onsite continuing domestic water rough in. <small>Carl Brinkerhoff 12/06/19 03:17PM</small>	2	8	520
Matt Hanson, Ron Frazier, Tanner Stengel, Chad Albertsons, Ryan Fox, Jim	Supervision, coordination and documentation. Crew continued setting upper level interior door frames. Continued blocking at walls for bath accessories and other devices. Continued framing at dented on area. Misc. framing for electrical panel in dispatch, fur out walls at rain leaders in dispatch and polygraph. Grinding fins and imperfections at lower level exposed concrete walls. <small>Carl Brinkerhoff 12/06/19 03:22PM</small>	7	8	5235.5
Puffin Electric	2 journeyman and an apprentice onsite continuing electrical rough in mainly upper level. Roughed in power to door frames as required. <small>Carl Brinkerhoff 12/06/19 03:24PM</small>	3	0	905.5
Total		12	72	10737

Time Cards

No entry

Materials

No entry

General Notes

No entry

Site Safety Observations

1. Site safety protocols were observed onsite today.

Carl Brinkerhoff | 12/06/19 | 03:26PM


Quality Control Observations

1. All materials and workmanship performed onsite today met or exceeded project specifications.

Carl Brinkerhoff | 12/06/19 | 03:26PM

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pat McNary was onsite to layout control room. Person from dispatch and officer Brown were onsite to coordinate control room layout. Gentleman from ProCom was onsite this afternoon. Carl Brinkerhoff 12/06/19 03:29PM
5. Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	No exterior door frames onsite yet. Carl Brinkerhoff 12/06/19 03:29PM
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	All terrain scissor lift. Carl Brinkerhoff 12/06/19 03:29PM



I, Carl Brinkerhoff, have reviewed and completed this report.

Carl Brinkerhoff | 12/06/19 | 03:29PM

SUBCONTRACTOR REPORTS



Fri 12/06/2019

Homer Public Safety Building: Grubstake Avenue Homer, Alaska 99603

Name	Description	Quantity	Hours	Hours To Date
1. Puffin Electric	No Entry	0	0.0	0.0
2. Eayrs Plumbing and Mechanical	No Entry	0	0.0	0.0
3. PEI	No Entry	0	0.0	32.0
Subtotal		0	0	32.0
Grand Total (Includes Cornerstone General Contractors Work Log Total)		12	72	10769.0
