



MEMO

Engineering Department

To: Board of Public Works
From: John Neumeier, Director of Public Works/City Engineer
Date: 3/17/2025
Re: **2d)** Interstate 41 - County Road J/Lawe Street Overpass Update

Background information:

Wisconsin Department of Transportation (WisDOT) will be reconstructing the County Road J Interchange in 2025 as part of the Interstate 41 project. Schedules can change and we will update you as necessary, but on the current schedule, important dates include:

- May 5 – Project to Begin
- May 12 – CTH J Bridge over I41 closes - demo
- June 20 – Full Closure of I-41 to set new bridge beams
- June 23 – Closure of On/Off Ramps to I-41/CTH J
- August 25 – CTH J Bridge and Ramps re-open
- September 9 – Final Completion

A full schedule is attached. More information, updates and schedules for the I-41 projects and the CTH J interchange specifically can be found at:

i41project.wisconsin.gov

Strategic Plan: NA

Budget: NA

Staff Recommended Action:


No action needed. Informational only.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	April 2025					May 2025					June 2025					July 2025					August 2025					September 2025					October 2025				
						23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05						
1130-66-78 CTH J Interchange						▼ Sep.09.25, 1130-66-78 CTH J Interch																																		
Admin						▼ Sep.09.25, Admin																																		
A1000	Planned Project Start (May 5th)		0	May.05.25*	0	◆ Planned Project Start (May 5th)																																		
A1020	Clearing & Grubbing/EC MOB #1 (Prior to March 31st)		5	Mar.24.25	30	■ Clearing & Grubbing/EC MOB #1 (Prior to March 31st)																																		
A1040	Stage 5-Must finish BY August 29th, 2025		0	Aug.25.25*	4	◆ Stage 5-Must finish BY August 29th, 2025																																		
A1050	Final Completion Date (October 15, 2025)		0	Sep.09.25*	25	◆ Final Completion Date (October 15, 2025)																																		
Stage 1A-Night Work						▼ May.07.25, Stage 1A-Night Work																																		
Roadway						▼ May.07.25, Roadway																																		
A1520	Erosion Control MOB #2		1	May.05.25	0	■ Erosion Control MOB #2																																		
A1530	Removals (Cable/Beam Guardrail)		1	May.05.25	0	■ Removals (Cable/Beam Guardrail)																																		
A1540	Asphalt milling (1,040 SY)		1	May.05.25	0	■ Asphalt milling (1,040 SY)																																		
A1560	Pave Median Shoulders (140 TN)		1	May.06.25	0	■ Pave Median Shoulders (140 TN)																																		
A1620	Crash Cushions/Barrier Wall (2,200 LF)		1	May.07.25	0	■ Crash Cushions/Barrier Wall (2,200 LF)																																		
Stage 1B-Night Work						▼ May.09.25, Stage 1B-Night Work																																		
Roadway						▼ May.09.25, Roadway																																		
A1630	Erosion Control MOB #3		1	May.08.25	0	■ Erosion Control MOB #3																																		
A1640	Removals (Guardrail)		1	May.08.25	0	■ Removals (Guardrail)																																		
A1645	Remove Concrete Barrier (156 LF)		1	May.08.25	0	■ Remove Concrete Barrier (156 LF)																																		
A1650	Asphalt milling (520 SY)		1	May.08.25	0	■ Asphalt milling (520 SY)																																		
A1670	Pave Outside Shoulders (60 TN)		1	May.08.25	0	■ Pave Outside Shoulders (60 TN)																																		
A1675	Temp Tape		1	May.08.25	1	■ Temp Tape																																		
A1680	Crash Cushions/Barrier Wall (2,200 LF)		1	May.09.25	0	■ Crash Cushions/Barrier Wall (2,200 LF)																																		
Stage 2-Night Work						▼ May.30.25, Stage 2-Night Work																																		
Structure Work						▼ May.30.25, Structure Work																																		
A1690	Close CTH J at RAB's for Bridge Demo/ECM #4		1	May.12.25	0	■ Close CTH J at RAB's for Bridge Demo/ECM #4																																		
A1700	Mob In/Site Prep		2	May.12.25	0	■ Mob In/Site Prep																																		
A1710	Demo Over 41 NB		2	May.13.25	0	■ Demo Over 41 NB																																		
A1720	North Abutment Removal/Pier 1 Removal		4	May.15.25	0	■ North Abutment Removal/Pier 1 Removal																																		
A1730	Demo Over 41 SB		2	May.21.25	0	■ Demo Over 41 SB																																		
A1740	South Abutment Removal/Pier 3 Removal		3	May.23.25	0	■ South Abutment Removal/Pier 3 Removal																																		
A1750	Pier 2 Removal/Temp Shoring		2	May.29.25	0	■ Pier 2 Removal/Temp Shoring																																		
Stage 3-Day Work						▼ Jun.19.25, Stage 3-Day Work																																		
Structure Work						▼ Jun.19.25, Structure Work																																		
North Abutment Construction						▼ Jun.10.25, North Abutment Construction																																		
A1840	Excavation/Storm Sewer		3	May.21.25	7	■ Excavation/Storm Sewer																																		
A1850	Piling/Form/Rebar/Pour/Strip		6	May.27.25	7	■ Piling/Form/Rebar/Pour/Strip																																		
A1860	Backfill Abutment/Slope Paving		5	Jun.04.25	7	■ Backfill Abutment/Slope Paving																																		
Pier Construction						▼ Jun.19.25, Pier Construction																																		
A1870	Piling		2	Jun.02.25	0	■ Piling																																		
A1880	Form/Rebar		7	Jun.04.25	0	■ Form/Rebar																																		
A1890	Pour/Strip		5	Jun.13.25	0	■ Pour/Strip																																		
South Abutment Construction						▼ Jun.17.25, South Abutment Construction																																		
A1900	Excavation/Storm Sewer		3	May.29.25	2	■ Excavation/Storm Sewer																																		
A1910	Piling/Form/Rebar/Pour/Strip		6	Jun.03.25	2	■ Piling/Form/Rebar/Pour/Strip																																		
A1920	Backfill Abutment/Slope Paving		5	Jun.11.25	2	■ Backfill Abutment/Slope Paving																																		
Stage 4A & 4B-Night Work Full Closure of Interstate						▼ Jun.20.25, Stage 4A & 4B-Night Work Full Closure of Interstate																																		
A1760	Set Beams		1	Jun.20.25	0	■ Set Beams																																		
Stage 5-(65 Calendar Day)						▼ Sep.09.25, Stage 5-(65 Calendar Day)																																		
Structure Work-Superstructure						▼ Aug.01.25, Structure Work-Superstructure																																		
A1340	Decking		8	Jun.23.25	16	■ Decking																																		
A1350	Rebar		4	Jul.01.25	16	■ Rebar																																		
A1360	Pour/Cure		10	Jul.08.25	16	■ Pour/Cure																																		
A1370	Parapets/Sidwalk		10	Jul.15.25	16	■ Parapets/Sidwalk																																		
A1380	Strip Deck		7	Jul.24.25	16	■ Strip Deck																																		
A1390	Install Railing		4	Jul.28.25	16	■ Install Railing																																		
Roadway Work						▼ Sep.09.25, Roadway Work																																		
North Side CTH J						▼ Aug.14.25, North Side CTH J																																		
A1395	Traffic Control-Close CTH J & Ramps		1	Jun.23.25	0	■ Traffic Control-Close CTH J & Ramps																																		
A1400	Erosion Control MOB #5		1	Jun.23.25	0	■ Erosion Control MOB #5																																		
A1410	Clearing and Grubbing		2	Jun.23.25	0	■ Clearing and Grubbing																																		
A1415	Storm Sewer		3	Jun.23.25	0	■ Storm Sewer																																		
A1420	Removals and Grading (5,229 CY)		5	Jun.24.25	0	■ Removals and Grading (5,229 CY)																																		
A1430	Install Select Crush (5,572 TN)		5	Jun.27.25	6	■ Install Select Crush (5,572 TN)																																		
A1435	Base Aggregate 1 1/4" (4,290 TN)		5	Jun.27.25	6	■ Base Aggregate 1 1/4" (4,290 TN)																																		
A1436	EC MOB #6		2	Jul.07.25	69	■ EC MOB #6																																		
A1440	Electrical Crossings		1	Jul.07.25	6	■ Electrical Crossings																																		
A1450	Staking for paving		1	Jul.08.25	6	■ Staking for paving																																		
A1460	Trim & Prep for paving		1	Jul.09.25	6	■ Trim & Prep for paving																																		
A1470	Pave 15' ramps		1	Jul.10.25	6	■ Pave 15' ramps																																		
A1480	Stake Curb & Gutter		1	Jul.11.25	6	■ Stake Curb & Gutter																																		
A1490	Slip Curb & Gutter		3	Jul.14.25	6	■ Slip Curb & Gutter																																		

■ Remaining Level of Effort
 ■ Remaining Work
 ■ Actual Work
 ■ Critical Remaining Work
 ◆ Milestone
 ▼ Summary

1130-66-78 CTH J Interchange

Feb.16.30 09:54

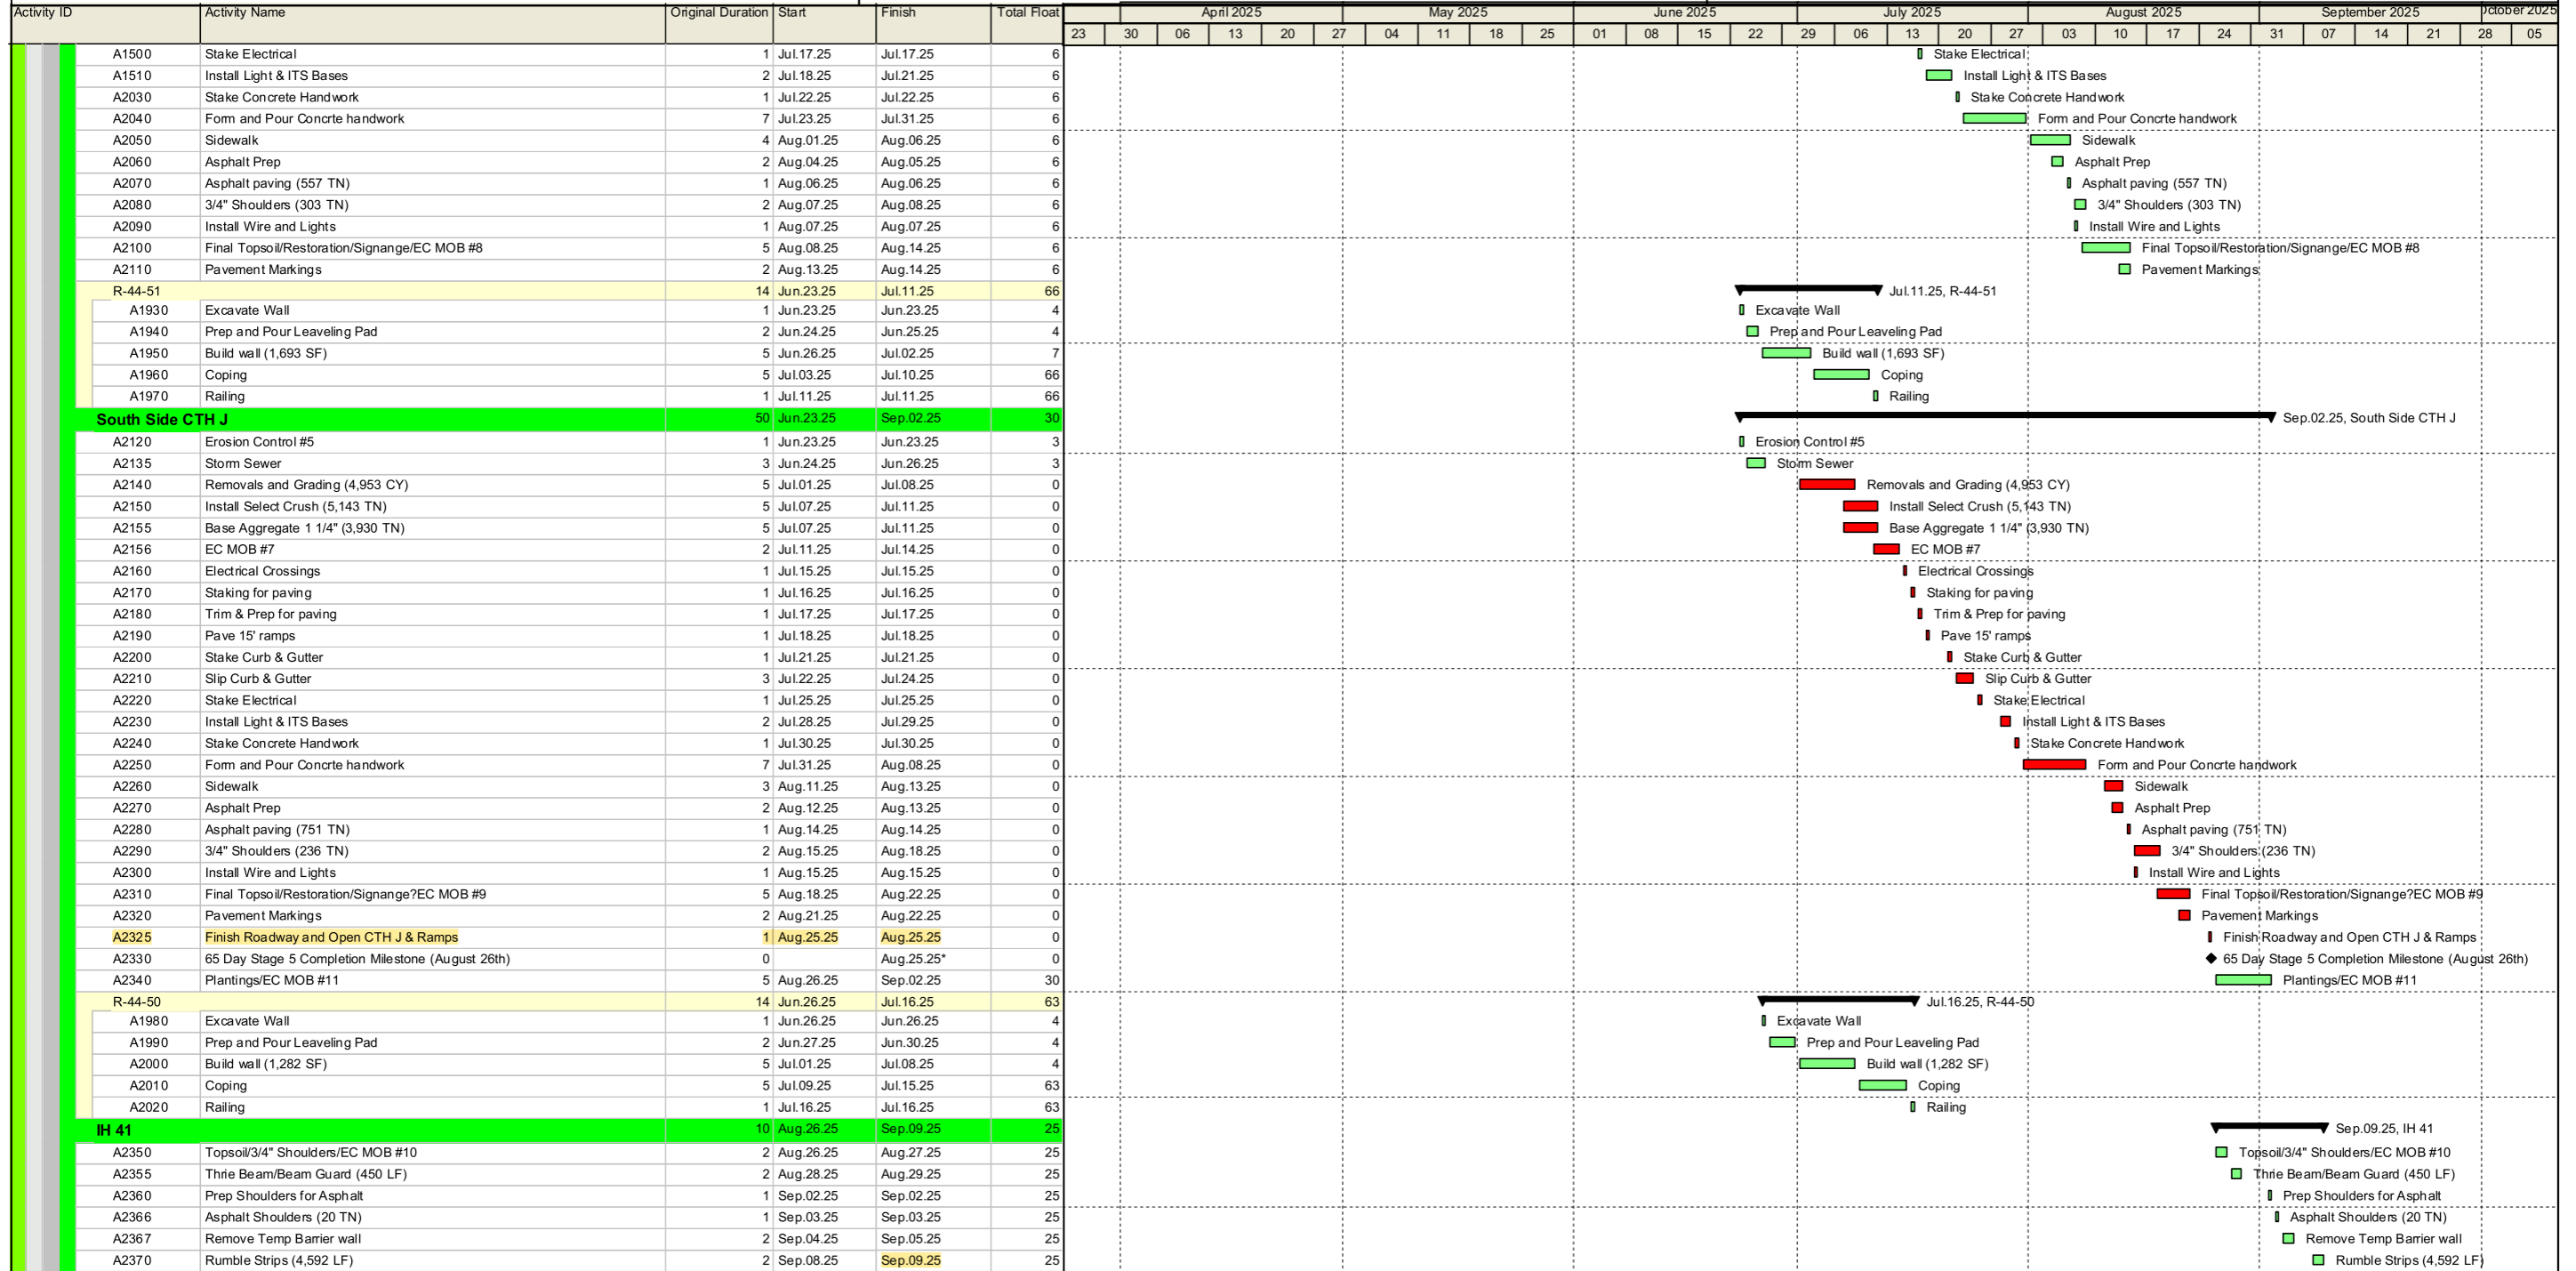

Remaining Level of Effort
 Remaining Work
 Milestone
 Actual Work
 Critical Remaining Work
 Summary

PROJECT BRIEF


I-41 Project | Outagamie and Brown Counties

County J

Schedule: early 2025 to fall 2025

TRAFFIC IMPACTS

- 1 County J bridge over I-41 CLOSED spring to summer 2025**
 - Traffic will be detoured using WIS 55 and WIS 96.
 - **SB I-41 to County J/Lawe St. detour:** SB I-41 to WIS 55/Delanglade St. Follow WIS 55 north to County JJ/Edgewood Dr. Turn east on Edgewood Dr. and continue to County J/Lawe St.
 - **NB I-41 County J/Lawe St. detour:** NB I-41 to WIS 55/Delanglade St. Follow WIS 55 south and continue to County J/ Lawe St.
- 2 County J ramps CLOSED summer 2025**

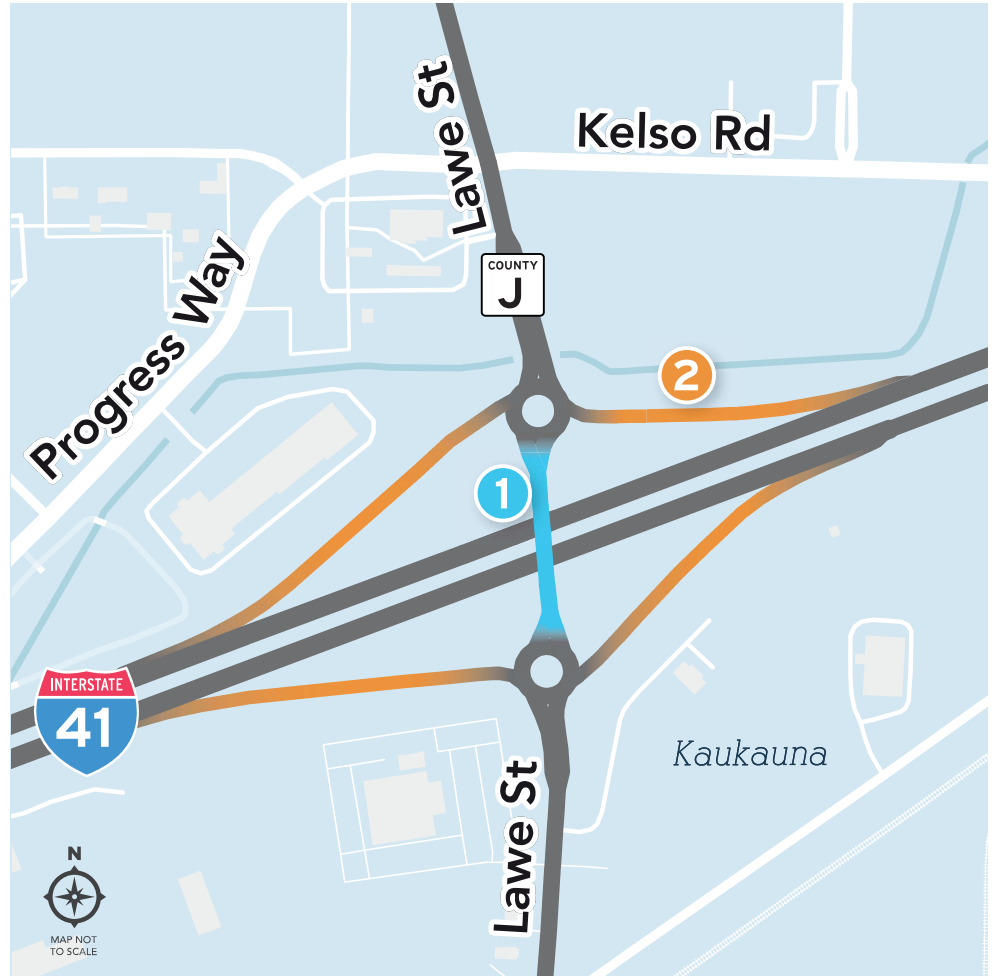

County J Interchange

The Wisconsin Department of Transportation (WisDOT) is reconstructing County J over I-41 along with the entrance and exit ramps, replacing pavement, constructing bicycle and pedestrian accommodations, and improving roundabouts to accommodate oversized/overweight vehicles as a part of the area improvements. The existing interchange configuration at County J remains the same as a diamond interchange with roundabouts.

Last updated January 15, 2025



For project information, contact I-41 Project Field office: (920) 492-7733 or;
Melissa (Missy) Kok, I-41 Communications Manager | Melissa2.Kok@dot.wi.gov



Find us online at:
i41project.wisconsindot.gov



Find us on Facebook:
[i41ProjectWI](https://www.facebook.com/i41ProjectWI)



Follow us on X:
[@i41ProjectWI](https://twitter.com/i41ProjectWI)

