This report was prepared by:
NAME Willy Brown
NAME Willy Brown PHONE # (208) 849-1707
DATE RECEIVED AT CITY HALL 1/11/2024 DATE PRESENTED TO CITY COUNCIL
The state of the s
COMMENTS FROM CITY COUNCIL:
INITIALED BY:
Mayor City Council Member

BROWN'S MOUNTAIN RECYCLING MONTHLY PROGRESS REPORT

For the month of Tuly

This report must be submitted to New Meadows City Hall on the Wednesd	ay prior
to the 4 th Monday of the month following the report month. A representa	tive of
Brown's Recycling must attend the City Council meeting on the 4th Monday	of the
month to answer questions regarding this report.	

If no action has been taken in the month on a condition, please note why no action has been taken. Failure to submit a completed report in a timely manner will result in revocation of the CUP to be considered at the next City Council meeting.

CONDITION # 1 - 7 foot sight obscuring fence with two runs of barbed wire constructed out of metal posts set 3 feet deep in concrete surrounding all four sides of the property.

DUE DATE: October 31, 2024

What work has been done on this part of the project this month? Please provide pictures of progress.

^ · · · · · · · · · · · · · · · · · · ·	
Kented Skidsteer, anger, drill bit, and tra	10
From Tates Rents. Got D7 Bulldozer	running.
Removing existing East and South fer	Ses
for post hole drilling on Friday the	(ew)
Sunday's Tates Rents rental of equip	
Purchased a pallet of ready mix concr	ete
Percentage Complete 3	2%

	es and 6 foot ornamental grass with large boulders and ground	ķ
er	r to the edge of the ditch to create appealing landscaping.	
	DUE DATE: August 31, 2024	1
	What work has been done on this part of the project this mon	ntn
	Please provide pictures of progress.	, ,
	No new progress. Looking for boulders for	<u>UY</u>
	Tanascape	
	Percentage Complete	10
N	DITION #3 – All tires removed from the property.	
	DUE DATE: August 31, 2024	
ı	What work has been done on this part of the project this mor	nth
	Please provide pictures of progress.	
	No new progress on tires. Coing to	<u>b</u>
	a large dump bed trailer for transpor	<u> (</u>

CONDITION # 4 – The area within at least 300 feet from the east property line and 300 feet from the creek that runs along the southern property line vacated and free from any potential contamination of fluids.

This 15	already in	complian	<u> </u>
			12
Percentage Comp	lete	er de Braer gae	10
ITION # 5 – Solid	Waste compliance	ce approved ar	nd documen
nd a DEQ approv	ed Containment		
nd a DEQ approv	ed Containment per 31, 2024	plan implemer	nted.
ind a DEQ approv DUE DATE: Octob What work has be	ed Containment per 31, 2024 een done on this	plan implement part of the pro	nted.
OITION # 5 – Solid and a DEQ approvement of DUE DATE: October What work has been provide pi	ed Containment per 31, 2024 een done on this ctures of progres	plan implement part of the pross.	nted. oject this mo
ind a DEQ approv DUE DATE: Octok What work has be Please provide pi	ed Containment per 31, 2024 een done on this ctures of progres	plan implement part of the pross.	nted. oject this mo
ind a DEQ approving a DEQ approving the DATE: October What work has been provided pires of the processions.	ed Containment per 31, 2024 een done on this ctures of progres s of Sending	plan implement part of the property $D = Q$	nted. oject this mo
ind a DEQ approv DUE DATE: Octok What work has be Please provide pi	ed Containment per 31, 2024 een done on this ctures of progres s of Sending	plan implement part of the property $D = Q$	nted. oject this mo
nd a DEQ approv DUE DATE: Octob What work has be Please provide pi <u>In proces</u> Cevisions	ed Containment per 31, 2024 een done on this ctures of progres s of Sending	plan implement part of the property $D = Q$	nted. oject this mo

CONDITION # 6 – A Design review for the office building on the property approved by the City Council.

DUE DATE: June 30, 2024

What work has been done on this part of the project this month?

Please provide pictures of progress.

This condition is finalized. Brain Grae Harper, the city's new engineer came by look at the flood plain drainage Situation. 3f+ burm along the gate would be plenty adequate drainage. Will construct apon completion of Percentage Complete

CONDITION # 7 – Office building set up on the property and hooked up to City water and sewer services.

DUE DATE: September 30, 2024

What work has been done on this part of the project this month? Please provide pictures of progress.

Sona Tubes for foundation pilings ready mix concrete rilling Six foundation holes

Percentage Complete



Customer Consent to proceed with Engineering/Design


Thank you for your req	quest. We are ex	cited to ser	rve as your elect	ic service prov	vider.		
I, BROWNS MO	UNTAIN RECYC	CLING	_ ("Applicant") re	equested for lo	laho Power Compa	any ("Idaho Power")	
to proceed with engine	eering for the wo	rk request l	located at:		ITH END RD DOWS , ID 83654		
Idaho Power's line exte	ension tariff prov	vides:					
Engineering Charge. / Installations and/or Alto billed to the Applicant of instances where consti	erations greater or Additional App	than 16 est olicant as pa	timated hours. E	stimates equal	to or less than 16	hours will be	
I understand I am resp in Oregon. I agree to p understand the engine	ay the engineer	ing charge,	whether the wor	k requested is	built or not. I		
Additional fees may inc the design and design							
The engineering hourly Commission's approve		e annually a	and is assessed l	peginning on ti	he Idaho or Oregor	n Public Utility	
Customer Signature: _	Don	ne	Brow	\sim	Date:	7-10-24	
Mailing Address:		РО ВОХ	325 NEW MEA	DOWS ID 83	3654		
Email Address:	dreyer	brow	N220	holmai	1. COMPhone:	208-849-1702	•
Idaho Power Represer	ntative:	SHI	ERI STALEY		Date:	7/11/2024	
Email Address:		SStaley@i	idahopower.com		Phone:	(208) 630-7904	<u>4</u>
		er og det er					
		Service Re	Internal Use quest Number: (00522943		5.000	




Condition # 1 Acquired metal for fense



Condition #1 More metal for fense

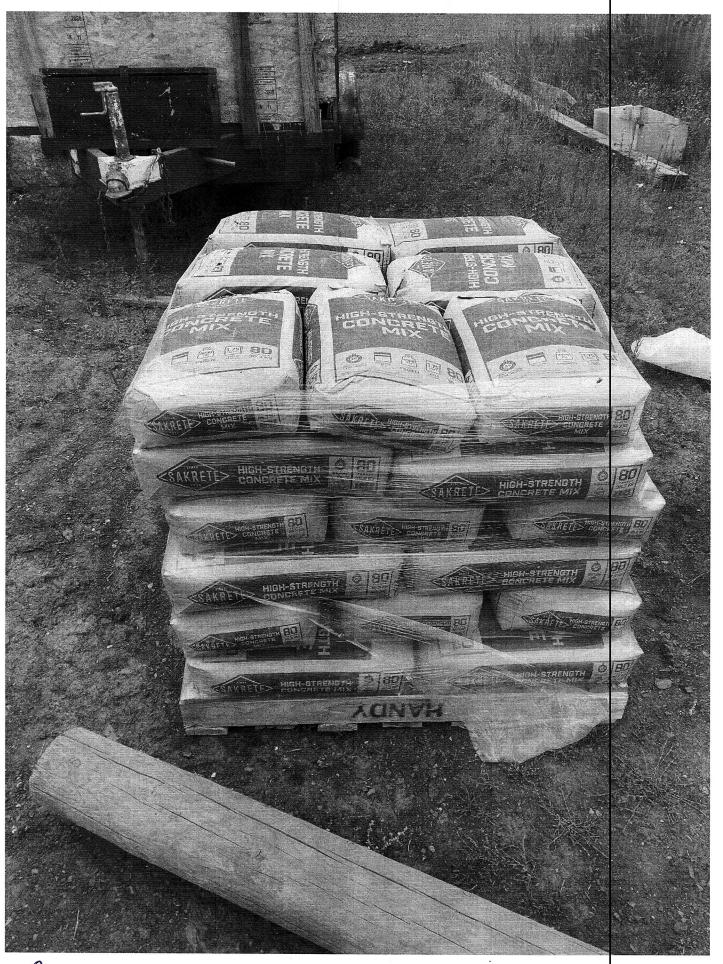

Conditions #1+#6 Pallet of reddy mix concrete

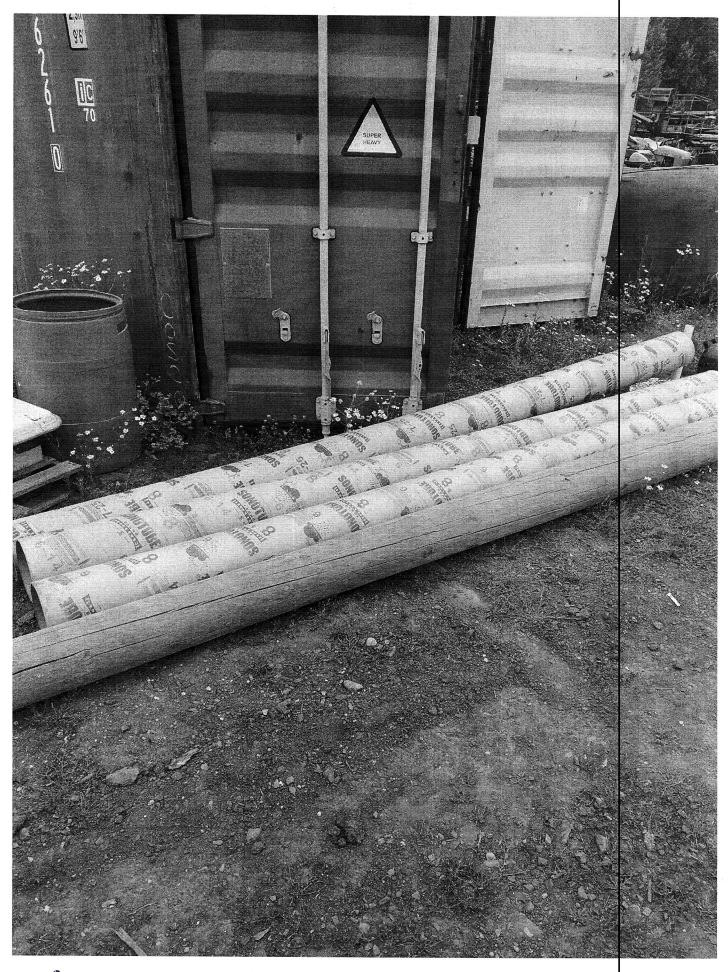

Condition # 6 Sona Tubes for office pilings
