
modular project PROPOSAL March 19, 2025

Maron 10, 2020

BOXX Project: Q-84219





Town of Prosper New Purchase- 48x56 and 60x56 offices



TIPS CONTRACT: **230902** Exp. Date:11/30/2025 Permanent Modular Buildings

Prosper, Texas

BOXX Modular, Inc. (Corporate Office) 3475 High River Road | Fort Worth, TX | 76155



modular project Sale Price Detail

This proposal is valid for 10 calendar days

TIPS CONTRACT: 230902

BASE PRICE

Scope of Work Description
New 48x56 Modular Office
New 60x56 Modular Office
Standard Delivery
Standard Set Up (Block/Level/Anchor)
Skirting to Match Siding

Amount (usd)

*Base Price Total:

\$689,049

OPTIONS

Initials = Selected Option Description

<u>Amount</u> (usd) **\$23,175**

Pressure Treated Access Ramp/Steps– 618 Square Feet at \$37.5 per SF Main Doors (2)

- 8x5 landing / 5x5 steps / 4x36 ramp/ 5x10 Switchback 2nd doors (2)
 - 5x5 landing / 5x5 steps

PROJECT DESCRIPTION DETAIL

The quote is for new 48x56 and 60x56 modular buildings. Standard installation includes block/level/anchor/skirt with set height not to exceed 36". Buildings to be set with CMU blocks on ABS pads on customer provided pad or foundation.

Installation rates are based on standard wages. If Prevailing wages or Davis Bacon wages are required, please provide wage sheet to re-quote installation.


No site-specific safety training or certifications included in cost.



Pricing excludes all applicable taxes. Buyer is responsible for all applicable taxes. Proposal Price does not include sales, use, or personal property taxes, except as may be additionally described. Unless otherwise specified, Proposal is valid for 10 calendar days from the "Proposal Date". BOXX Modular's willingness to enter into a contract at the price and/or terms of payment proposed is contingent upon satisfactory credit review and approval. Pricing is based on acceptance of BOXX's standard contract terms and conditions, along with timely receipt of any contractually required down payment.




60x56 Modular Complex

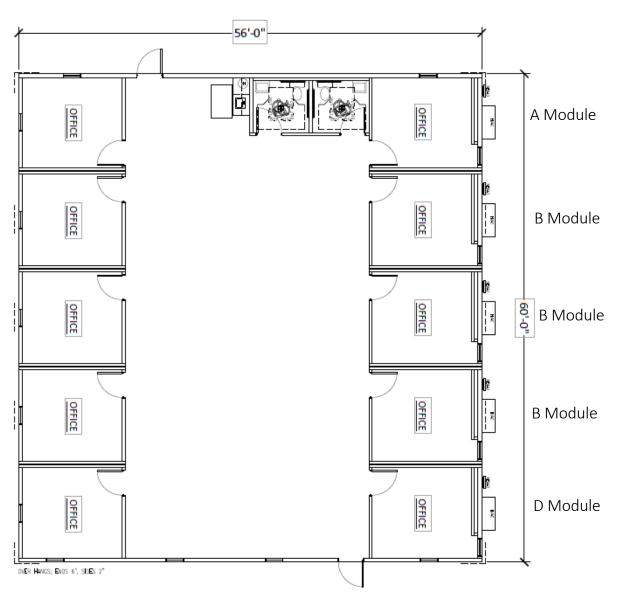

*SEE EXHIBITS FOR MODULE SPECIFICATIONS



48x56 Modular Complex

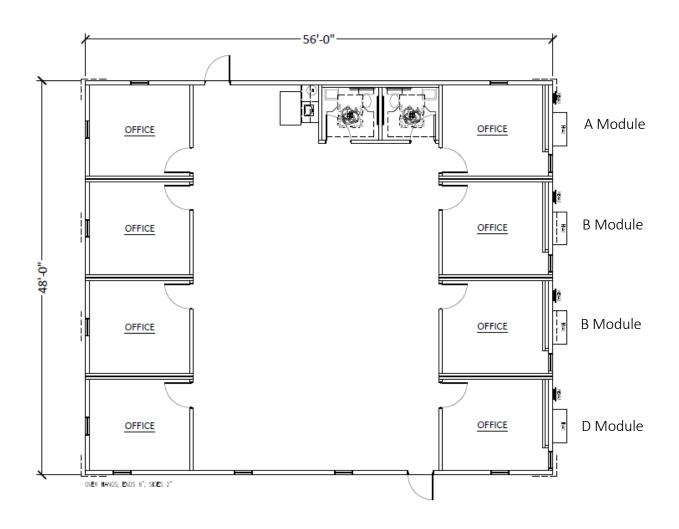


*SEE EXHIBITS FOR MODULE SPECIFICATIONS




modular project Delineation of Responsibilities

Division	Sub	Description	вохх	Owner	NA		
DIVISION 1 : GENERAL CONDITIONS							
	1011	Performance Bonds			X		
	1040	Building Permits/License		X			
	1500	Temporary Heat/Lighting			X		
		Portable Toilets		X			
		Temporary Water & Power			X		
	1502	Site Cleanup BOXX/Dumpster BY OWNER	X	X			
	1700	Closeout/Acceptance	X				
	1900	Miscellaneous					
		Taxes		X			
		Prevailing Wage Scale (Davis-Bacon)			X		
		Safety and Security Access Requirements For Workers		X			
		Project Terms of Payment	X				
		Invoicing Procedure	X				
DIVISION 2: SIT	E WORK						
	2000	Site Work		X			
		Accessibility		Х			
		Stake Site/Building Location		X			
	2160	Excavation & Grading		X			
		Spoilage Disposal		X			
		Erosion Control		X			
	2660	Final Connection of Domestic Water To Building		X			
		Final Connection of Sewer To Building					
	2740	(including manifolds in crawlspace)		X			
	2900	Landscaping / Fine Grading		X			
		Seeding		X			
		Restoration		X			
DIVISION 3 : Con			Г	 			
	3300	Foundations		X			
DIVISION 5 : Meta	als (SITE (ONLY)	Г	 			
	5000	Decks/Landings/Ramps (Engineered Aluminum)			X		
DIVISION 6 : WO	OD & PLA	STIC (SITE ONLY)	Г	 			
	6670	Decks/Landings (Pressure Treated Wood) IF SELECTED	X				
DIVISION 9 : FINI	SHES (SI	re only)	Т	,			
	9650	VCT Flooring with carpet bar	X				
	9680	Carpeting with / without carpet bar			X		



modular project **Delineation of Responsibilities**

Division	Sub	Description	вохх	Owner	NA		
DIVISION 10 : SP	DIVISION 10 : SPECIALTIES (SITE ONLY)						
	10100	Marker/Chalk/Tack Boards			Х		
	10425	Signage/Braille		Х			
	10520	Fire Extinguishers		Х			
	10532	Awnings			Х		
	10800	Toilet Accessories		X			
DIVISION 13 : BUILDING (MODULAR BUILDING)							
	13121	Delivery Of Modular Units To Site Including Transp. Permits	X				
	13122	Piers	X				
		Dry-Stack Block/Steel Piers On ABS Pads	X				
		Surface Bond Dry Stack			X		
	13123	Set-up					
		Structurally Connect Modular Floors & Roofs	X				
		Remove Hitches (Store Under Bldg. If stored in different					
		location, may be an additional cost)	Х				
	13125	Trim Out Exterior & Interior Walls/ Ceiling/Floors/Adjust Doors	x				
	13126	Anchor Modular Units Per Design Criteria	X				
	13127	Metal Skirting (Frame, Venting Included)	Х				
	13128	Roof Seaming	Х				
	13151	Site Construct Connector Corridors			Х		
DIVISION 16 : EL	ECTRICAL	L (SITE ONLY)					
	16410	Connect Electrical Service From Site to Modular Subpanels		Х			
		Main Disconnect For Modular Building Connection		Х			
	_	Supply and Install MDP		Х			
	16610	Fire / Smoke Alarm Systems		Х			
	16620	Security Intrusion System		Х			
	16740	Clocks/Bells			Х		
	16750	Communication Systems in Modular		X			
		Tap & Extend Existing Comm Service To Site		X			
		Final Connection of Comm System in Modular		Х			
	16770	Data Systems in Modular		X			
		Tap & Extend Existing Data Service To Site		Х			
		Final Connection of Data System in Modular		X			





This proposal is valid for 10 calendar days

TIMELINE

<u>Estimated Completion</u> <u>Milestone Description</u>

Day 1 Executed contract and down payment received


2-3 weeks Transport lead time

2 weeks1 weekBuilding set up and trim outBuild decks/ramps- Final punch

SCHEDULE NOTES

Additional Information

Schedule subject to building availability and transport/set up schedule at time of execution. Will expedite if possible.




modular project Terms & Exclusions

Terms

- 1. Unless otherwise specified, Proposal is valid for 10 calendar days from the "Proposal Date". Building costs and production schedules change daily. At expiration of validity period Price and Delivery are subject to change without notice until Proposer accepts Order.
- 2. BOXX's willingness to enter into a contract at the price and/or terms of payment proposed is contingent upon satisfactory credit review and approval
- 3. Proposal pricing and project schedule is based on acceptance of BOXX's standard contract terms and conditions, along with timely receipt of any contractually required down payment.
- 4. Any Project Schedule provided with the Proposal is an estimate. Project Schedule will be confirmed at or around the time of Award, and may be subject to change orders throughout the Project.
- 5. Unless otherwise agreed in writing, BOXX will not accept any Liquidated or other damages for delays.
- 6. Prior to start of its Work, BOXX shall provide a proper Certificate of Liability Insurance and Worker's Compensation. Unless otherwise agreed in writing, "All Risk" and other special insurance is not provided by BOXX. As of the time of Substantial Completion, or as otherwise agreed, Buyer shall be responsible to insure the building(s), providing insurance coverage in the types and limits as may be required by the contract to adequately protect the interests of all applicable parties.
- 7. Buyer is responsible for all applicable taxes. Proposal Price does not include sales, use, or personal property taxes, except as may be additionally described. Customer is responsible for paying a personal property fee of eight percent (8%) of the monthly rent (or lease) payment to BOXX.
- 8. Unless otherwise agreed to in advance as a condition of the Contract, price assumes the use of non-union labor at non-prevailing wages. Any requirement for the payment of prevailing wages or the use of union labor will result in additional charges.
- BOXX will take reasonable protective precautions to avoid damage to property and equipment. BOXX will not accept responsibility for damage caused to
 paved or unpaved surfaces due to weight of heavy equipment.
- 10. TITLE BOXX Modular, Inc. will retain title to the work until such time that they have been paid in full for the delivery, installation and either direct sale or receipt of all amounts due to complete the finance lease of the building(s). BOXX does not waive its rights to retain title and/or to place a lien or claim against the Owner/Buyer/Lessee if it becomes reasonably necessary in order to protect BOXX's interests.
- 11. INDEMNIFICATION BOXX Modular, Inc. will indemnify Owner/Buyer/Lessee to the extent that they are legally responsible and permitted by BOXX's insurance carrier.
- 12. START AND COMPLETION DATES The contract Start Date shall be upon receipt of award and an executed contract. Barring any unforeseen delays, The Completion Date will be in accordance with bid specifications and the attached Schedule (to be confirmed upon receipt of award). BOXX is not responsible for any delays or damages beyond its control including material shortages, strikes or union activity, fire, acts of God, freight embargoes, acts of war or terrorism, delays by regulatory or permit authorities, delays by the Owner or Architect or any employed by them, or any cause of delay beyond the control of BOXX. In no event shall BOXX be responsible for consequential or actual damages.
- 13. Labor will be non-union at non-prevailing wages unless required by contract

Exclusions


V E I I I	
X = Excluded	
X	1. Impact fees
X	2. All applicable taxes (sales, property & use)
X	3. Bonding
X	4. Special insurance
X	5. Cranes and additional spotting apparatus
X	6. Fire suppression system
X	7. Site security (unless otherwise stated)
X	8. Landscaping, irrigation, paving, walkways, curbing, and site restoration
X	9. Tap fees and lift station (if required)
X	10. Exterior fire rating
X	11. Architect and engineering fees
X	12. Rock removal
X	13. Off-site spoilage removal
X	14. Site utilities and connections to modular building – includes electric, gas, water, and sewer or septic
X	15. Communications services and connection – including but not limited to telephone, data, intercom, intrusion alarm, smoke & fire alarm
X	16. Lightning protection
X	17. Temporary access roads and walkways
X	18. Removal, repair, and/or replacement of obstructing fences, walls or gates
X	19. Temporary electric and water (contractor will supply power source for own tools and equipment)
X	20. Portable toilets
X	21. Laboratory and field testing of materials
X	22. Dedicated full-time site supervisory personnel (foreman will supervise work unless other provisions are required per the contract)
X	23. Costs associated with easement(s)



modular project Site Requirements

Site Requirements

Site Requiremen	
X = Applicable	
X	1. No provisions allowed for obstructions below grade. If encountered, they would be a change order to the contract at an additional charge
X	2. The site must be level, dewatered, and accessible by truck with adequate turning radius and clearance from road to the site for delivery
X	3. Assumes site with 2,500 psf soil bearing capacity, bearing tests to be provided by Customer
X	4. All site plans and surveys to be provided by Customer
X	5. All underground utilities are to be clearly marked and flagged
X	6. Customer is responsible for obtaining and the cost of all permits, licenses, and Certificate of Occupancy
X	7. Due to volatility in fuel prices delivery charges are subject to a fuel surcharge.
X	8. Staging area adjacent to installation site, including any site improvements required to make it usable, by Customer
X	9. Where applicable, wheels and axles will remain on module(s), but may be removed and stored under for an additional fee
X	10. Site preparation by Customer
	11. Building removal, return delivery, and site restoration will be billed at prevailing rates at time of return
X	12. Main electrical service to building panels by Customer
X	13. Customer is solely responsible to inform BOXX Modular if site location is in a flood or fire zone
X	14. Customer is responsible for building maintenance



modular project Important Clarifications

Important Clarifications

Typical standard building sealed plans will include a cover page with notes/codes/calculations, floor plan with dimensions/electrical/plumbing/ mechanical on same page, typical elevation (NOT job specific), and a standard typical cross section (NOT job specific and may have actual roof designed truss attached). Any additional detail needed on sealed prints, other than what is typically provided will result in additional charges.

Does not include site specific foundation drawings that may be needed for permitting.

Standard installation assumes clear access and level site.

Typical blocking & tie down plans are non-site-specific using ABS pads and single dry stacked CMU blocks.

Customer is responsible for removing any vegetation under footprint of building install.

Customer is responsible for meeting any local codes for underpinning ventilation.

Standard set height is no more than three (8"x8"x16") blocks high or 40" finished floor height. Greater than 40" due to site conditions will require double stacking not to exceed 60" finished floor height. High set will require a change order for additional cost.

Deck/step/ramp is using treated lumber and provided as an estimate. Actual cost to be determined by final design @ \$37.50 per SF.

Pricing is subject to change based on Site Inspection by BOXX for access and staging

Standard payment terms are Net 30. Sales invoicing will be 25% down, 65% prior to delivery and 10% at substantial completion pending credit approval.

Safety Training, Background Checks, Badging Requirements, and any additional unlisted requirements not included.

If units to be power washed/painted after arriving on site, it will be at an additional cost

Warranty starts at the time of building completion at factory. Warranty Note - Bard HVAC warranty will not cover the unit if it is ran on a generator.

Schedule based on the current availability of units ready to deliver. If not available at time of execution we can fabricate new buildings with a longer lead time.

