



DONALD PRESTON DRIVE
JUNE SCHEDULE UPDATE DD = 7-1-26


Jul-01-26 04:56 PM

Activity ID	Activity Name	At Completion Duration	Start	Finish	May 31							Jun 07							Jun 14							Jun 21						
					on	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	
DONALD PRESTON DR		60.00	Jun-01-26 08:00 AM A	Aug-21-26 04:00 PM																												
ADMINISTRATION		60.00	Jun-01-26 08:00 AM A	Aug-21-26 04:00 PM																												
A1010	SUBMITTALS	10.00	Jun-01-26 08:00 AM A	Jun-12-26 04:00 PMA	SUBMITTALS																											
A1020	RAILROAD ROE AGREEMENT	15.00	Jun-01-26 08:00 AM A	Jun-19-26 04:00 PMA	RAILROAD ROE AGREEMENT																											
A1000	PROJECT START	0.00	Jun-01-26 08:00 AM A		PROJECT START																											
A1030	PROJECT TIME	82.00	Jun-01-26 08:00 AM A	Aug-21-26 04:00 PM																												
CONSTRUCTION		60.00	Jun-01-26 08:00 AM A	Aug-21-26 04:00 PM																												
PHASE I		31.00	Jun-01-26 08:00 AM A	Jul-13-26 04:00 PM																												
L1000	INSTALL PROJECT SIGNAGE AND TCP - PHASE I	1.00	Jun-01-26 08:00 AM A	Jun-01-26 04:00 PMA	INSTALL PROJECT SIGNAGE AND TCP - PHASE I																											
L1010	REMOVE EXISTING ASPHALT AND BASE - PHASE I	4.00	Jun-02-26 08:00 AM A	Jun-05-26 04:00 PMA	REMOVE EXISTING ASPHALT AND BASE - PHASE I																											
L1020	REMOVE CURB & GUTTER - PHASE I	1.00	Jun-08-26 08:00 AM A	Jun-08-26 04:00 PMA	REMOVE CURB & GUTTER - PHASE I																											
L1030	PROCESS SUBGRADE - NON-RAILROAD - PHASE I	0.00	Jun-09-26 08:00 AM A	Jun-09-26 08:00 AM A	PROCESS SUBGRADE - NON-RAILROAD - PHASE I																											
L1110	TIE REBAR - P1-6, P1-7, P1-14	1.00	Jun-10-26 08:00 AM A	Jun-10-26 04:00 PMA	TIE REBAR - P1-6, P1-7, P1-14																											
L1120	POUR - P1-6, P1-7, P1-14	2.00	Jun-11-26 08:00 AM A	Jun-12-26 04:00 PMA	POUR - P1-6, P1-7, P1-14																											
L1130	CURE - P1-6, P1-7, P1-14	5.00	Jun-13-26 08:00 AM A	Jun-17-26 04:00 PMA	CURE - P1-6, P1-7, P1-14																											
L1100	PROCESS SUBGRADE - RAILROAD AREA - PHASE I	0.00	Jun-17-26 08:00 AM A	Jun-17-26 08:00 AM A	PROCESS SUBGRADE - RAILROAD AREA - PHASE I																											
L1040	TIE REBAR - P1-1, P1-2, P1-3, P1-4	2.00	Jun-23-26 08:00 AM A	Jun-24-26 04:00 PMA	TIE REBAR - P1-1, P1-2, P1-3, P1-4																											
L1050	POUR - P1-1, P1-2, P1-3, P1-4	1.00	Jun-29-26 08:00 AM A	Jun-29-26 04:00 PMA																												
L1340	TIE REBAR - P1-12	1.00	Jun-30-26 08:00 AM A	Jun-30-26 04:00 PMA																												
L1060	CURE - P1-1, P1-2, P1-3, P1-4	5.00	Jun-30-26 08:00 AM A	Jul-05-26 08:00 AM A																												
L1350	POUR - P1-12	1.00	Jul-01-26 08:00 AM	Jul-01-26 04:00 PM																												
L1070	TIE REBAR - P1-9, P1-10, P1-11	2.00	Jul-01-26 08:00 AM A	Jul-02-26 04:00 PM																												
L1360	CURE - P1-12	3.00	Jul-02-26 08:00 AM	Jul-04-26 04:00 PM																												
L1080	POUR - P1-9, P1-10, P1-11	2.00	Jul-03-26 08:00 AM	Jul-06-26 04:00 PM																												
L1140	TIE REBAR - P1-4, P1-13	2.00	Jul-06-26 08:00 AM	Jul-07-26 04:00 PM																												
L1090	CURE - P1-9, P1-10, P1-11	3.00	Jul-07-26 08:00 AM	Jul-09-26 04:00 PM																												
L1150	POUR - P1-4, P1-13	3.00	Jul-08-26 08:00 AM	Jul-10-26 04:00 PM																												
L1160	CURE - P1-4, P1-13	3.00	Jul-11-26 08:00 AM	Jul-13-26 04:00 PM																												
PHASE II		29.00	Jul-14-26 08:00 AM	Aug-21-26 04:00 PM																												
L1170	INSTALL TCP - PHASE II	1.00	Jul-14-26 08:00 AM	Jul-14-26 04:00 PM																												
L1180	REMOVE EXISTING ASPHALT AND BASE - PHASE II	4.00	Jul-15-26 08:00 AM	Jul-20-26 04:00 PM																												
L1200	PROCESS SUBGRADE - PHASE II	0.00	Jul-21-26 08:00 AM	Jul-21-26 08:00 AM																												
L1210	TIE REBAR - P2-1, P2-3	3.00	Jul-21-26 08:00 AM	Jul-23-26 04:00 PM																												
L1220	POUR - P2-1, P2-3	2.00	Jul-24-26 08:00 AM	Jul-27-26 04:00 PM																												
L1240	CURE - P2-1, P2-3	3.00	Jul-28-26 08:00 AM	Jul-30-26 04:00 PM																												
L1250	TIE REBAR - P2-4, P2-5, P2-10, P2-11	2.00	Jul-28-26 08:00 AM	Jul-29-26 04:00 PM																												
L1260	POUR - P2-4, P2-5, P2-10, P2-11	4.00	Jul-31-26 08:00 AM	Aug-05-26 04:00 PM																												
L1270	CURE - P2-4, P2-5, P2-10, P2-11	3.00	Aug-06-26 08:00 AM	Aug-08-26 04:00 PM																												
L1280	TIE REBAR - P2-6, P2-7, P2-9	2.00	Aug-06-26 08:00 AM	Aug-07-26 04:00 PM																												
L1290	POUR - P2-6, P2-7, P2-9	3.00	Aug-10-26 08:00 AM	Aug-12-26 04:00 PM																												
L1300	CURE - P2-6, P2-7, P2-9	3.00	Aug-13-26 08:00 AM	Aug-15-26 04:00 PM																												
L1310	TIE REBAR - BLOCKOUTS	1.00	Aug-13-26 08:00 AM	Aug-13-26 04:00 PM																												
L1320	POUR - BLOCKOUTS	2.00	Aug-14-26 08:00 AM	Aug-17-26 04:00 PM																												



DONALD PRESTON DRIVE
JUNE SCHEDULE UPDATE DD = 7-1-26

Jul-01-26 04:56 PM

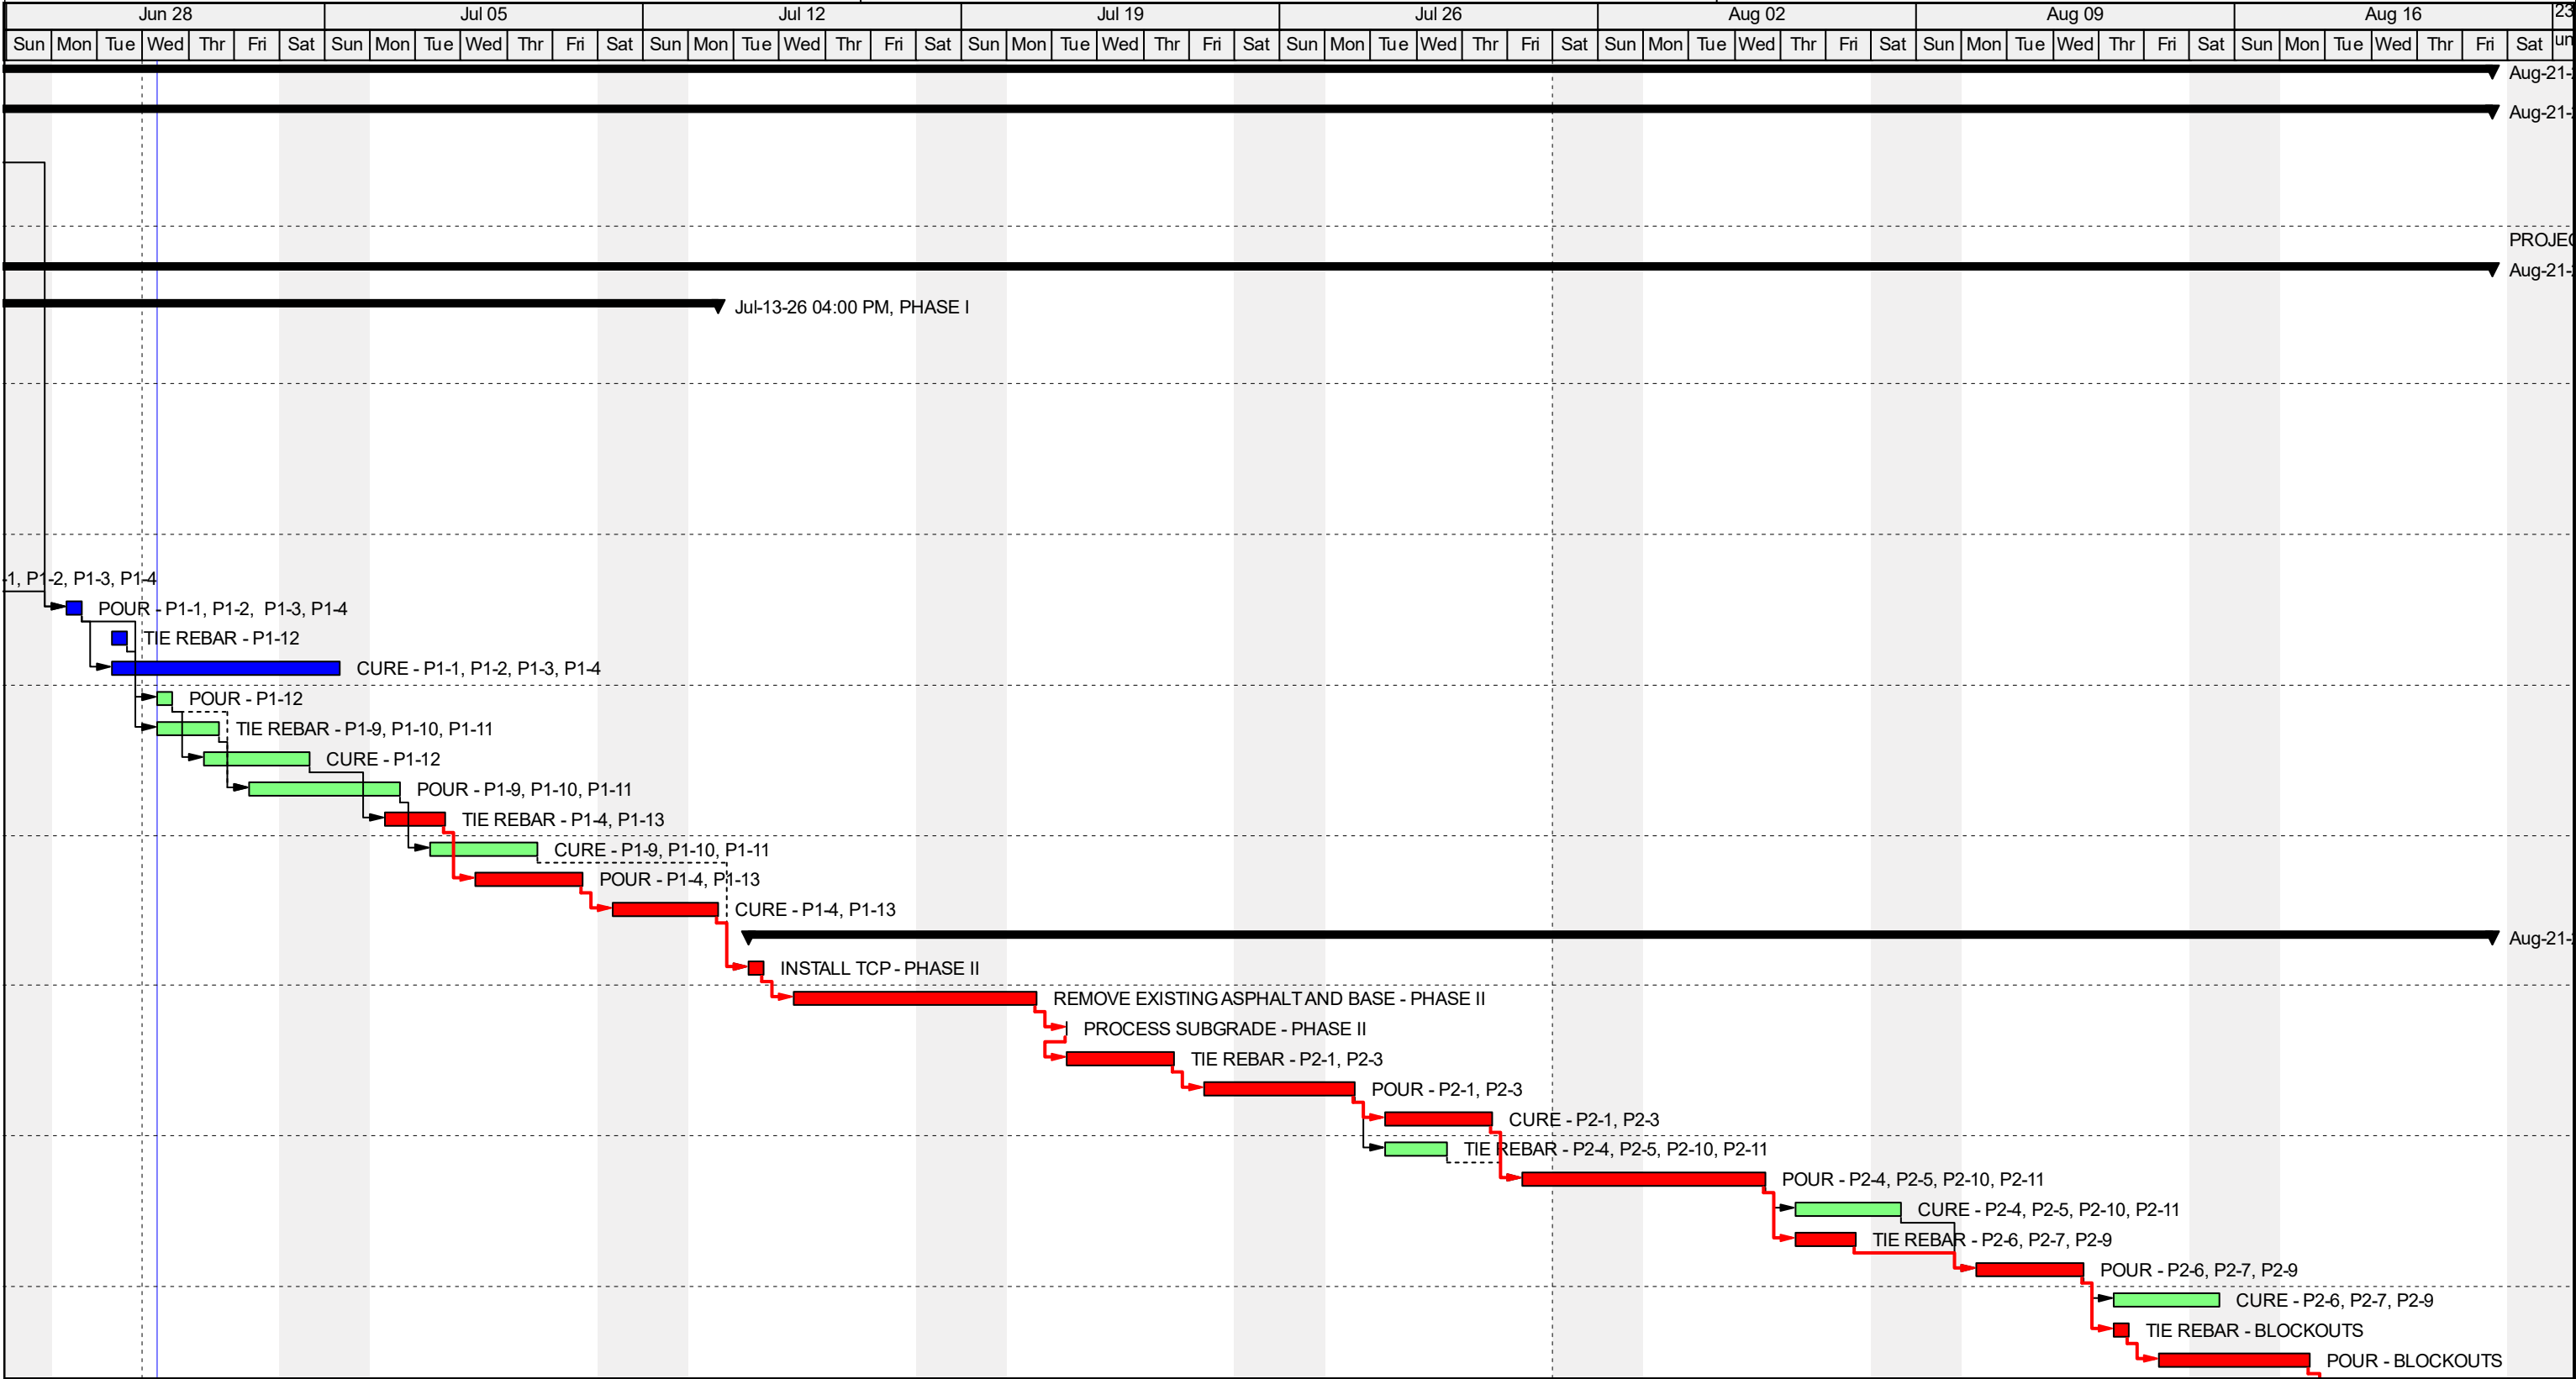

Actual Work Critical Remaining Work Summary
Remaining Work Milestone



DONALD PRESTON DRIVE
JUNE SCHEDULE UPDATE DD = 7-1-26

Jul-01-26 04:56 PM

Activity ID				Activity Name	At Completion Duration	Start	Finish	May 31							Jun 07							Jun 14							Jun 21						
								on	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	
	L1330	CURE - BLOCKOUTS	3.00	Aug-18-26 08:00 AM	Aug-20-26 04:00 PM																														
	A1040	FINAL STRIPING	1.00	Aug-21-26 08:00 AM	Aug-21-26 04:00 PM																														
	A1050	PROJECT FINISH	0.00		Aug-21-26 04:00 PM																														



Jun 28							Jul 05							Jul 12							Jul 19							Jul 26							Aug 02							Aug 09							Aug 16														
Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat								
															</																																																

 Actual Work
  Critical Remaining Work
  Summary
 Remaining Work
 
  Milestone
