



DONALD PRESTON DRIVE
JULY SCHEDULE UPDATE DD = 7-30-26


Jul-30-26 12:29 PM

Activity ID	Activity Name	At Completion Duration	Start	Finish	May 31						Jun 07						Jun 14						Jun 21									
					on	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr			
DONALD PRESTON DR		55.00	Jun-01-26 08:00 AM A	Aug-14-26 04:00 PM																												
ADMINISTRATION		55.00	Jun-01-26 08:00 AM A	Aug-14-26 04:00 PM																												
A1000	PROJECT START	0.00	Jun-01-26 08:00 AM A		PROJECT START																											
A1010	SUBMITTALS	10.00	Jun-01-26 08:00 AM A	Jun-12-26 04:00 PMA	SUBMITTALS																											
A1020	RAILROAD ROE AGREEMENT	15.00	Jun-01-26 08:00 AM A	Jun-19-26 04:00 PMA	RAILROAD ROE AGREEMENT																											
A1030	PROJECT TIME	75.00	Jun-01-26 08:00 AM A	Aug-14-26 04:00 PM																												
CONSTRUCTION		55.00	Jun-01-26 08:00 AM A	Aug-14-26 04:00 PM																												
PHASE I		31.00	Jun-01-26 08:00 AM A	Jul-13-26 04:00 PMA																												
L1000	INSTALL PROJECT SIGNAGE AND TCP - PHASE I	1.00	Jun-01-26 08:00 AM A	Jun-01-26 04:00 PMA	INSTALL PROJECT SIGNAGE AND TCP - PHASE I																											
L1010	REMOVE EXISTING ASPHALT AND BASE - PHASE I	4.00	Jun-02-26 08:00 AM A	Jun-05-26 04:00 PMA	REMOVE EXISTING ASPHALT AND BASE - PHASE I																											
L1020	REMOVE CURB & GUTTER - PHASE I	1.00	Jun-08-26 08:00 AM A	Jun-08-26 04:00 PMA	REMOVE CURB & GUTTER - PHASE I																											
L1030	PROCESS SUBGRADE - NON-RAILROAD - PHASE I	0.00	Jun-09-26 08:00 AM A	Jun-09-26 08:00 AM A	PROCESS SUBGRADE - NON-RAILROAD - PHASE I																											
L1110	TIE REBAR - P1-6, P1-7, P1-14	1.00	Jun-10-26 08:00 AM A	Jun-10-26 04:00 PMA	TIE REBAR - P1-6, P1-7, P1-14																											
L1120	POUR - P1-6, P1-7, P1-14	2.00	Jun-11-26 08:00 AMA	Jun-12-26 04:00 PMA	POUR - P1-6, P1-7, P1-14																											
L1130	CURE - P1-6, P1-7, P1-14	5.00	Jun-13-26 08:00 AM A	Jun-17-26 04:00 PMA	CURE - P1-6, P1-7, P1-14																											
L1100	PROCESS SUBGRADE - RAILROAD AREA - PHASE I	0.00	Jun-17-26 08:00 AM A	Jun-17-26 08:00 AM A	PROCESS SUBGRADE - RAILROAD AREA - PH																											
L1040	TIE REBAR - P1-1, P1-2, P1-3, P1-4	2.00	Jun-23-26 08:00 AM A	Jun-24-26 04:00 PMA	TIE																											
L1050	POUR - P1-1, P1-2, P1-3, P1-4	1.00	Jun-29-26 08:00 AM A	Jun-29-26 04:00 PMA																												
L1060	CURE - P1-1, P1-2, P1-3, P1-4	5.00	Jun-30-26 08:00 AM A	Jul-05-26 08:00 AM A																												
L1340	TIE REBAR - P1-12	1.00	Jun-30-26 08:00 AM A	Jun-30-26 04:00 PMA																												
L1070	TIE REBAR - P1-9, P1-10, P1-11	2.00	Jul-01-26 08:00 AM A	Jul-02-26 04:00 PMA																												
L1350	POUR - P1-12	1.00	Jul-01-26 08:00 AM A	Jul-01-26 04:00 PMA																												
L1360	CURE - P1-12	3.00	Jul-02-26 08:00 AM A	Jul-04-26 04:00 PMA																												
L1080	POUR - P1-9, P1-10, P1-11	2.00	Jul-03-26 08:00 AM A	Jul-06-26 04:00 PMA																												
L1140	TIE REBAR - P1-4, P1-13	2.00	Jul-06-26 08:00 AM A	Jul-07-26 04:00 PMA																												
L1090	CURE - P1-9, P1-10, P1-11	3.00	Jul-07-26 08:00 AM A	Jul-09-26 04:00 PMA																												
L1150	POUR - P1-4, P1-13	3.00	Jul-08-26 08:00 AM A	Jul-10-26 04:00 PMA																												
L1160	CURE - P1-4, P1-13	3.00	Jul-11-26 08:00 AMA	Jul-13-26 04:00 PMA																												
PHASE II		22.00	Jul-16-26 08:00 AM A	Aug-14-26 04:00 PM																												
L1170	INSTALL TCP - PHASE II	1.00	Jul-16-26 08:00 AM A	Jul-16-26 04:00 PMA																												
L1180	REMOVE EXISTING ASPHALT AND BASE - PHASE II	2.00	Jul-20-26 08:00 AM A	Jul-21-26 04:00 PMA																												
L1200	PROCESS SUBGRADE - PHASE II	0.00	Jul-21-26 08:00 AM A	Jul-21-26 08:00 AM A																												
L1210	TIE REBAR - P2-1, P2-3	3.00	Jul-22-26 08:00 AM A	Jul-24-26 04:00 PMA																												
L1220	POUR - P2-1, P2-3	2.00	Jul-23-26 08:00 AM A	Jul-24-26 04:00 PMA																												
L1240	CURE - P2-1, P2-3	4.00	Jul-24-26 08:00 AM A	Jul-27-26 04:00 PMA																												
L1250	TIE REBAR - P2-4, P2-5, P2-10, P2-11	2.00	Jul-24-26 08:00 AM A	Jul-27-26 04:00 PMA																												
L1260	POUR - P2-4, P2-5, P2-10, P2-11	3.00	Jul-27-26 08:00 AM A	Jul-29-26 04:00 PMA																												
L1270	CURE - P2-4, P2-5, P2-10, P2-11	3.00	Jul-30-26 08:00 AM	Aug-01-26 04:00 PM																												
L1280	TIE REBAR - P2-6, P2-7, P2-9	2.00	Jul-30-26 08:00 AM	Jul-31-26 04:00 PM																												
L1290	POUR - P2-6, P2-7, P2-9	3.00	Aug-03-26 08:00 AM	Aug-05-26 04:00 PM																												
L1300	CURE - P2-6, P2-7, P2-9	3.00	Aug-06-26 08:00 AM	Aug-08-26 04:00 PM																												
L1310	TIE REBAR - BLOCKOUTS	1.00	Aug-06-26 08:00 AM	Aug-06-26 04:00 PM																												
L1320	POUR - BLOCKOUTS	2.00	Aug-07-26 08:00 AM	Aug-10-26 04:00 PM																												



DONALD PRESTON DRIVE
JULY SCHEDULE UPDATE DD = 7-30-26

Jul-30-26 12:29 PM

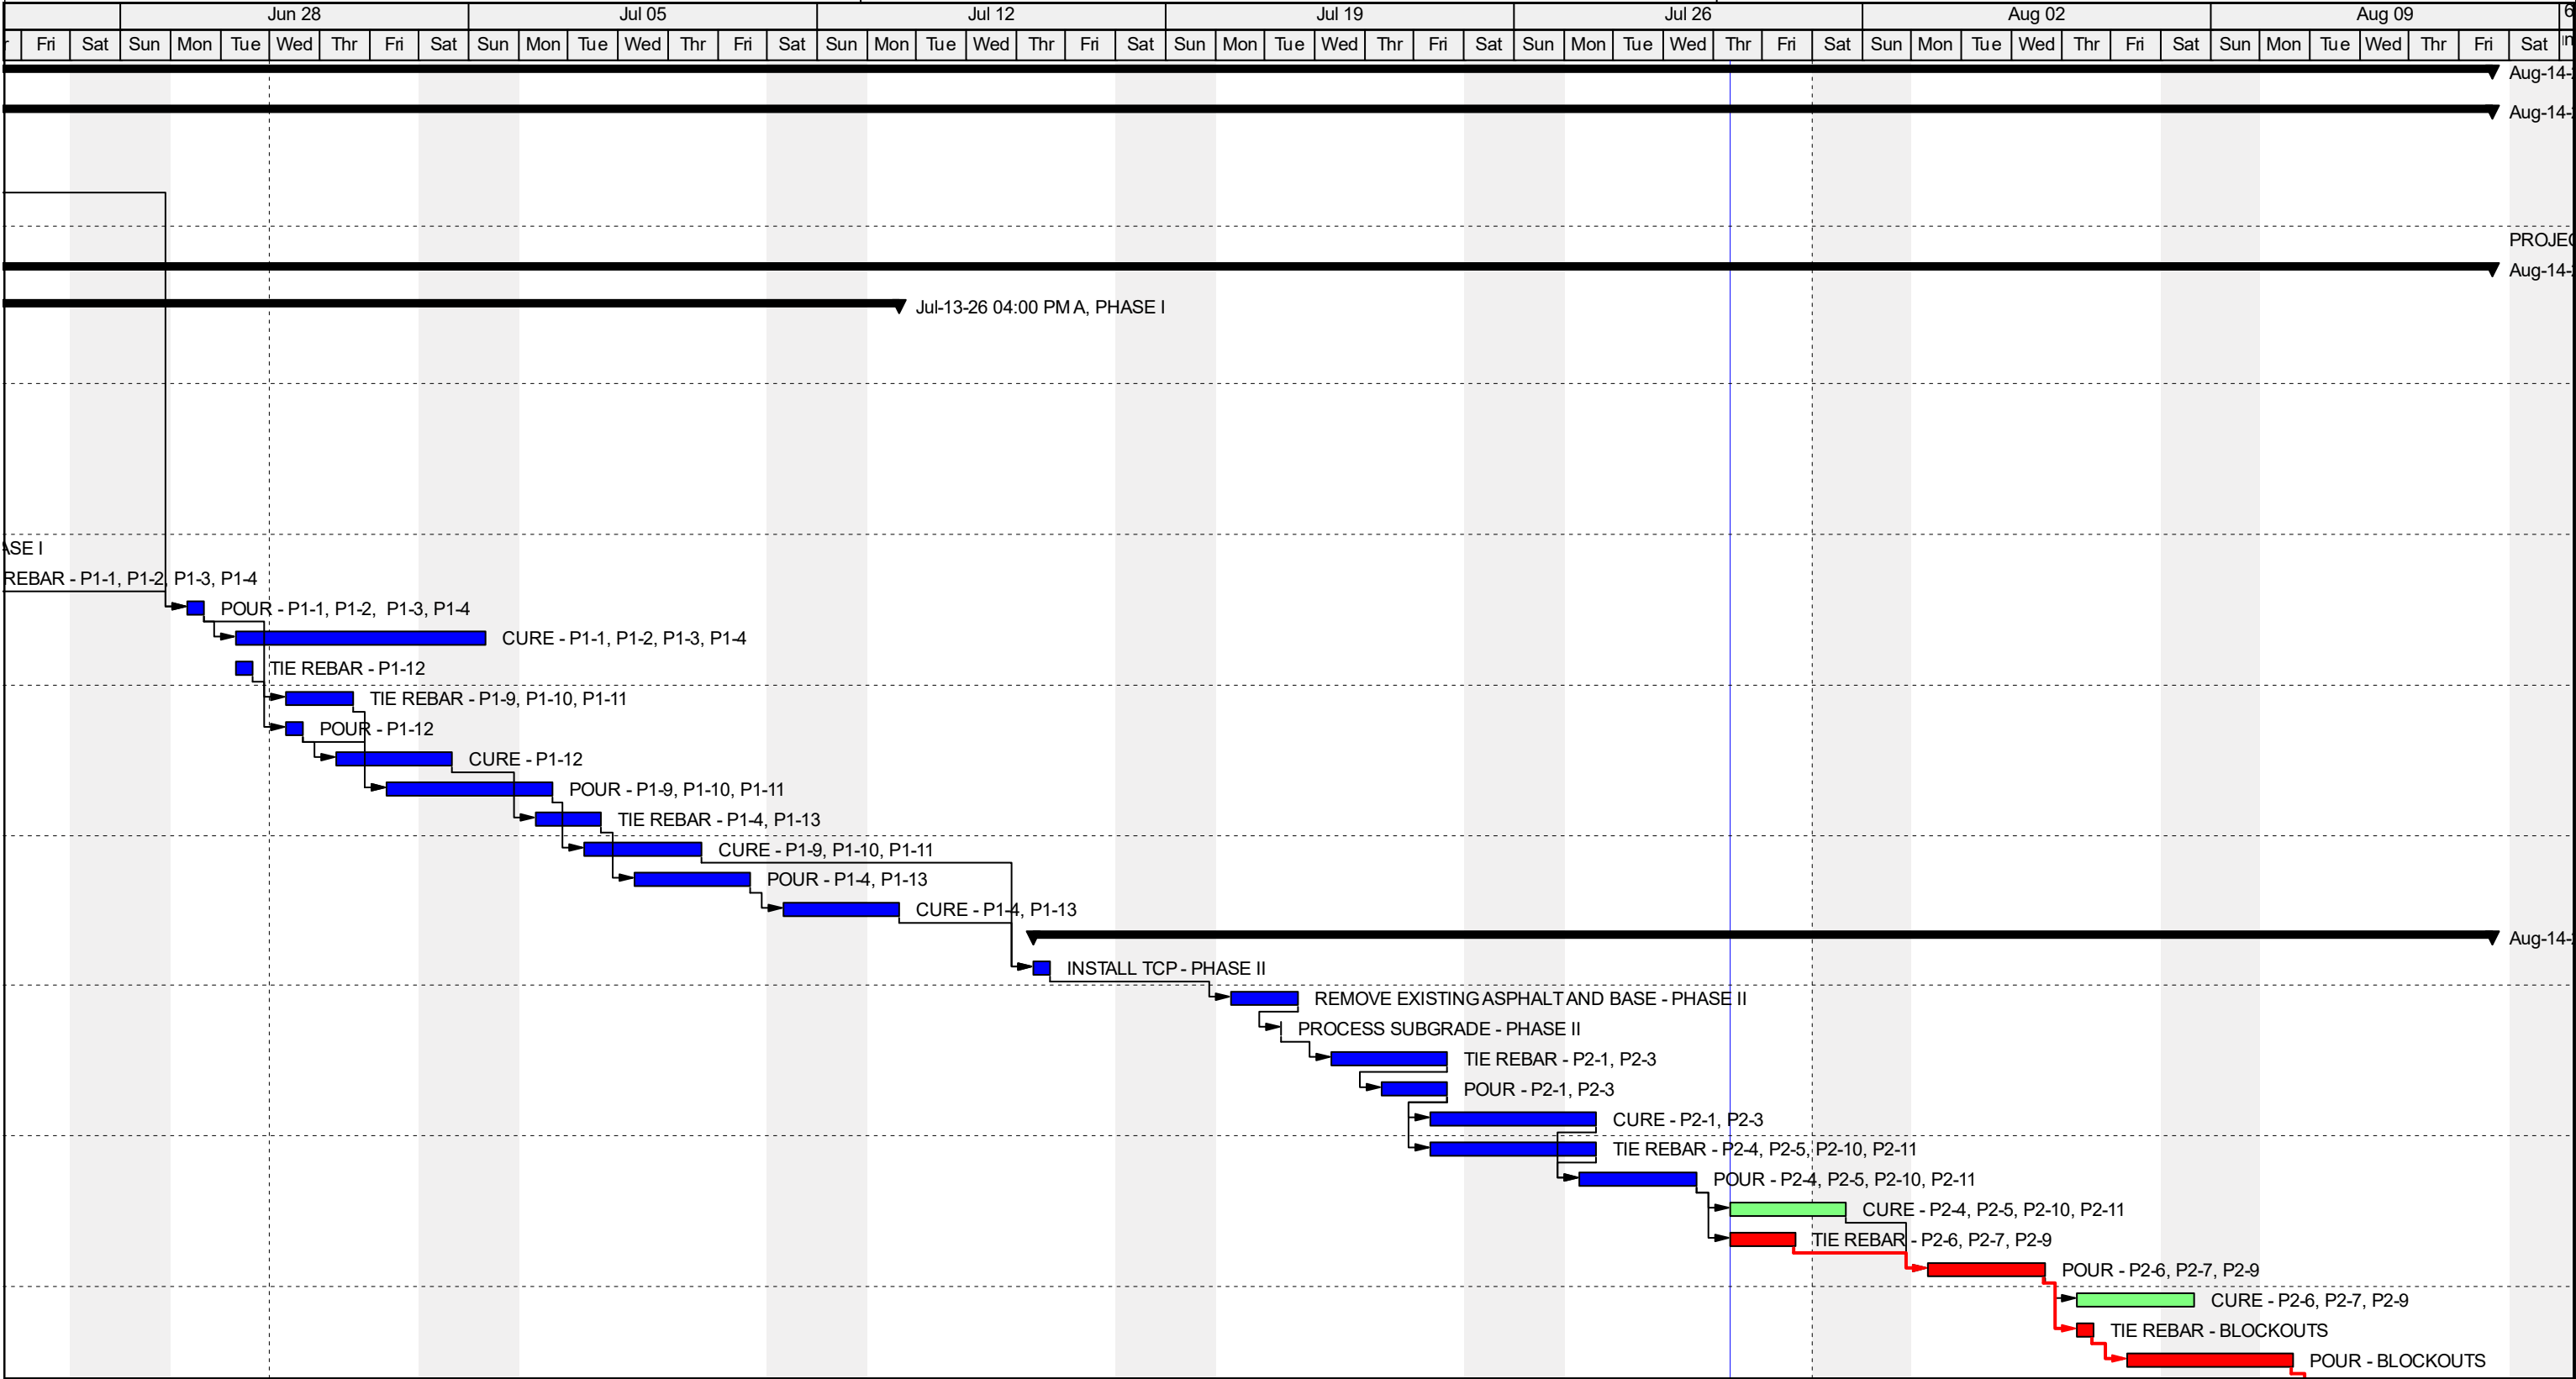

Actual Work Critical Remaining Work Summary
Remaining Work Milestone



DONALD PRESTON DRIVE
JULY SCHEDULE UPDATE DD = 7-30-26

Jul-30-26 12:29 PM

Activity ID				Activity Name	At Completion Duration	Start	Finish	May 31						Jun 07						Jun 14						Jun 21				
								on	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue
	L1330	CURE - BLOCKOUTS	3.00	Aug-11-26 08:00 AM	Aug-13-26 04:00 PM																									
	A1040	FINAL STRIPING	1.00	Aug-14-26 08:00 AM	Aug-14-26 04:00 PM																									
	A1050	PROJECT FINISH	0.00		Aug-14-26 04:00 PM																									



DONALD PRESTON DRIVE
JULY SCHEDULE UPDATE DD = 7-30-26

Jul-30-26 12:29 PM

			Jun 28							Jul 05							Jul 12							Jul 19							Jul 26							Aug 02							Aug 09							6
r	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	Sun	Mon	Tue	Wed	Thr	Fri	Sat	in														

