




## W1045 SR500 12in Waterline Replacement Project Summary

**Project Type:** Water Utility

**Total Project Cost:** \$286,503.74

**Project Timeline:** December 2024 - Jan 2025

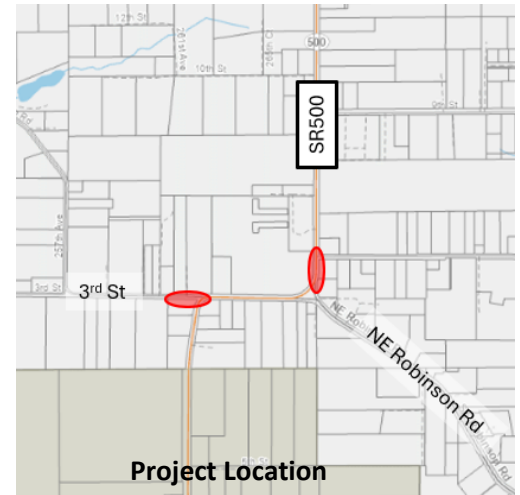

### Project Description

The project consisted of relocating 300 linear feet of 12-inch waterline to make way for upcoming WSDOT roundabouts project on SR500 at NE 3<sup>rd</sup> Street and at NE Robinson Road. Additional required work was added to the scope of the project to extend the 18-inch water stub on NE 3<sup>rd</sup> Street beyond WSDOT's project limits.

### Project Details and Benefits

- The existing 12-inch waterline will be out of the way of WSDOT's improvements.
- The cost of removing and hauling the abandoned 12-inch waterline will be covered by WSDOT at the time of their improvements.

### Project Funding

Project Phase	Year	Total
Design	2024	\$25,000
Construction	2024- 2025	\$260,803.74
Testing	2025	\$700
<b>Total</b>		<b>\$286,503.74</b>
Original Budget Estimate 2025 Omnibus	2025	\$400,000

