

Project: Overall Project Schedule Date: Tue 2/3/26


█ Task █ Milestone █ Summary █ Inactive Task █ Inactive Summary █ Inactive Milestone █ Inactive Summary █ Manual Task █ Manual Summary Rollup █ Manual Summary █ Start-only █ Finish-only █ External Tasks █ External Milestone █ Deadline █ Critical █ Critical Split █ Progress █ Manual Progress

ID	Task Mode	Task Name	Duration	% Complete	Start	Finish	Predecessors	Timeline (Apr '25 to May '26)																											
203	✓	Wharf Wall Paneling	3 days	100%	Tue 3/10/26	Thu 3/12/26	202FS-1 day	[Gantt bar: 3/10/26 - 3/12/26]																											
204	✓	Reception Desk Paneling	2 days	0%	Thu 3/12/26	Fri 3/13/26	203FS-1 day	[Gantt bar: 3/12/26 - 3/13/26]																											
205	✓	Wood Wall Paneling	3 days	100%	Fri 2/27/26	Tue 3/3/26	204FS-1 day	[Gantt bar: 2/27/26 - 3/3/26]																											
206	✓	Corner Guards	2 days	0%	Tue 3/3/26	Wed 3/4/26	205FS-1 day	[Gantt bar: 3/3/26 - 3/4/26]																											
207	✓	Interior Signage	2 days	0%	Wed 3/4/26	Thu 3/5/26	206FS-1 day	[Gantt bar: 3/4/26 - 3/5/26]																											
208	✓	<b>Acoustics (SOV #36)</b>	<b>15 days</b>	<b>0%</b>	<b>Wed 3/4/26</b>	<b>Tue 3/24/26</b>		[Gantt bar: 3/4/26 - 3/24/26]																											
209	✓	Ceiling Baffles	7 days	0%	Wed 3/4/26	Thu 3/12/26	176	[Gantt bar: 3/4/26 - 3/12/26]																											
210	✓	Ceiling PET Panels	4 days	0%	Fri 3/13/26	Wed 3/18/26	209	[Gantt bar: 3/13/26 - 3/18/26]																											
211	✓	Wall Panels	4 days	0%	Thu 3/19/26	Tue 3/24/26	210	[Gantt bar: 3/19/26 - 3/24/26]																											
212	✓	<b>Finish Electrical (SOV #32)</b>	<b>55 days</b>	<b>8%</b>	<b>Tue 1/20/26</b>	<b>Wed 4/8/26</b>		[Gantt bar: 1/20/26 - 4/8/26]																											
213	✓	Main Switchgear Delivery	0 days	100%	Tue 1/20/26	Tue 1/20/26	139FS+3 days	[Milestone: 1/20/26]																											
214	✓	Triad Switchgear & Transformer Pad Install/QAC	8 days	100%	Tue 1/20/26	Fri 1/30/26	213	[Gantt bar: 1/20/26 - 1/30/26]																											
215	✓	<b>PG&amp;E Primary Scope (By PG&amp;E)</b>	47 days	0%	Fri 1/30/26	Wed 4/8/26	214	[Gantt bar: 1/30/26 - 4/8/26]																											
216	✓	Finish Electrical Tasks Concurrent with waiting on PG&E Primary	30 days	0%	Fri 1/30/26	Mon 3/16/26	214	[Gantt bar: 1/30/26 - 3/16/26]																											
217	✓	Finish Electrical Tasks After PG&E Primary	11 days	0%	Mon 3/16/26	Tue 3/31/26	216	[Gantt bar: 3/16/26 - 3/31/26]																											
218	✓	AV Equipment	5 days	0%	Tue 3/24/26	Tue 3/31/26	217FF	[Gantt bar: 3/24/26 - 3/31/26]																											
219	✓	<b>Landscaping (SOV #35 &amp; Patio Project)</b>	<b>35 days</b>	<b>21%</b>	<b>Fri 1/30/26</b>	<b>Mon 3/23/26</b>		[Gantt bar: 1/30/26 - 3/23/26]																											
220	✓	Fountain	5 days	0%	Fri 1/30/26	Fri 2/6/26	214	[Gantt bar: 1/30/26 - 2/6/26]																											
221	✓	Irrigation	5 days	100%	Fri 2/6/26	Fri 2/13/26	220	[Gantt bar: 2/6/26 - 2/13/26]																											
222	✓	Gravel Bases	2 days	0%	Fri 2/13/26	Wed 2/18/26	221	[Gantt bar: 2/13/26 - 2/18/26]																											
223	✓	Top Soil	3 days	0%	Wed 2/18/26	Mon 2/23/26	222	[Gantt bar: 2/18/26 - 2/23/26]																											
224	✓	Planting	7 days	0%	Mon 2/23/26	Wed 3/4/26	223	[Gantt bar: 2/23/26 - 3/4/26]																											
225	✓	Mulch	3 days	0%	Wed 3/4/26	Mon 3/9/26	224	[Gantt bar: 3/4/26 - 3/9/26]																											
226	✓	Bike Rack	2 days	0%	Mon 3/9/26	Wed 3/11/26	225	[Gantt bar: 3/9/26 - 3/11/26]																											
227	✓	Wood Benches	3 days	75%	Wed 3/11/26	Mon 3/16/26	226	[Gantt bar: 3/11/26 - 3/16/26]																											
228	✓	Landscaping Repairs	5 days	0%	Mon 3/16/26	Mon 3/23/26	227	[Gantt bar: 3/16/26 - 3/23/26]																											
229	✓	Striping	3 days	0%	Mon 3/23/26	Thu 3/26/26	219	[Gantt bar: 3/23/26 - 3/26/26]																											
230	✓	Punch List Walk	0 days	0%	Wed 4/8/26	Wed 4/8/26	212	[Milestone: 4/8/26]																											
231	✓	Punch List Tasks	10 days	0%	Wed 4/8/26	Wed 4/22/26	230	[Gantt bar: 4/8/26 - 4/22/26]																											
232	✓	<b>Substantial Completion</b>	0 days	0%	Wed 4/22/26	Wed 4/22/26	233	[Milestone: 4/22/26]																											
233	✓	<b>Building Final Inspection</b>	0 days	0%	Wed 4/22/26	Wed 4/22/26	231	[Milestone: 4/22/26]																											
234	✓	<u>Closeout Procedures</u>	65 days	0%	Tue 1/20/26	Wed 4/22/26	233FS-65 days	[Gantt bar: 1/20/26 - 4/22/26]																											

Project: Overall Project Schedule Date: Tue 2/3/26

Task Milestone Project Summary Inactive Milestone Manual Task Manual Summary Rollup Start-only External Tasks Deadline Critical Split Manual Progress  
Split Summary Inactive Task Inactive Summary Duration-only Manual Summary Finish-only External Milestone Critical Progress

ID	Task Mode	Task Name	Duration	% Complete	Start	Finish	Predecessors	Notes	Qtr 4, 2025	Nov	Dec	Qtr 1, 2026	Jan	Feb	Mar	Qtr 2, 2026	Apr	May
1		<b>Overall Project Schedule</b>	<b>109 days</b>	<b>53%</b>	<b>Mon 11/3/25</b>	<b>Wed 4/15/26</b>												
2	✓	<b>Mobilization</b>	<b>10 days</b>	<b>100%</b>	<b>Mon 11/3/25</b>	<b>Fri 11/14/25</b>												
8	✓	Surveying	45 days	100%	Wed 11/19/25	Thu 1/29/26		EPIC										
9		<b>Sitework</b>	<b>90 days</b>	<b>74%</b>	<b>Mon 11/3/25</b>	<b>Thu 3/19/26</b>												
10	✓	<b>Sitework Demolition</b>	<b>15 days</b>	<b>100%</b>	<b>Mon 11/3/25</b>	<b>Fri 11/21/25</b>		Kraemer										
11	✓	Remove Existing Play Structures	15 days	100%	Mon 11/3/25	Fri 11/21/25												
12	✓	Remove Existing Hardscapes	15 days	100%	Mon 11/3/25	Fri 11/21/25												
13	✓	Miscellaneous Demolition	15 days	100%	Mon 11/3/25	Fri 11/21/25												
14	✓	Rough Grade	30 days	100%	Mon 11/17/25	Tue 1/6/26	10	Kraemer										
15		Underground Utilities	45 days	90%	Mon 11/24/25	Tue 2/3/26	10	Kraemer										
16		Bioswale	45 days	90%	Mon 11/24/25	Tue 2/3/26	10	Kraemer										
17		Finish Grade	5 days	50%	Wed 1/14/26	Fri 2/6/26	15	Kraemer										
18		Class 2 AB	10 days	50%	Wed 1/21/26	Tue 2/17/26	17	Kraemer										
19		Site Concrete	30 days	25%	Wed 2/4/26	Thu 3/19/26	18	Kraemer										
20		Fence Post Sleeves	30 days	25%	Wed 2/4/26	Thu 3/19/26	16	AAA										
21		<b>Landscaping</b>	<b>87 days</b>	<b>9%</b>	<b>Fri 12/5/25</b>	<b>Wed 4/15/26</b>												
22		Automatic Irrigation System	25 days	50%	Wed 12/10/25	Tue 1/20/26	15SS+5 days	K&D										
23		Decomposed Granite	10 days	0%	Fri 3/20/26	Thu 4/2/26	9	K&D										
24		<b>Play Structure Lead Time (Estimated)</b>	<b>67 days</b>	<b>0%</b>	<b>Fri 12/5/25</b>	<b>Wed 3/18/26</b>		K&D										
25		Play Structure(s)	10 days	0%	Thu 3/19/26	Wed 4/1/26	24	K&D										
26		PIP Surfacing	5 days	0%	Thu 4/2/26	Wed 4/8/26	25	K&D										
27		Site Furnishings	5 days	0%	Thu 4/2/26	Wed 4/8/26	25	K&D										
28		Planting	10 days	0%	Thu 4/2/26	Wed 4/15/26	25	K&D										
29		<b>Rod Iron Fencing</b>	<b>19 days</b>	<b>0%</b>	<b>Fri 3/20/26</b>	<b>Wed 4/15/26</b>												
30		42" Fencing	8 days	0%	Fri 3/20/26	Tue 3/31/26	20	AAA										
31		46" Fencing	8 days	0%	Wed 4/1/26	Fri 4/10/26	30	AAA										
32		Hand Rail	3 days	0%	Mon 4/13/26	Wed 4/15/26	31	AAA										
33		Banner Pole	15 days	0%	Fri 3/13/26	Thu 4/2/26	19FF+10 days	SSB										
34		Exterior Painting	5 days	0%	Fri 4/3/26	Thu 4/9/26	19FS+10 days	SSB										
35		Water Fountain Railings	2 days	0%	Fri 4/3/26	Mon 4/6/26	19FS+10 days	SSB										

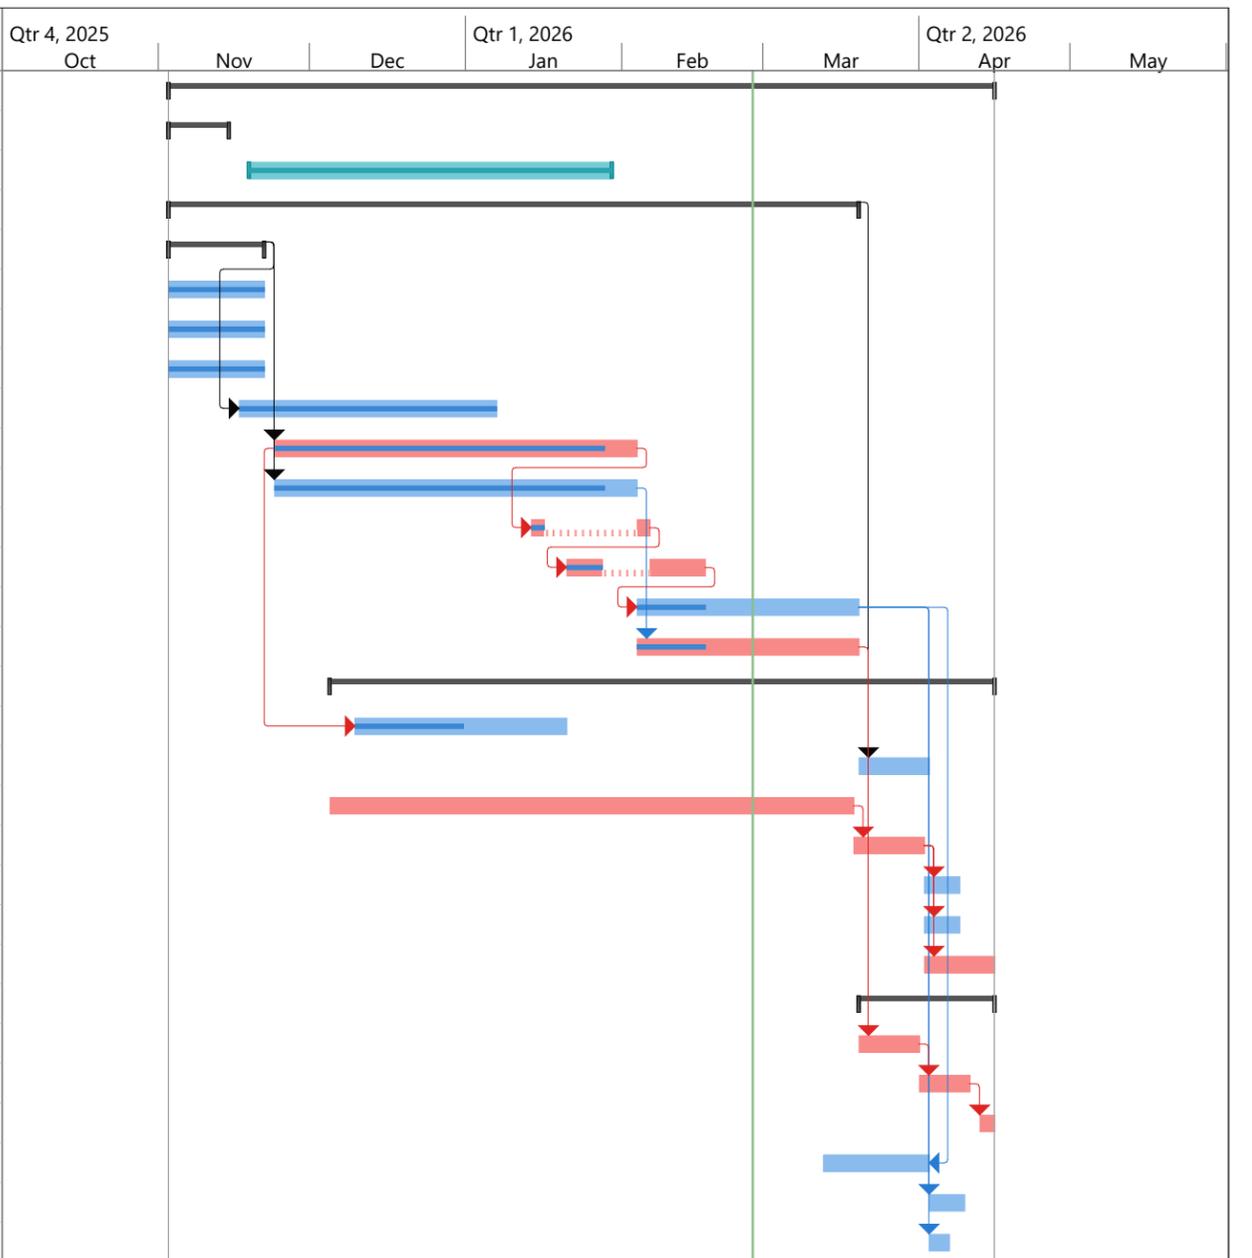

Project: Treasure Cover Playgro  
Date: Fri 2/27/26

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	D	Half 1, 2026	J	F	M	A	M	J	Half
1		<b>JADE ST RESTROOM REMODEL</b>	<b>54 days</b>	<b>Mon 1/12/26</b>	<b>Mon 3/30/26</b>										
2		<b>Mobilize</b>	<b>2 days</b>	<b>Mon 1/12/26</b>	<b>Tue 1/13/26</b>										
3		Restrooms and Fence	1 day	Mon 1/12/26	Mon 1/12/26										
4		Safeoff	1 day	Tue 1/13/26	Tue 1/13/26	3									
5		<b>Interiors</b>	<b>49 days</b>	<b>Wed 1/14/26</b>	<b>Wed 3/25/26</b>										
6		Demo fixtures, Doors, Windows, etc	5 days	Wed 1/14/26	Wed 1/21/26	4									
7		Framing & Backing Modifications	4 days	Thu 1/22/26	Tue 1/27/26	6									
8		Plumbing Rough-In	7 days	Wed 1/28/26	Thu 2/5/26	7									
9		Electrical Rough-In	7 days	Fri 2/6/26	Tue 2/17/26	8									
10		Rough-In Inspections	1 day	Wed 2/18/26	Wed 2/18/26	9									
11		CMU Patchback	1 day	Thu 2/19/26	Thu 2/19/26	10									
12		Install New Louvers	2 days	Fri 2/20/26	Mon 2/23/26	11									
13		Install New Doors	2 days	Tue 2/24/26	Wed 2/25/26	12									
14		Epoxy Flooring and Base	5 days	Thu 2/26/26	Wed 3/4/26	13									
15		Epoxy Wall	5 days	Thu 2/26/26	Wed 3/4/26	13									
16		Bathroom Fixture Install	3 days	Thu 3/5/26	Mon 3/9/26	15									
17		Bathroom Accessories Install	2 days	Tue 3/10/26	Wed 3/11/26	16									
18		Electrical Fixture Install	3 days	Thu 3/12/26	Mon 3/16/26	17									
19		Final Plumbing Connections	2 days	Tue 3/17/26	Wed 3/18/26	18									
20		Final Electrical Connections	2 days	Thu 3/19/26	Fri 3/20/26	19									
21		Painting	3 days	Mon 3/23/26	Wed 3/25/26	20									
22		Plumb & Electrical Final Inspections	1 day	Mon 3/23/26	Mon 3/23/26	20									
23		<b>Roofing</b>	<b>17 days</b>	<b>Mon 2/2/26</b>	<b>Wed 2/25/26</b>	<b>2</b>									
24		Demo Existing Roof Sheating Roof	2 days	Mon 2/2/26	Tue 2/3/26										
25		Repair Rafter	2 days	Wed 2/4/26	Thu 2/5/26	24									
26		Installing New Plywood sheathing on Roof	1 day	Fri 2/6/26	Fri 2/6/26	25									
27		Roof Shear Inspection	1 day	Mon 2/9/26	Mon 2/9/26	26									
28		Install Roof Underlayment	4 days	Tue 2/10/26	Fri 2/13/26	27									
29		Install Shingle Roof	4 days	Tue 2/17/26	Fri 2/20/26	28									
30		Install Gutters, Downpouts and Flashing	2 days	Mon 2/23/26	Tue 2/24/26	29									
31		Roofing Final Inspection	1 day	Wed 2/25/26	Wed 2/25/26	30									
32		<b>Site work</b>	<b>25 days</b>	<b>Mon 2/2/26</b>	<b>Mon 3/9/26</b>										
33		Demo Existing Sidewalks	5 days	Mon 2/2/26	Fri 2/6/26										
34		New Concrete Sidewalk	5 days	Mon 2/9/26	Fri 2/13/26	33									
35		New Asphalt Sidewalk	5 days	Tue 2/17/26	Mon 2/23/26	34									
36		New Concrete Bench	5 days	Tue 2/24/26	Mon 3/2/26	35									
37		Concrete Curbs	5 days	Tue 3/3/26	Mon 3/9/26	36									
38		<b>Punch List</b>	<b>4 days</b>	<b>Tue 3/24/26</b>	<b>Fri 3/27/26</b>	<b>22</b>									
39		<b>Final Clean</b>	<b>1 day</b>	<b>Mon 3/30/26</b>	<b>Mon 3/30/26</b>	<b>38</b>									

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			
