


Columbus Integrated Waste




We do amazing.

ACC

ATLANTIC COAST
CONSULTING, INC.

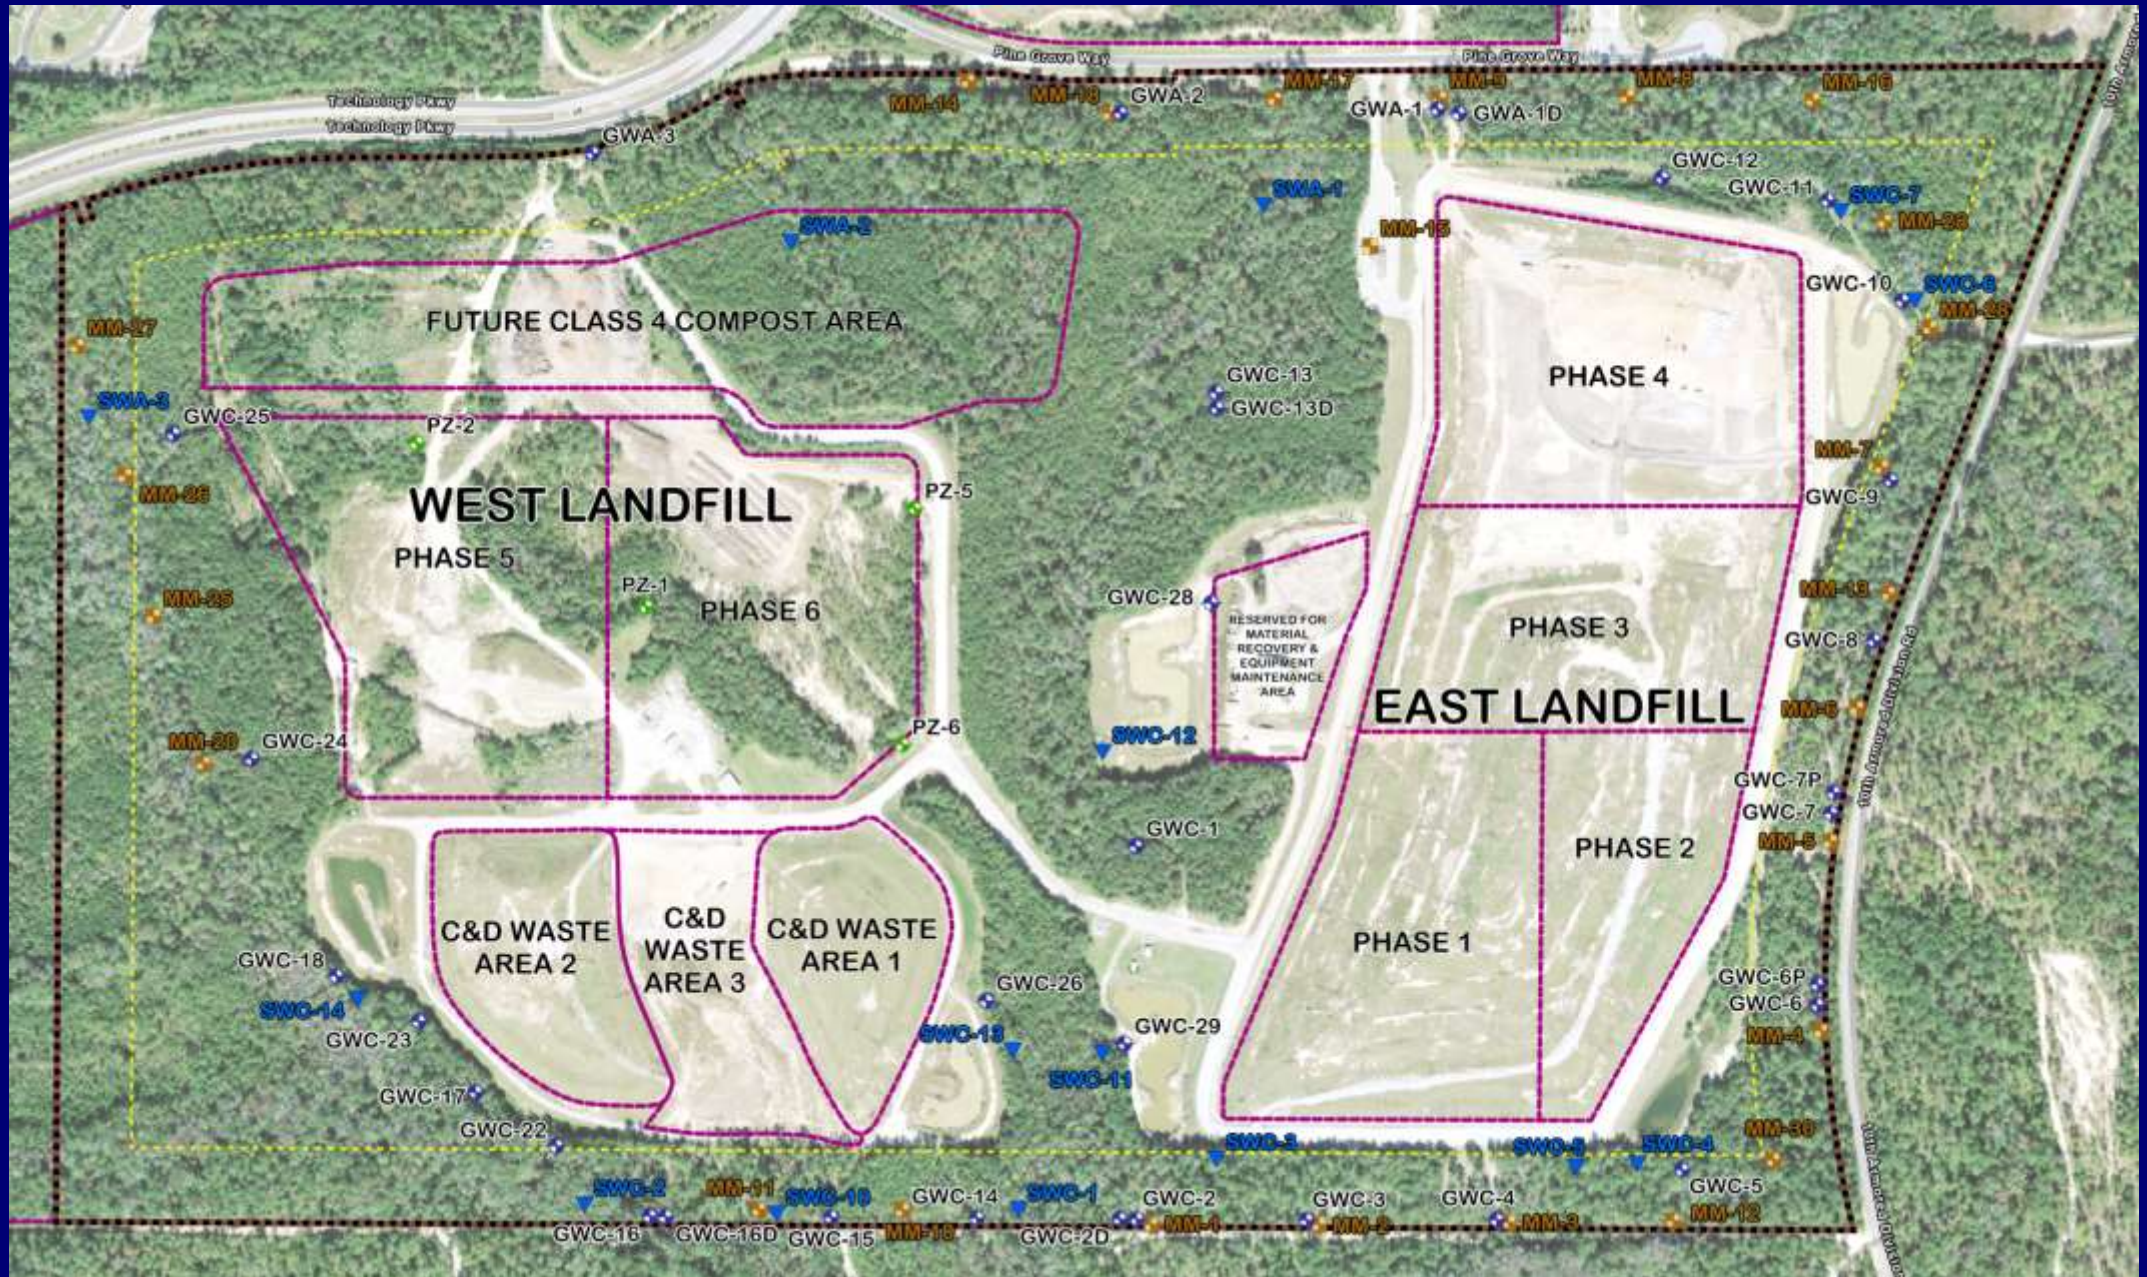



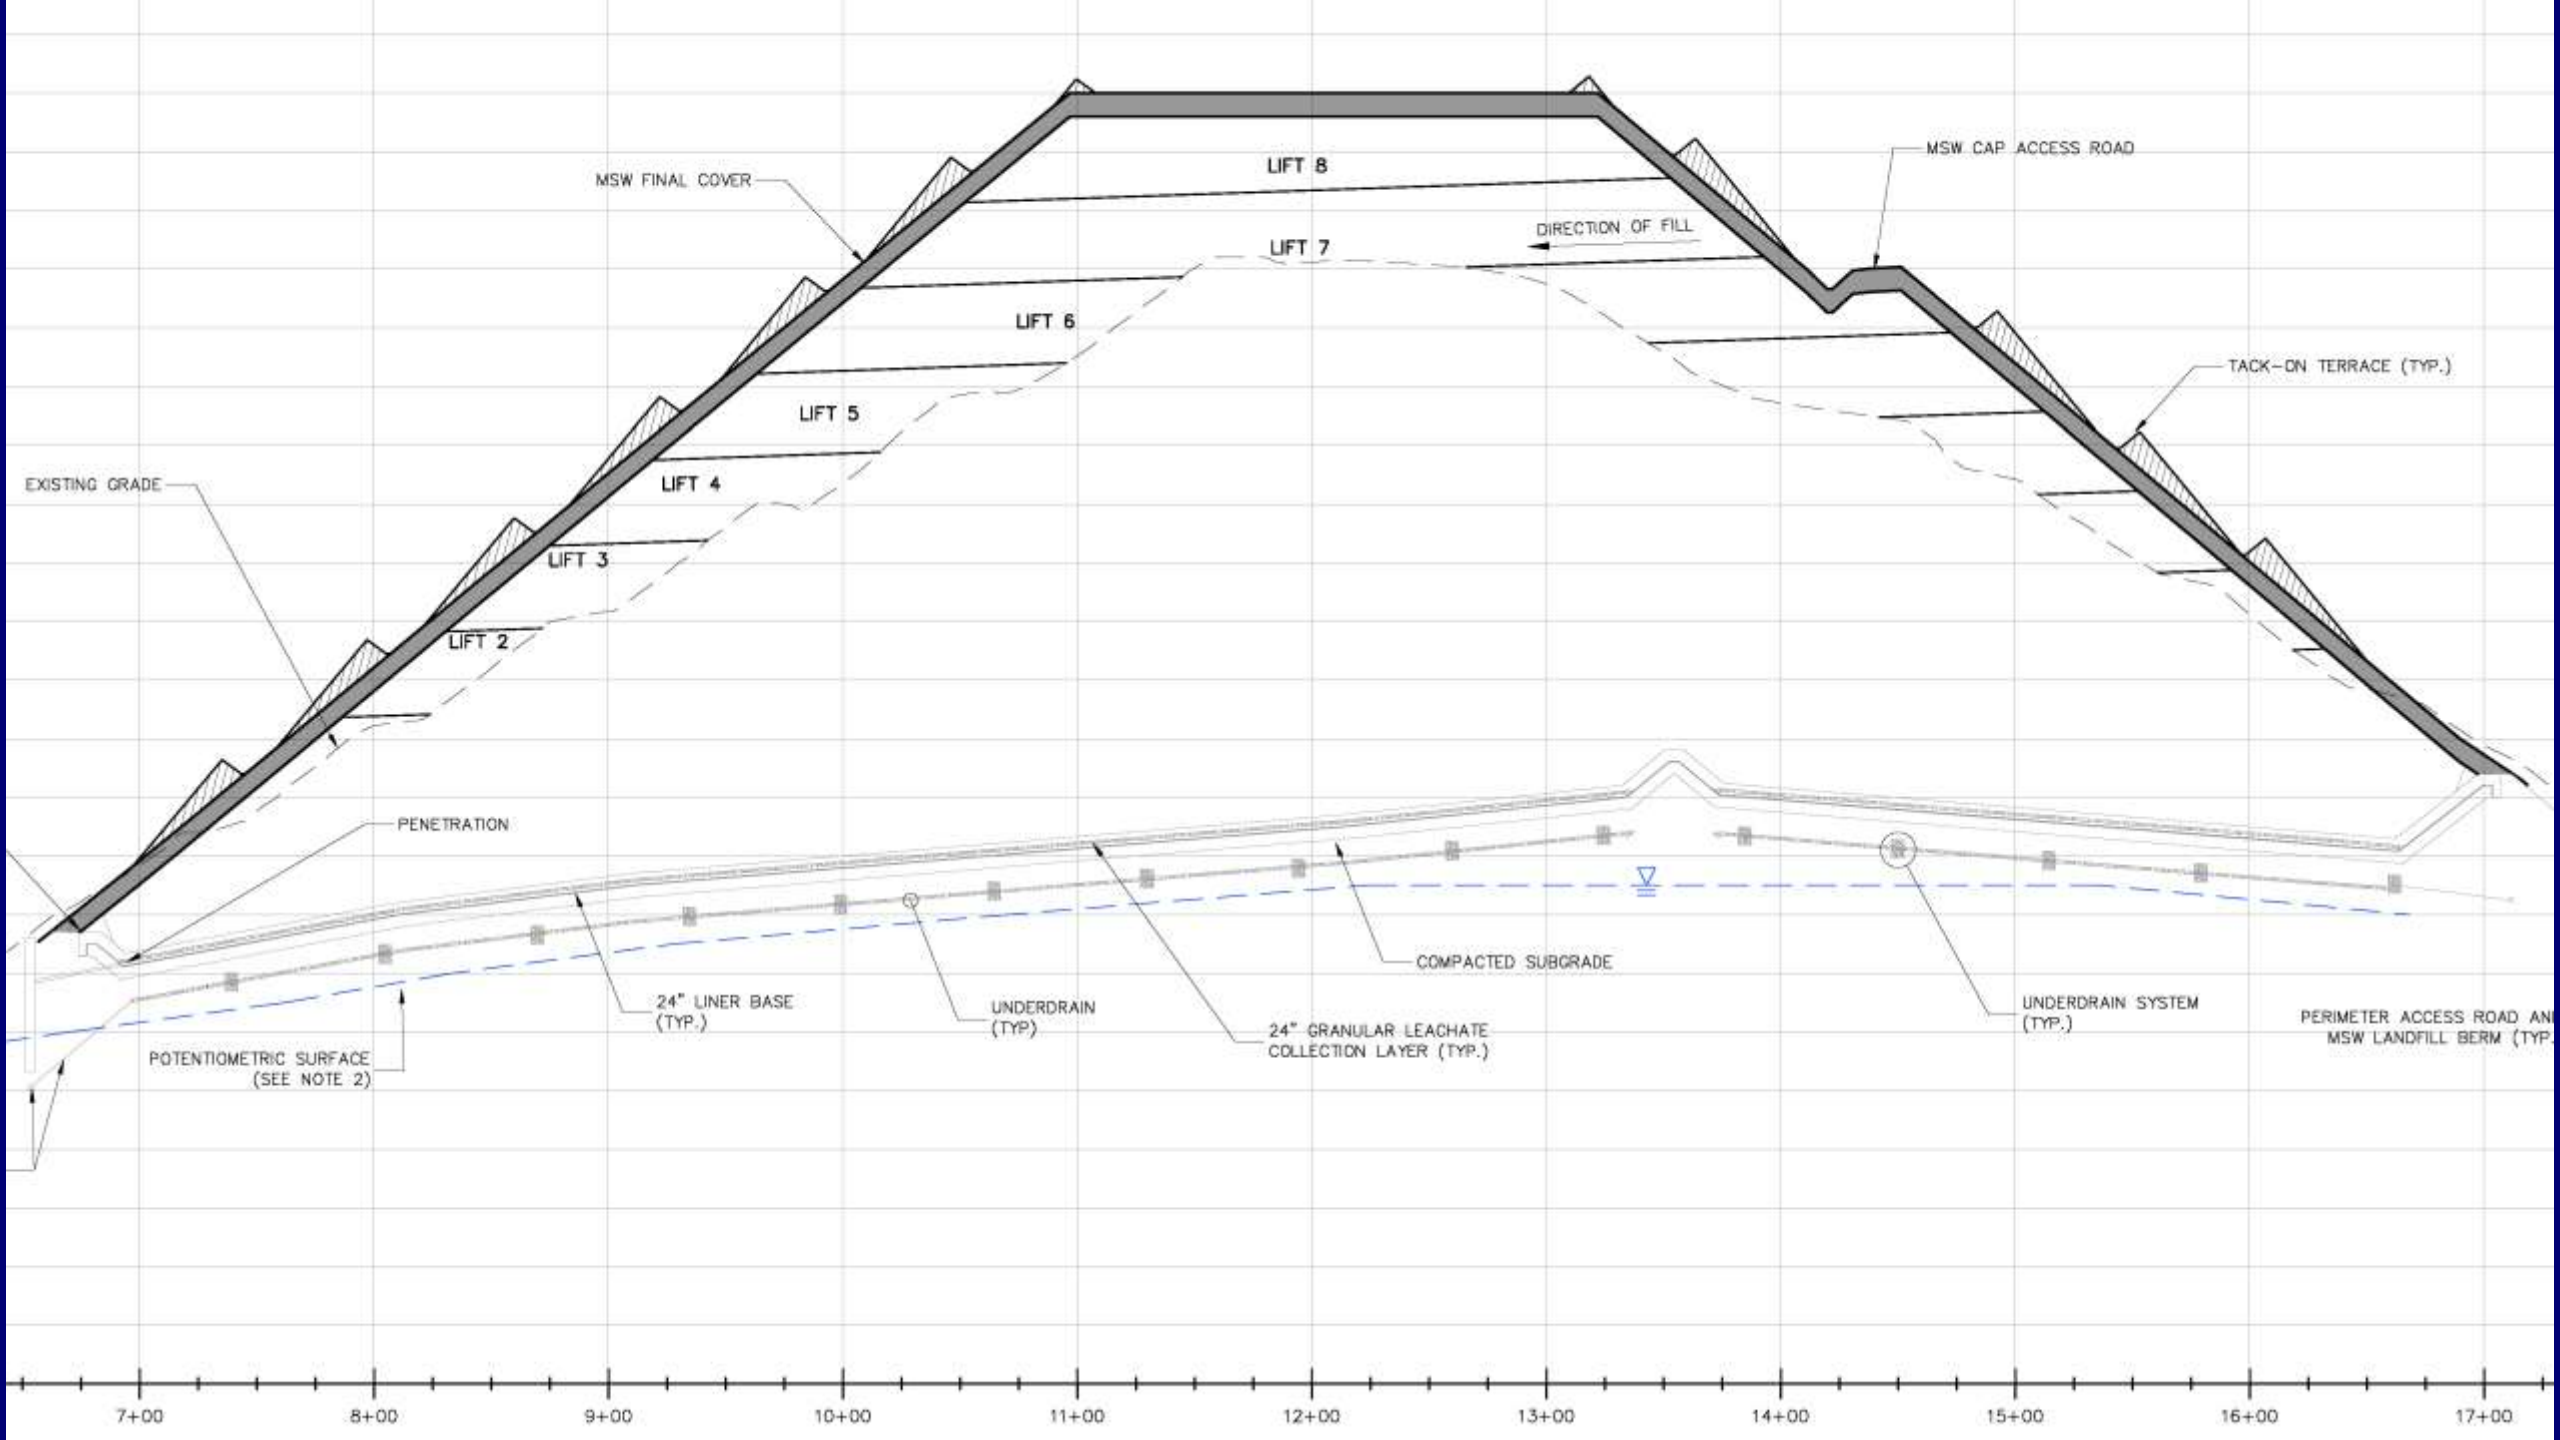

Pine Grove Major Modification Permitting Timeline

- September 2019 task order approved and initiated work
- August 2020 Suitability Report submitted; approved April 2021
- August 2021 revised D&O Plan submitted
- August 2021 to January 9, 2024
 - **2.5-year timeline to receive EPD comments**
 - Multiple follow-ups by CCG/ACC to expedite review
- Currently in the comment/response phase

Pine Grove

Remaining Capacity/End of Life

- MSW currently constructed (Phases 1-4) – January 2026
- MSW Phases 1-4 w/ vertical expansion – October 2035
- MSW currently permitted total – December 2045
- MSW total w/ vertical expansion – January 2062
- C&D total – November 2044

Pending MSW Major Modification Vertical Expansion

- Will increase airspace by ~ 2.5M CYs
- Will bring in ~ **\$61M** revenue from additional MSW airspace
- Life expectancy will increase ~ 17 years
- Class 4 compost area

Phase 5 Construction

- Construct 3 of 5 cells with two cells to be completed by January 2026
- New infrastructure; access road, lift station, force-main
- Engineer's Opinion of Probable Cost:
 - Cells 5A-5C Construction - \$7,436,330
 - Construction Drawings and Bid Assistance - \$93,000
 - Construction Administration Engineering - \$75,000
 - Construction Quality Assurance - \$530,500

THANK YOU

