




INFRASTRUCTURE UPDATE

MARCH 11, 2025

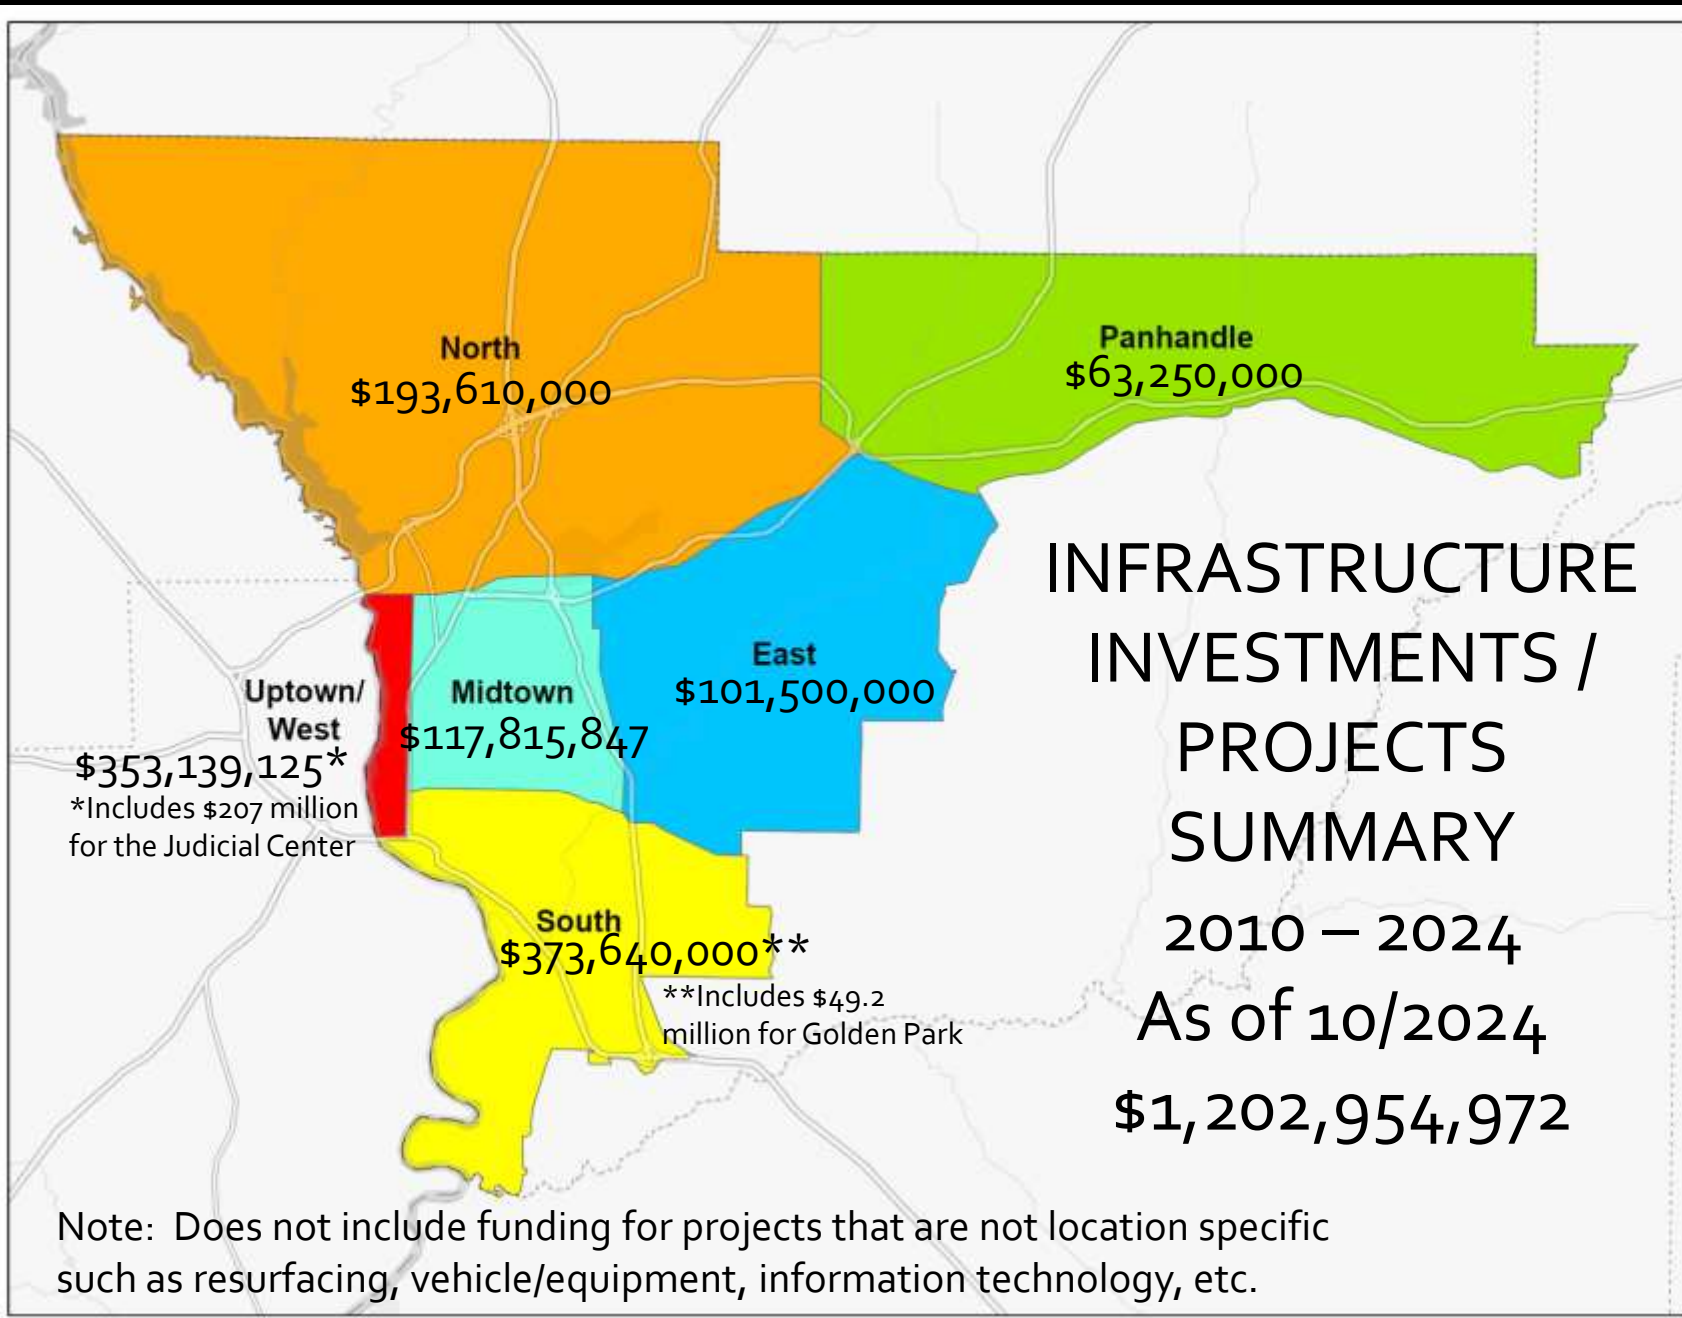

Funding Sources

-
- Transportation Special Purpose Local Option Sales Tax (TSPLOST) 2012
 - Transportation Special Purpose Local Option Sales Tax (TSPLOST) 2022
 - TSPLOST Discretionary Funds
 - Special Purpose Local Option Sales Tax (SPLOST) 2021
 - Other Local Option Sales Tax (OLOST) Infrastructure Fund
 - Stormwater Fund
 - Paving Fund
 - Georgia Department of Transportation (GDOT) Grants and Programs
 - Private Donations and Public-Private Partnerships (Friends of the Dragonfly Trail, Columbus Regional Tennis Association (CORTA), Columbus, GA Pickleball Association and others)
 - Columbus Building Authority Bonds

Projects Under Construction

Williams Road/Fortson Road Roundabout

Construction of new Roundabout

Start Date: April 2, 2024

Est. Completion: Sept. 2025

Budget: \$5,066,958.10

Funding Sources:

FY 17 LMIG

FY 20 LMIG

Paving Fund

OLOST Infrastructure

Percent Complete: 20%



Projects Under Construction (continued)

Mott's Green Plaza Enhancement

Plaza enhancement including riverwalk realignment and re-use of existing donor brick.

Start Date: May 20, 2024

Anticipated Completion: March 2025

Budget: \$1,423,636,05

Funding Source: FY12 TSPLOST Discretionary –Transportation

Percent Complete: 95%

GDOT Grant



Projects Under Construction (continued)

Flood Abatement Project 19th Street System

New box culvert which will contain and run in conjunction with the CSS and reduce flooding issues.

Bids Received: August 7, 2024

Low Bid: Southeastern Site Development
\$13,590,652.61

Start Date: January 14, 2025

Scheduled Completion: November 2025



Projects Under Construction (continued)

I-185 / Buena Vista Road Interchange

- GDOT Managed, 71% Complete
- Est. Cost: \$47.7 million
- Funding Source: FY12 TSPLOST



Projects Under Construction (continued)

I-185 / Cusseta Road Interchange


- GDOT Managed, 53% Complete
- Est. Cost: \$58 million
- Funding Source: FY12 TSPLOST



Projects Under Construction (continued)

SR 1 / US 27 Widening

- GDOT Managed, 29% Complete
- Est. Cost: \$40 million
- Funding Source: FY12 TSPLOST

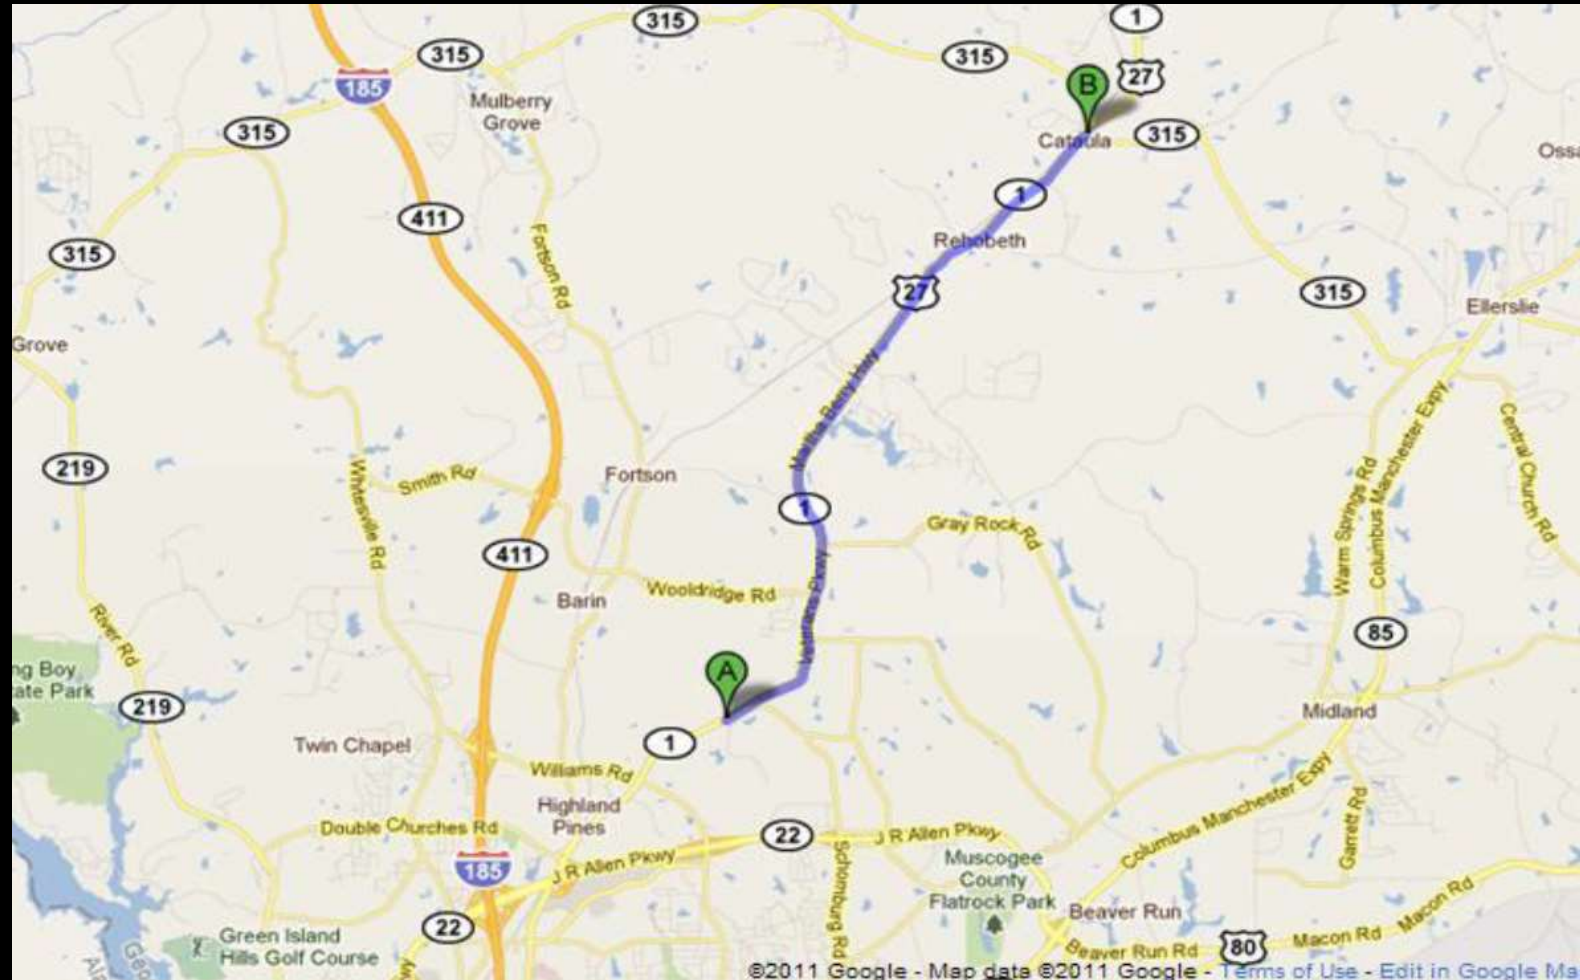

Projects Under Construction (continued)

Spiderweb Phase II (RFB 24-0029)

- Start Date: April 7, 2025
- Anticipated Completion Date: April 2027
- 24-month intersection closure
- Funding Source: FY12 TSPLOST, LMIG, LRA, GDOT, TSPLOST Discretionary




Bids Received & Awaiting Award

Infantry Road and Follow-Me Trail (RFB 24-0040)

PI 0015285

- New road from S. Lumpkin to Fort Benning Road and new trail along Fort Benning Road.
- Bids Received: August 7, 2024
- Low Bid: \$2,439,946.30
- Anticipated Start: 2nd Quarter 2025
- Anticipated Completion: 2nd Quarter 2026

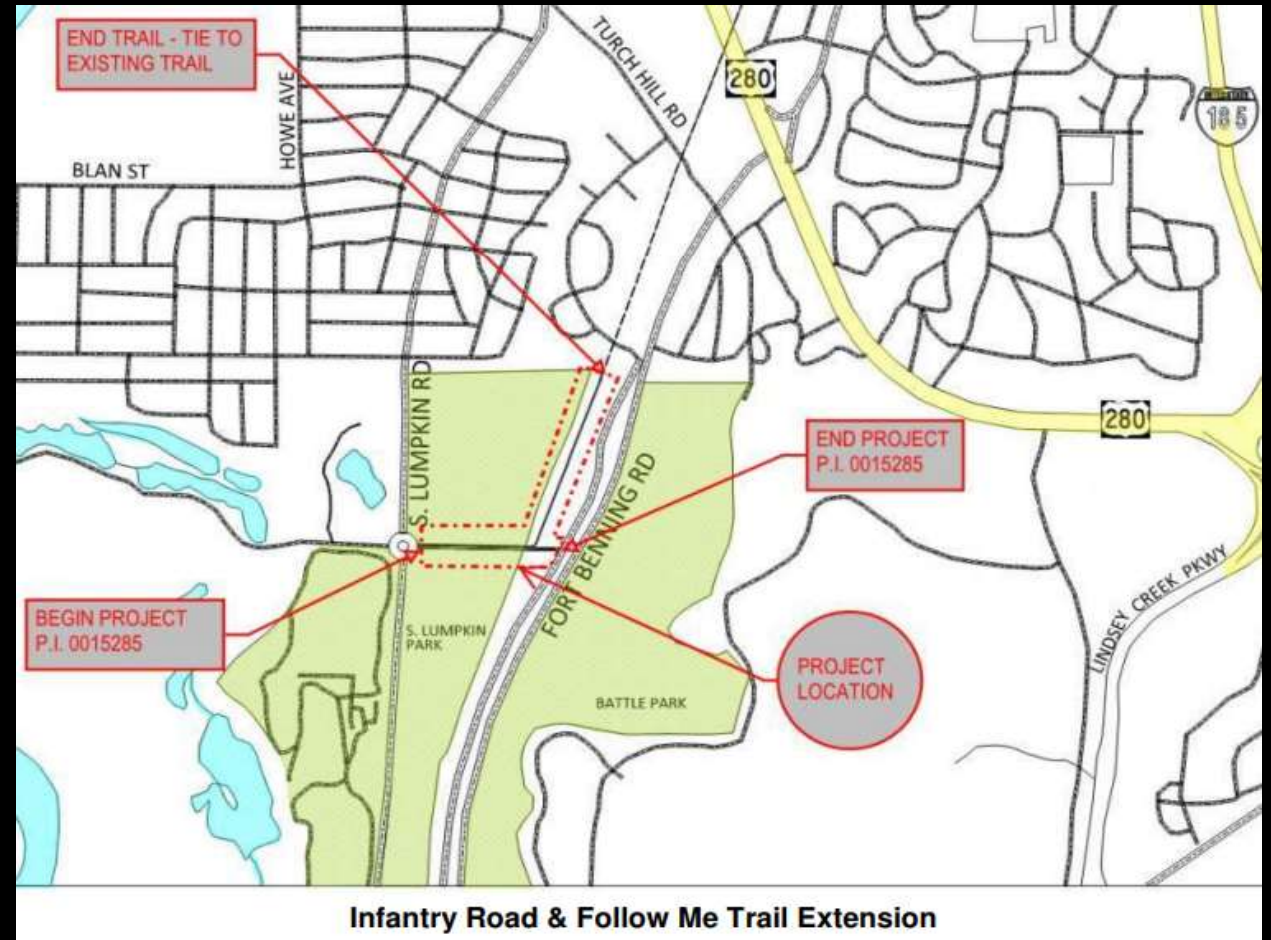

TIA Band 1 Projects

Steam Mill Road

- Road improvements from Buena Vista Road to Pinecrest Drive with pedestrian bridge over I-185 and roundabouts at Dogwood Drive, McCartha Drive and Northstar Drive.
- Est. Design Completion: March 2025
- Est. Cost: \$22.5M to \$26M
- Funding Source: FY22 TSPLOST
- Critical Path: ROW Acquisition (ads running now for 4 straight weeks)



TIA Band 1 Projects (continued)

Whitesville Road

Road widening will start on the north side of the bridge over SR 22/US 80/J R Allen Parkway and will end at the intersection of Williams Road. The design will go from 2 lanes to 3 lanes with intersection improvements or roundabouts with a sidewalk and multiuse trail.

Est. Letting: Spring 2027

PIOH held on February 4, 2025

Funding Source: FY22 TSPLOST

Est. Cost: \$14.3M



TIA Band 1 Projects (continued)

South Lumpkin Road

Road improvements from Victory Drive to the proposed Infantry Road.

Est. Letting: June 2026

PIOH set for March 27, 2025

Funding Source: FY22 TSPLOST

Est. Cost: \$9.6M (3-lane) / \$11.9M (5-lane)



TIA Band 1 Projects (continued)

5th Avenue

- 5th Avenue Multi-use path from 10th St. to 14th St.
- Est. Design Completion: December 2025
- Est. Cost: \$690,000
- Funding Source: FY22 TSPLOST



13th Avenue, 17th St. and Linwood Blvd. Roundabout

- New Roundabout @ 13th, 17th and Linwood.
- Est. Design Completion: December 2025
- Est. Cost: \$6,650,000
- Funding Source: FY22 TSPLOST
- PIOH: January 15, 2025



TIA Band 1 Projects (continued)

- Andrews Road Improvements - (Buena Vista Road to Cusseta Road) - GDOT Administered – Under Design
 - **PIOH: between late April-June 2025 (combined with Brennan Road project)**
- Brennan Road Improvements - (St. Mary's Road to Cusseta Road) - GDOT Administered – Under Design
- University Avenue Road Diet- (Gentian Boulevard to Macon Road) – GDOT Administered – Developing concept report
- Manchester Expy @ Central Church Road Intersection Improvements – GDOT Administered – Final plan package under review

TIA Band 1 Projects (continued)

- Columbus Riverwalk Repaving and Maintenance – (CCG Scoping Project) – CCG Administered – Engineering Department working on bid package
- Buena Vista Road Corridor Improvements – (Spiderweb to Wynnton Road) – GDOT Administered – Draft concept report: late March 2025
- Liberty Theater Block Enhancement – (Streetscape improvements along 8th Avenue)

TIA Band 2 Projects

- Morris Road Improvements - (Buena Vista Road to Forrest Road) - CCG Administered
- Forrest Road Widening - (Macon Road to Railroad) – CCG Administered - Consultant selected
- JR Allen (US 80) @ Schomburg and Blackmon Rd. Intersections - GDOT Administered – Consultant Selected – Letting September 2028
- Second Avenue Improvements - (Talbotton Road to Manchester Expressway) - GDOT Administered – Under Design – Letting April 2028
- Columbus Airport Improvements – CCG Administered – only \$2.5 million will now go to runway

TIA Band 3 Projects

- Manchester Expressway - (County Line Road/Mahaffey Road Interchange) –
GDOT Administered
- Williams Road Widening - (Veterans Road to I-185) - GDOT Administered
- Cusseta Road Widening - (Brown Avenue to Roundabout) - GDOT Administered
- Double Churches Rd. Improvements - (Veterans Parkway to River Road) - CCG
Administered
- Bull Creek Dragonfly Trail Connector – CWW working on sewer and trail rights
- Metra – Multi Band Projects

Additional Projects

- 8 Streets Resurfacing – Z230 – Under Design
- 8th Street Improvements (Front Ave. to Veterans Parkway) – TIA Discretionary – On-call
- Columbus Storm Drain System College Drive Drainage Rehab – On-call
- Wynnton Road Wall Replacement – On-call
- Northstar Drive/Kennedy Street Roundabout – Final plans estimated by June 2025

Additional Projects

- Front Ave - 10th to 11th Street – On-call – Bids due March 21, 2025
- Street Rehabilitation – Broadway 4th to 5th Street – Under Design
- Military Drive – Preliminary Field Plan Review, Let 2027
- Gateway Signage – mock-up recieved

Additional Projects - GDOT

- RR Crossing – 9th Street / Veterans Parkway
- Olgethorpe Bridge – Let early 2028
- Miller Road / Manchester Expressway
Bridge – 50% Complete
- Bradley Park at J. R. Allen Diverging
Diamond – 59% Complete





Concept Only; Subject to Change

Facility Project Update

City Council Meeting
March 11, 2025

Judicial Center Update

Judicial Center Update

- Cast in place concrete activities ongoing
- Structure projected to be complete this summer
- Interior and Exterior framing will start this month
- Project remains on schedule for a Summer 2026 completion



Mar 4th, 2025 - 11:24 AM

OxBlue
part of Hexagon

Judicial Center Progress Photos



2025/03/04 05:49:56

Judicial
Center
Progress
Photos



2025/03/04 05:47:40

Judicial Center Progress Photos



Judicial
Center
Progress
Photos



2025/03/04 05:58:46

Judicial
Center
Progress
Photos



2025/03/04 05:52:55

Synovus Park Update

Synovus Park Update

- Finishes are currently being installed
- Site paving and landscaping is on-going
- Punchlist corrections on-going
- Project remains on schedule for an April 2025 completion







Synovus Park
Progress
Photos



Synovus Park
Progress
Photos



Fire Station #5





Other Projects



City Hall Phase II – Renovations are underway. Estimated completion August 2025.



Fire Stations #4 & #8 – Design activities for renovations have started. Construction will start after completion of FS #5



Fire and EMS Administration – Notice to Proceed issued to contractor. Estimated completion October 2025.

Other Projects



Oxbow Creek Clubhouse
– Under design;
Anticipate construction
to start this summer.

QUESTIONS
