



Concept Only; Subject to Change

Project Update

City Council Meeting
July 30, 2024

Judicial Center Update

Judicial Center Update

- Deep Foundation work ongoing
- Cast in place concrete activities have started
- 1st tower crane will be erected in August; 2nd tower crane will be erected in September
- Project remains on schedule for a Summer 2026 completion



Judicial Center Progress Photos




Judicial
Center
Progress
Photos



Synovus Park Update

Synovus Park Update

- Cast in Place concrete at the Patron Building is complete
- Installation of roofing and exterior walls at Patron Building in ongoing
- Structural steel erection for clubhouse has started
- New dugout installation is ongoing
- Project remains on schedule for a April 2025 completion

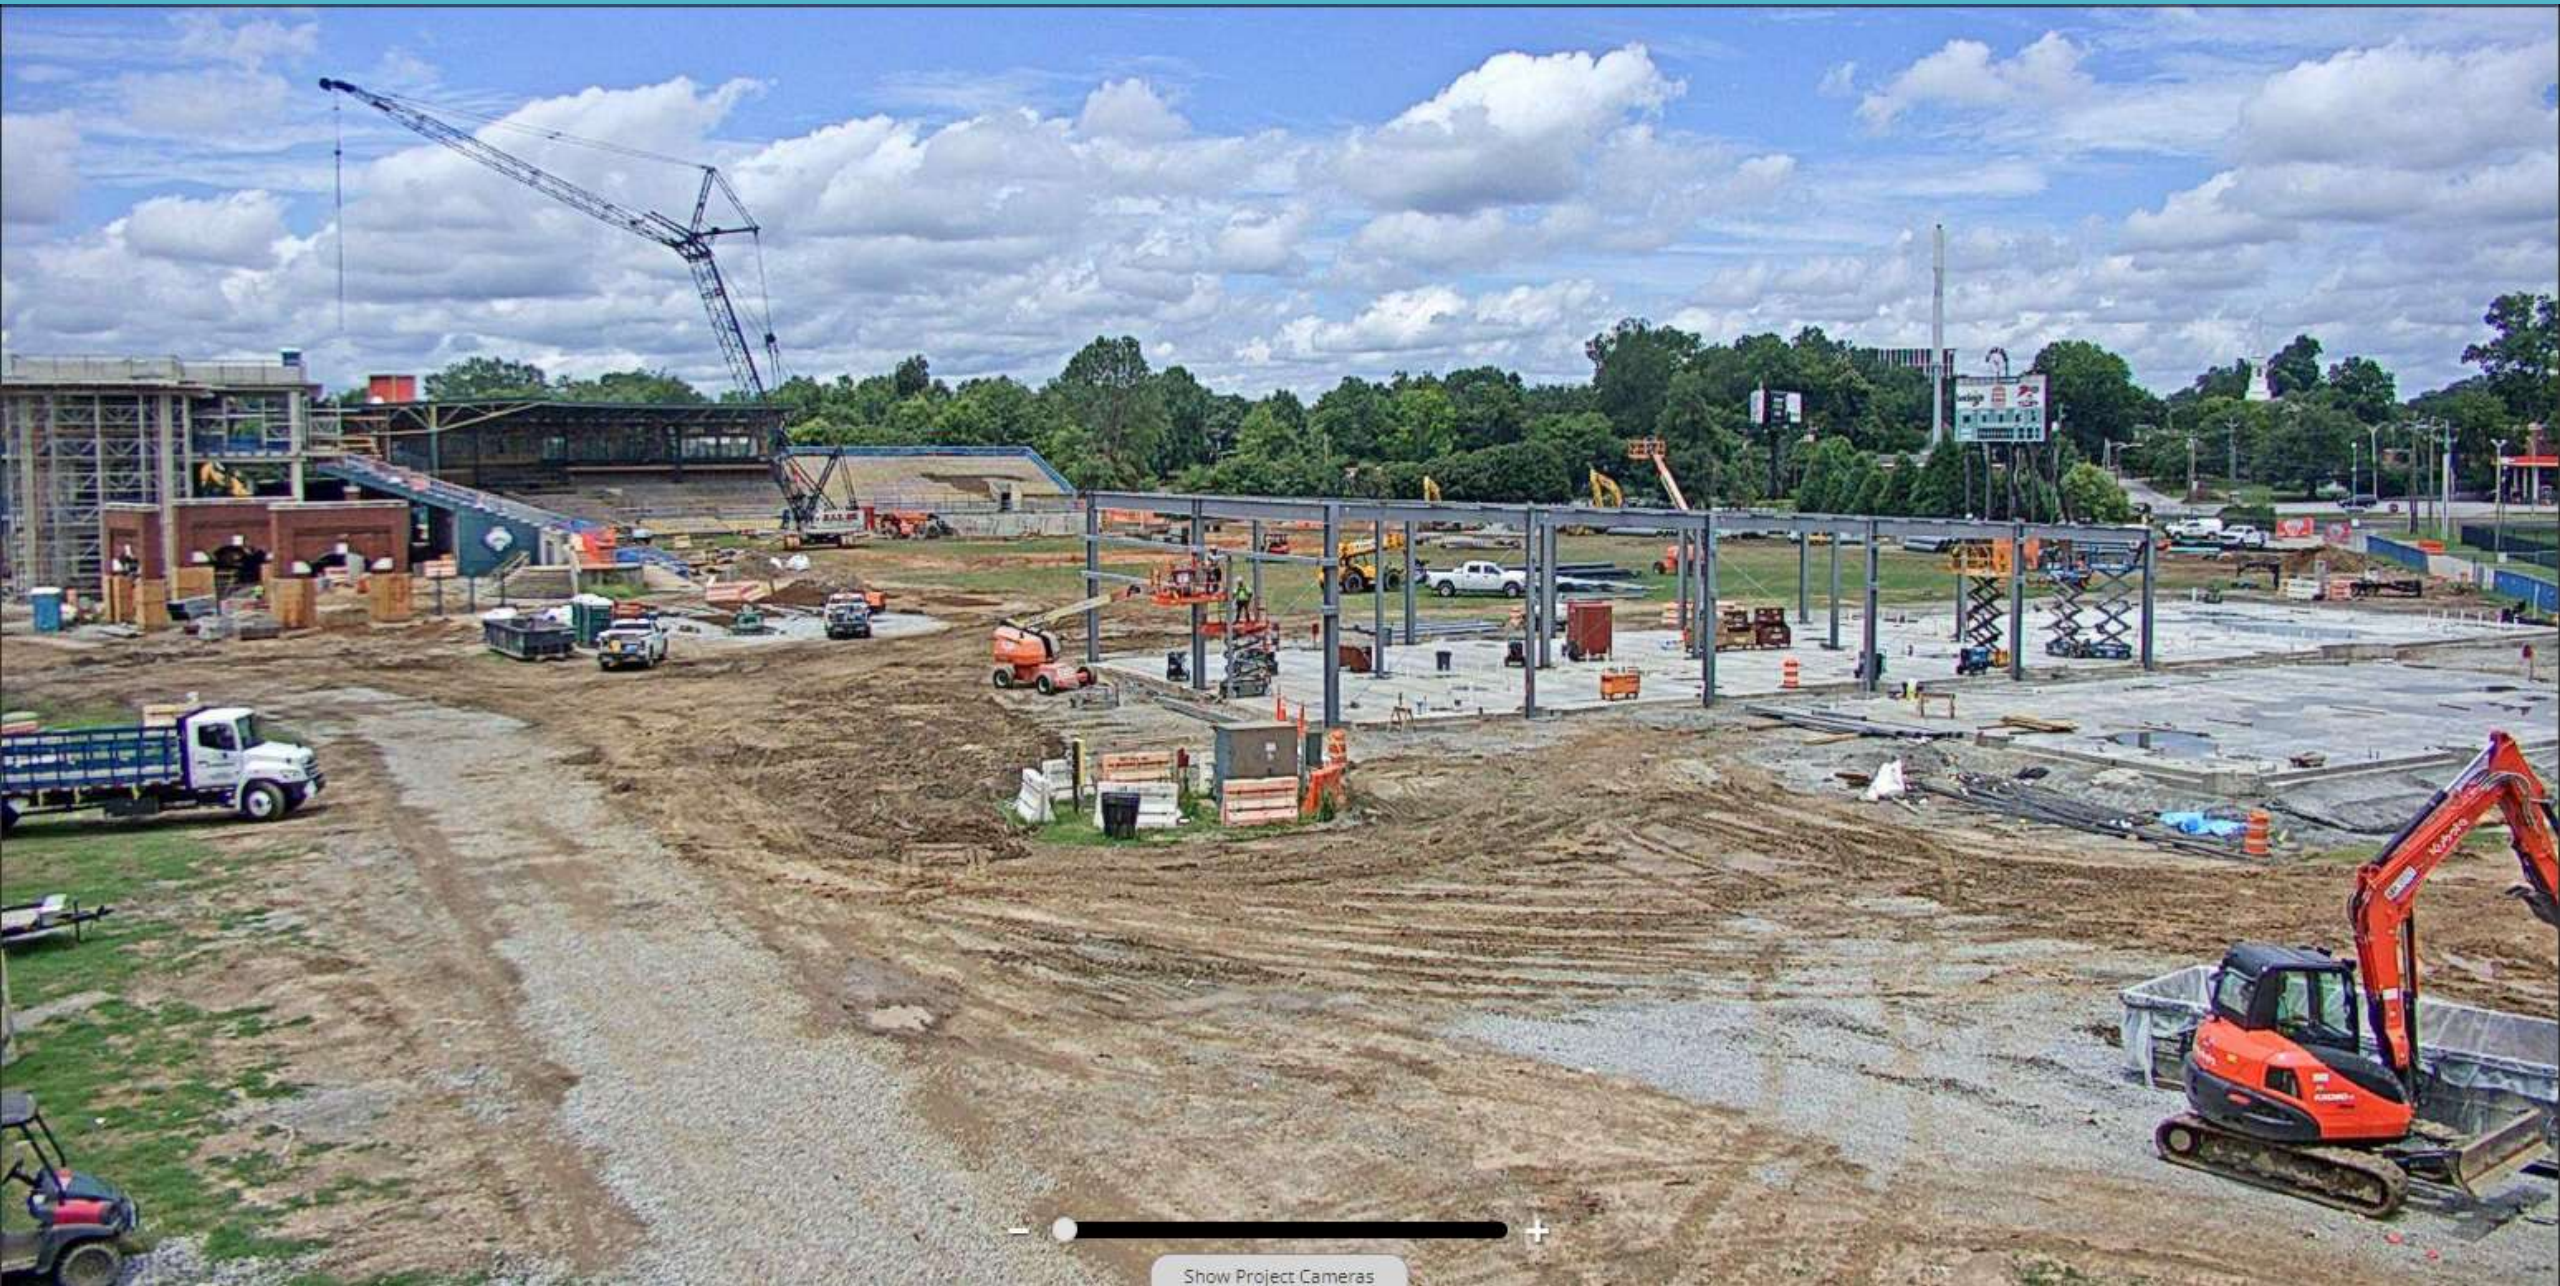

Show Project Cameras



Show Project Cameras



Sheriff's Office Administration Building Update

Sheriff's Office Administration Building Update

- Installation of finishes is ongoing. Final inspections are scheduled for early August.
- Construction of garage addition is ongoing.
- Furniture installation began July 22nd.
- Project scheduled to be complete in September 2024.

Sheriff's
Office
Progress
Photos



Sheriff's
Office
Progress
Photos



Sheriff's
Office
Progress
Photos



Sheriff's
Office
Progress
Photos



Sheriff's
Office
Progress
Photos



Sheriff's
Office
Progress
Photos



Other Projects



City Hall Phase II – Renovations will start in November 2024. Anticipated completion is Summer 2025



Fire Station #5 – Design work is 85% complete. Construction anticipated to start in October 2024.



Trade Center Parking Garage – RFP for design-build services is currently advertised.

QUESTIONS
