




ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	September 2025										October	
									18	23	28	2	7	12	17	22	27			
1			Contracts Executed	7 days	Wed 5/7/25	Thu 5/15/25														
2			Submittal Review	10 days	Fri 5/16/25	Thu 5/29/25	1													
3			Procurement	45 days	Fri 5/30/25	Thu 7/31/25	2													
4			Demo	10 days	Tue 5/20/25	Mon 6/2/25														
5			Demo designated interior spaces (walls, ceilings, flooring, etc)	10 days	Tue 5/20/25	Mon 6/2/25	2SS+2 days													
6			Interior Framing	23 days	Mon 7/14/25	Wed 8/13/25														
7			Framing of New interior walls	6 days	Mon 7/14/25	Mon 7/21/25														
8			Rough Carpentry	3 days	Tue 7/22/25	Thu 7/24/25	7													
9			Masonry Work	8 days	Mon 8/4/25	Wed 8/13/25														
10			Set HM Door Frames	3 days	Mon 8/4/25	Wed 8/6/25	3SS+25 days													
11			MEP Rough-Ins	15 days	Tue 7/22/25	Mon 8/11/25	7													
12			HVAC Demo	5 days	Tue 6/3/25	Mon 6/9/25	5													
13			Fab and Deliver Duct	10 days	Tue 6/10/25	Mon 6/23/25	12													
14			Install Duct, Piping, and Equipment	30 days	Tue 6/24/25	Mon 8/4/25	13													
15			Enclosure & Exterior Work	78 days	Fri 5/30/25	Tue 9/16/25														
16			Roof Material Procurement	30 days	Fri 5/30/25	Thu 7/10/25	2													
17			Roof Removal	10 days	Fri 7/11/25	Thu 7/24/25	16													
18			Soffit / Fascia Removal	10 days	Fri 7/11/25	Thu 7/24/25	17SS													
19			Roof Blocking	5 days	Fri 7/25/25	Thu 7/31/25	18													
20			Soffit Framing Repair as Necessary	5 days	Fri 7/25/25	Thu 7/31/25	18													
21			New Fully Adhered Roof	20 days	Fri 8/1/25	Thu 8/28/25	19													
22			New Soffit / Fascia Instal	7 days	Fri 9/5/25	Mon 9/15/25	21SS+25 days													
23			Gutters & Downspouts	5 days	Wed 9/10/25	Tue 9/16/25	22SS+3 days													
24			Interior Buildout	31 days	Mon 8/11/25	Mon 9/22/25														
25			Drywall installation / tap	8 days	Mon 8/11/25	Wed 8/20/25														
26			Paint	3 days	Thu 8/21/25	Mon 8/25/25	25													
27			Casework / countertop	4 days	Tue 8/26/25	Fri 8/29/25	26													
28			Install Ceiling Grid	3 days	Tue 9/16/25	Thu 9/18/25	36													
29			Install ceiling tiles	2 days	Fri 9/19/25	Mon 9/22/25	28													
30			Flooring/Tile install	8 days	Mon 8/25/25	Wed 9/3/25	26SS+2 days													
31			Wood Doors	4 days	Thu 9/4/25	Tue 9/9/25	30													
32			Vestibule	2 days	Thu 8/28/25	Fri 8/29/25														
33			Specialties	2 days	Wed 9/10/25	Thu 9/11/25	31													


Project: Dodgeville Admin Ph 2
Date: Thu 8/28/25

Task

Split

Milestone

Summary









Project Summary

Inactive Task

Inactive Milestone

Inactive Summary









Manual Task

Duration-only

Manual Summary Rollup

Manual Summary









Start-only

Finish-only

External Tasks

External Milestone









Deadline

Progress


Manual Progress









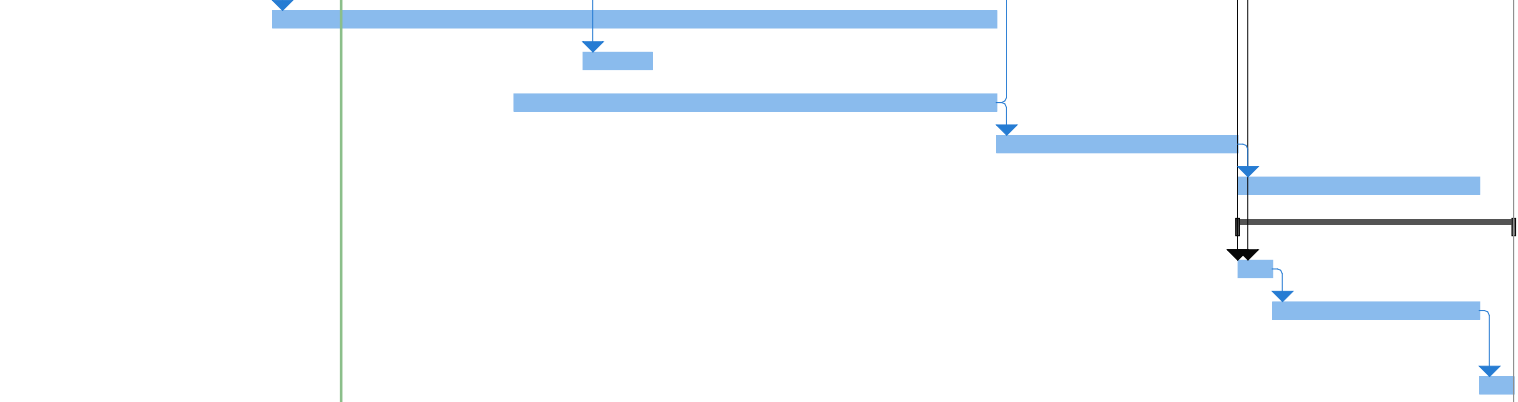

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	182328September 20252127October 2025											
34			Final MEP Installation	15 days	Tue 8/26/25	Mon 9/15/25	26													
35			Plumbing Fixtures	2 days	Thu 9/4/25	Fri 9/5/25	30													
36			Damaged Piping Resolution	10 days	Tue 9/2/25	Mon 9/15/25														
37			Startup/Commissioning	5 days	Tue 9/16/25	Mon 9/22/25	36													
38			Test & Balance	5 days	Tue 9/23/25	Mon 9/29/25	37													
39			Final Inspection & Handov	6 days	Tue 9/23/25	Tue 9/30/25														
40			Punch list walk through	1 day	Tue 9/23/25	Tue 9/23/25	6,15,24													
41			Final corrections / touch ups	4 days	Wed 9/24/25	Mon 9/29/25	40													
42			Final cleaning / occupan	1 day	Tue 9/30/25	Tue 9/30/25	41													

Project: Dodgeville Admin Ph 2
Date: Thu 8/28/25

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
