




ID	Task Name	Duration	Start	Finish																			
					Aug 3, '25			Sep 7, '25			Oct 12, '25			Nov 16, '25			Dec 21, '25			Jan 25, '26			
					T	F	S	S	M	T	W	T	F	S	S	M	T	W					
44	MEP In-Wall Rough-In	9.2 wks	Thu 5/21/26	Wed 8/5/26																			
45	MEP Overhead Rough-In	6 wks	Thu 5/21/26	Wed 9/2/26																			
46	Window abatement	1 wk	Mon 7/6/26	Fri 7/10/26																			
47	Sheetrock	2 wks	Tue 6/30/26	Tue 9/8/26																			
48	Tape, Float and Paint	4 wks	Thu 7/16/26	Tue 9/22/26																			
49	ACT Ceiling Grid Install	1 wk	Tue 9/22/26	Tue 9/29/26																			
50	MEP, AV, IT FS, FA Trim Out	5 wks	Tue 9/15/26	Tue 10/20/26																			
51	Storefront	2 wks	Mon 8/17/26	Fri 8/28/26																			
52	MEP Start-Up	5 days	Thu 9/3/26	Wed 9/9/26																			
53	Doors and Hardware	12 days	Tue 9/29/26	Thu 10/15/26																			
54	Millwork	3 wks	Thu 9/10/26	Wed 9/30/26																			
55	Tiling	1 wk	Thu 9/10/26	Wed 9/16/26																			
56	Specialties	1 wk	Tue 9/22/26	Tue 9/29/26																			
57	Commissioning	1 day	Tue 9/22/26	Tue 9/22/26																			
58	Life Safety and Fire Alarm Testing	1 day	Wed 9/30/26	Wed 9/30/26																			
59	Flooring	4 wks	Wed 9/23/26	Tue 10/20/26																			
60	QA Pre-Punchlist	5 days	Tue 10/6/26	Mon 10/12/26																			
61	Exterior Windows	3 wks	Mon 12/7/26	Fri 12/25/26																			
62	Window Shades & Millwork	1 wk	Mon 12/28/26	Fri 1/1/27																			
63	Final Clean	2 days	Mon 1/4/27	Tue 1/5/27																			
64	Site	243 days	Fri 11/14/25	Tue 10/20/26																			
65	Make Safe	9 days	Fri 11/14/25	Wed 11/26/25																			
66	Site Demolition	5 days	Tue 11/25/25	Mon 12/1/25																			
67	Clear & Grub Site	5 days	Fri 11/21/25	Thu 11/27/25																			
68	Earthwork	5 wks	Mon 12/8/25	Fri 1/9/26																			
69	Site Utilities & Underground MEP	24.6 wks	Mon 2/23/26	Wed 8/12/26																			
70	Light Pole Bases	2 wks	Mon 3/30/26	Fri 4/10/26																			
71	Subgrade Prep & Parking Lot Subbase	3.2 wks	Thu 8/13/26	Thu 9/3/26																			
72	Concrete Curbs & Gutters	3 wks	Fri 9/4/26	Thu 9/24/26																			
73	Concrete Flatwork	3 wks	Fri 9/4/26	Thu 9/24/26																			
74	Landscaping	4 wks	Wed 9/23/26	Tue 10/20/26																			
75	Permeable Paver System	4 wks	Mon 9/7/26	Fri 10/2/26																			
76	Asphalt Paving	3 wks	Fri 8/21/26	Thu 9/10/26																			
77	Pavement Striping	1 wk	Mon 10/5/26	Fri 10/9/26																			
78	Exterior Improvements	3 wks	Mon 9/21/26	Fri 10/9/26																			
79	Site Furnishings	2 wks	Wed 9/30/26	Tue 10/13/26																			
Project: Dripping Springs Stephen Date: Tue 8/11/26		Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline													
		Split		External Tasks		Inactive Summary		Manual Summary		Progress													
		Milestone		External Milestone		Manual Task		Start-only															
		Summary		Inactive Task		Duration-only		Finish-only															
Page 2																							

ID	Task Name	Duration	Start	Finish	Aug 3, '25 T F S Sep 7, '25 S M Oct 12, '25 T W T Nov 16, '25 F S Dec 21, '25 S M Jan 25, '26 T W
80	QA Pre-Punchlist	1 wk	Wed 10/14/26	Tue 10/20/26	
81	Final Clean	3 days	Fri 10/16/26	Tue 10/20/26	
82	Substantial Completion	0 days	Tue 10/20/26	Tue 10/20/26	
83	Owner Punchlist	4 wks	Wed 10/21/26	Tue 11/17/26	
84	Closeout Documents	45 days	Wed 10/21/26	Tue 12/22/26	
85	Project Closed	1 day	Wed 1/20/27	Wed 1/20/27	

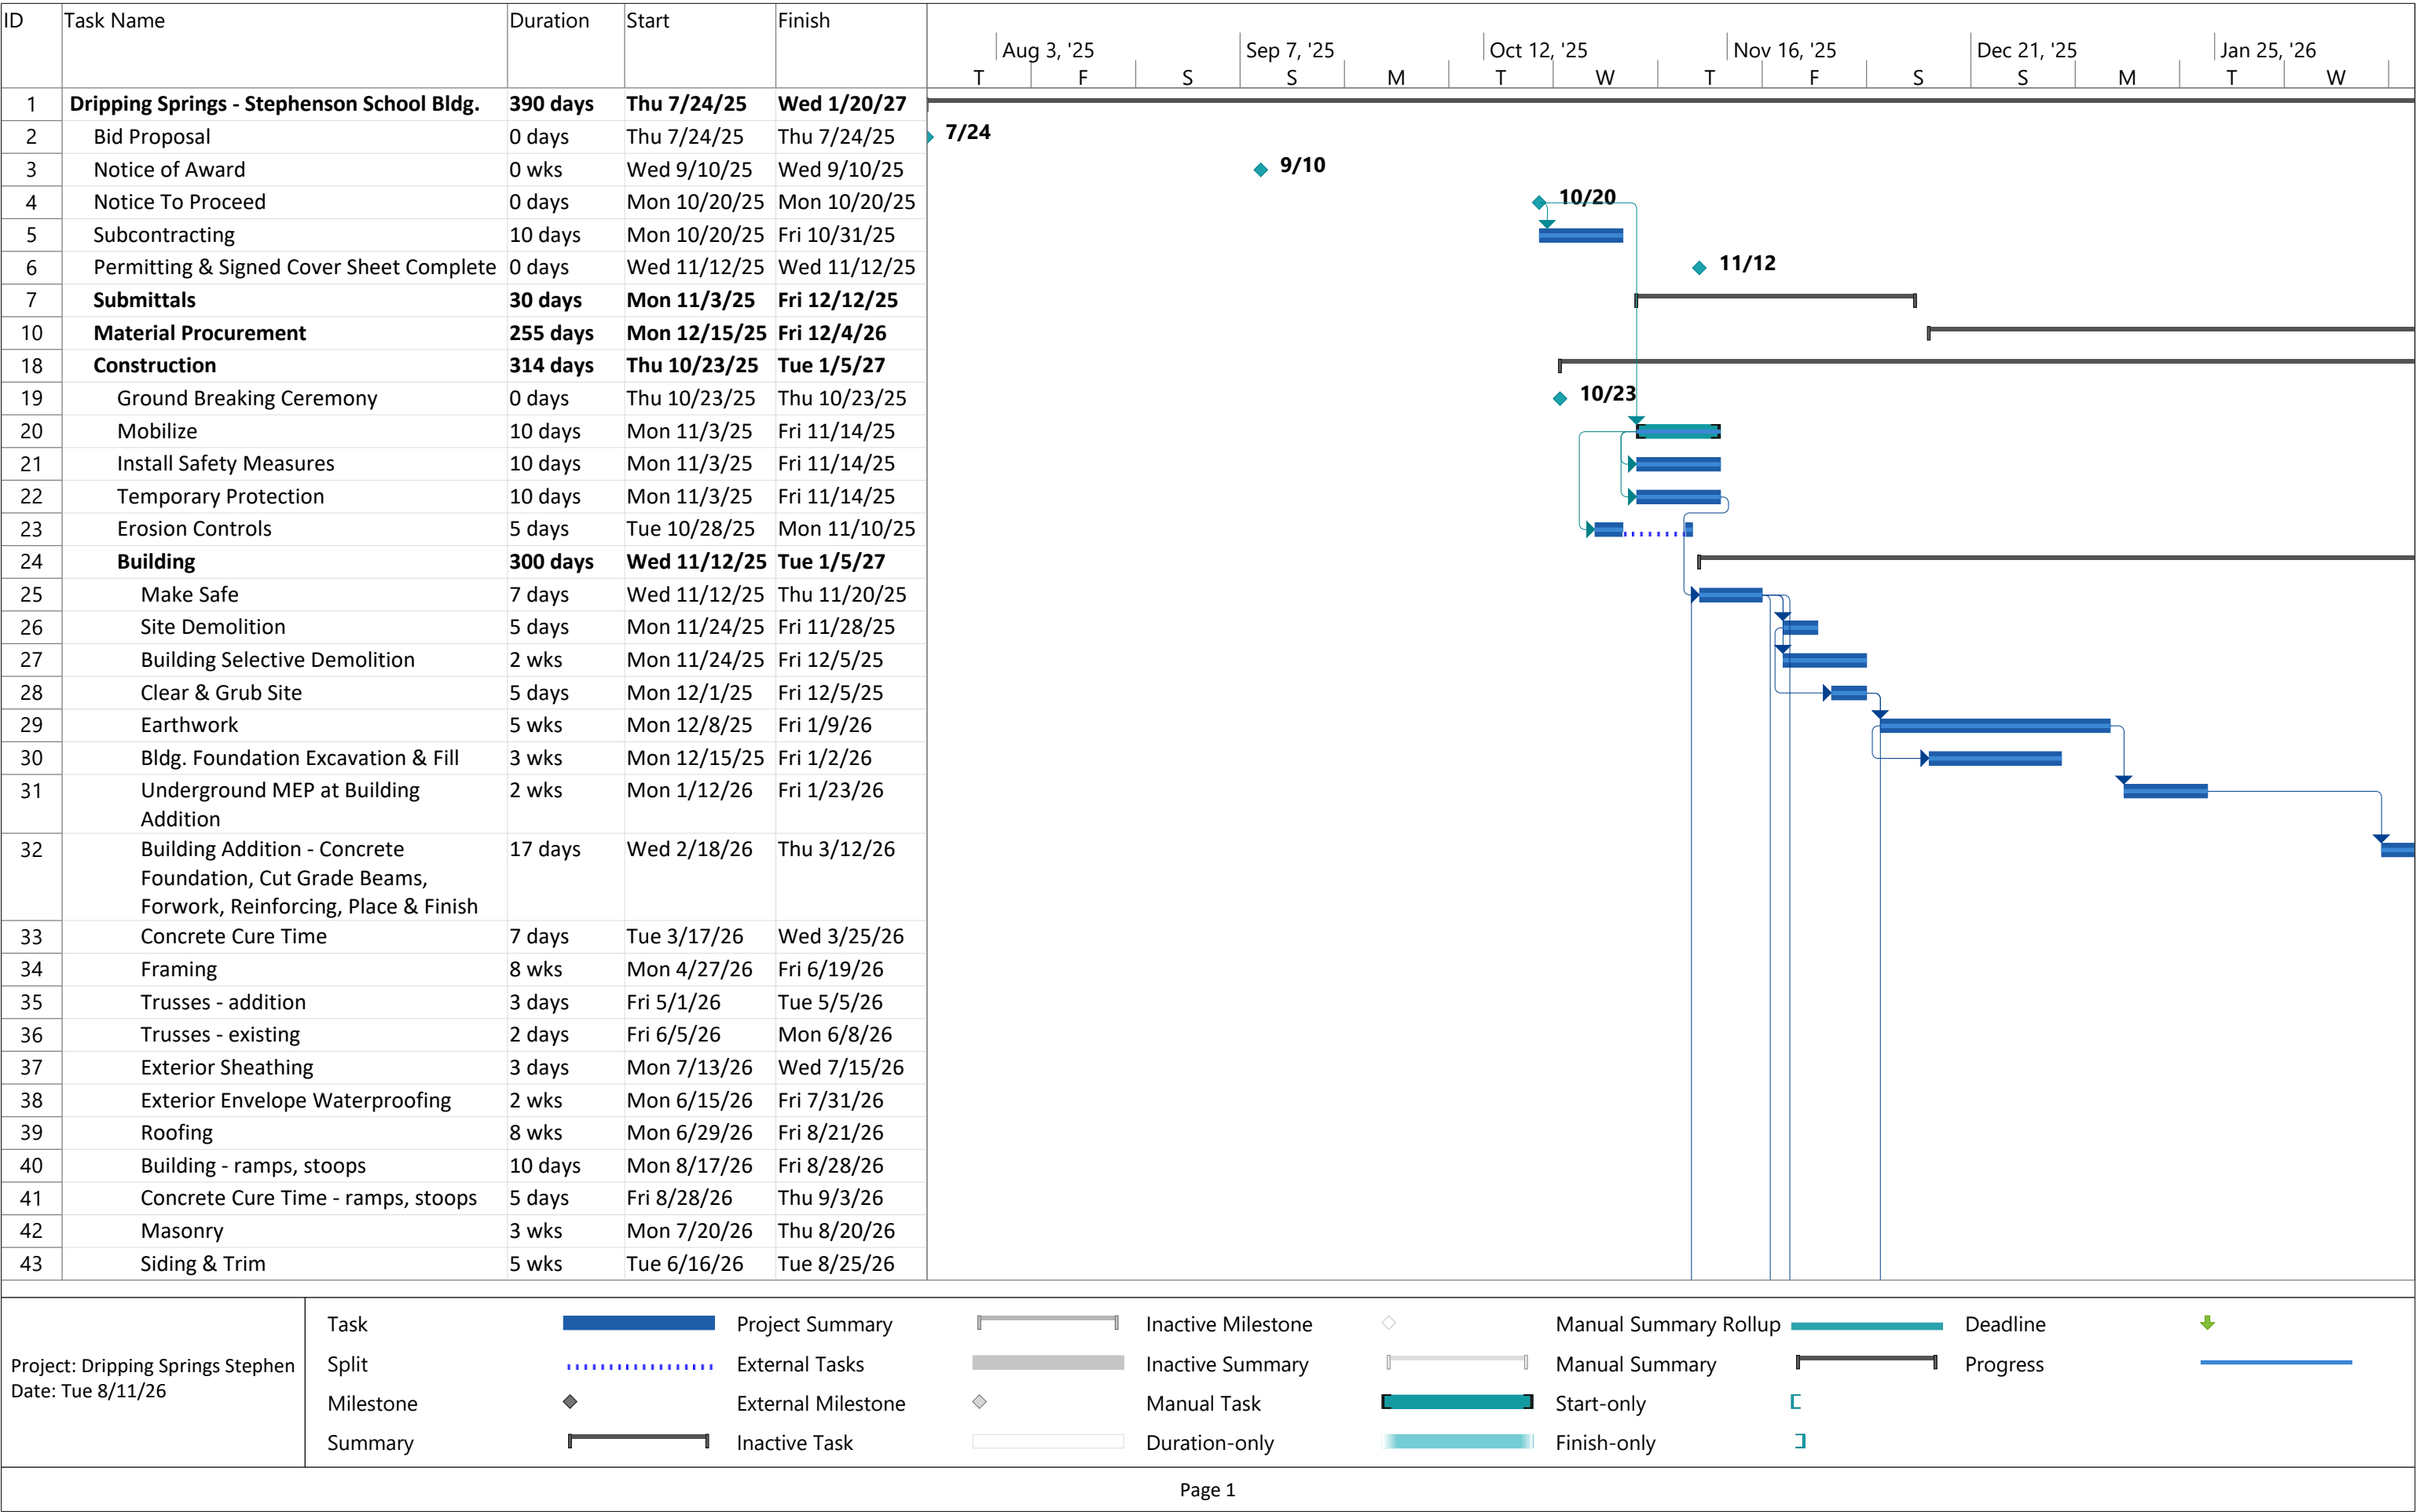

Project: Dripping Springs Stephen
Date: Tue 8/11/26

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

