



**GRAND RAPIDS
PUBLIC UTILITIES**


Service is Our Nature

500 SE Fourth Street • Grand Rapids, Minnesota 55744


WASTEWATER UTILITY MONTHLY REPORT March 2024 Commission Meeting

Wastewater Operations

The Wastewater Treatment Plant (WWTP) met all National Pollutant Discharge Elimination System (NPDES) permit requirements last month. We treated 147 million gallons of water removing 99.8% of the Total Suspended Solids (TSS) and 99.7% Biochemical Oxygen Demand (cBOD).

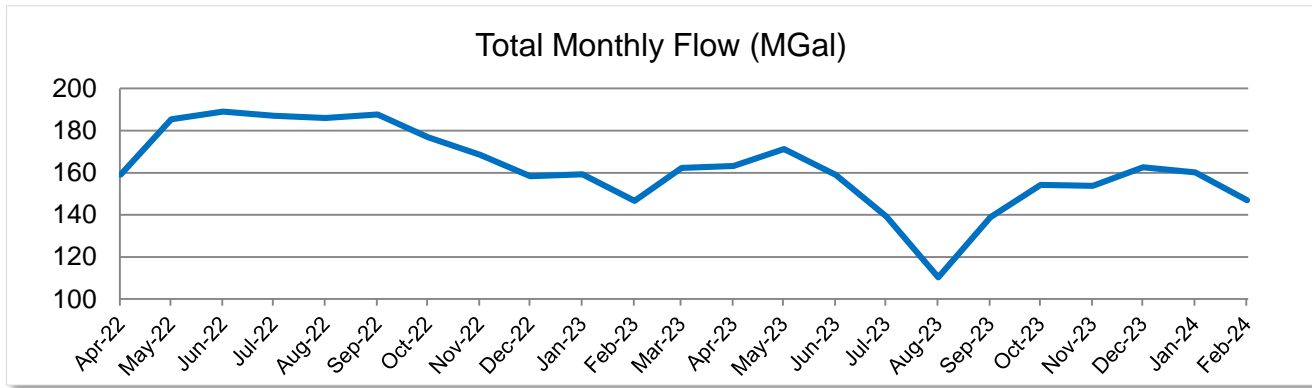

	Design Limits (monthly AVG)	Actual Results
<u>Primary Plant</u>		
Flow (MGD)	13.25	3.8
TSS (Tons/day)	162	18.3
TSS Peak (Tons/Day)	284	47.8


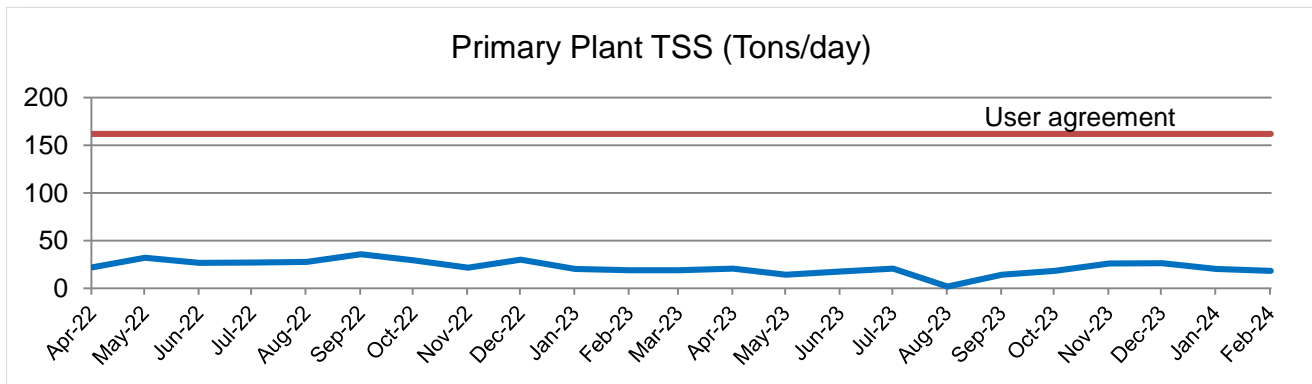


Design Limits
(monthly AVG)

Actual Results

Secondary Plant

Flow (MGD)	15.25	5.1
cBOD (lbs/Day)	41,300	23,134
Peak cBOD (lbs/Day)	57,350	33,694
Zinc-weekly (ug/L)	418	260
% GRPUC		29.7%

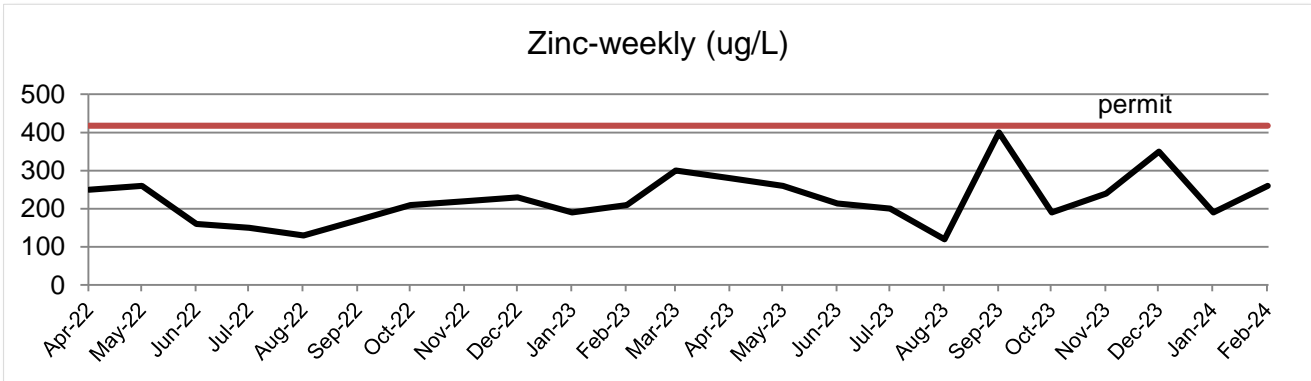
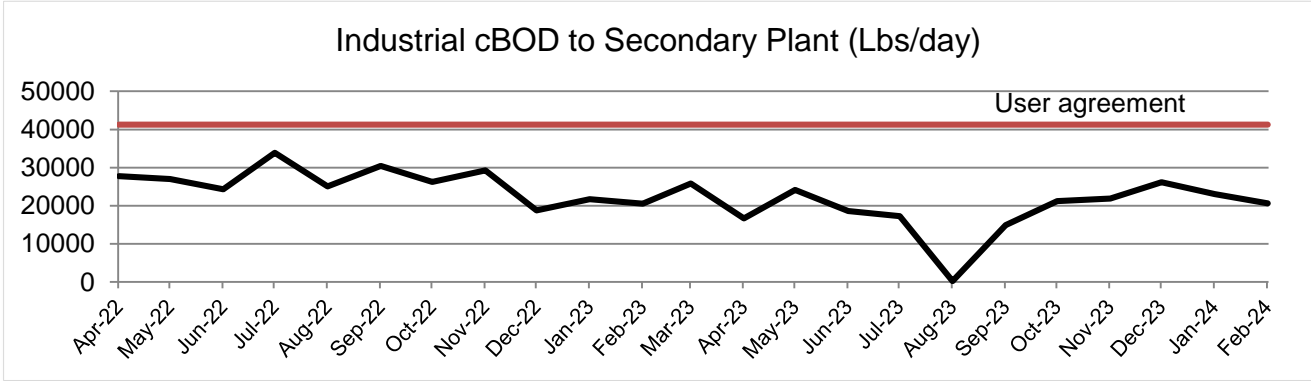


Permit Limits
(monthly AVG)

Actual Results


Effluent

TSS (mg/L) – monthly average	30	1.9
cBOD (mg/L) – monthly average	25	2.1
Dissolved Oxygen (mg/L)	>1.0	9.3

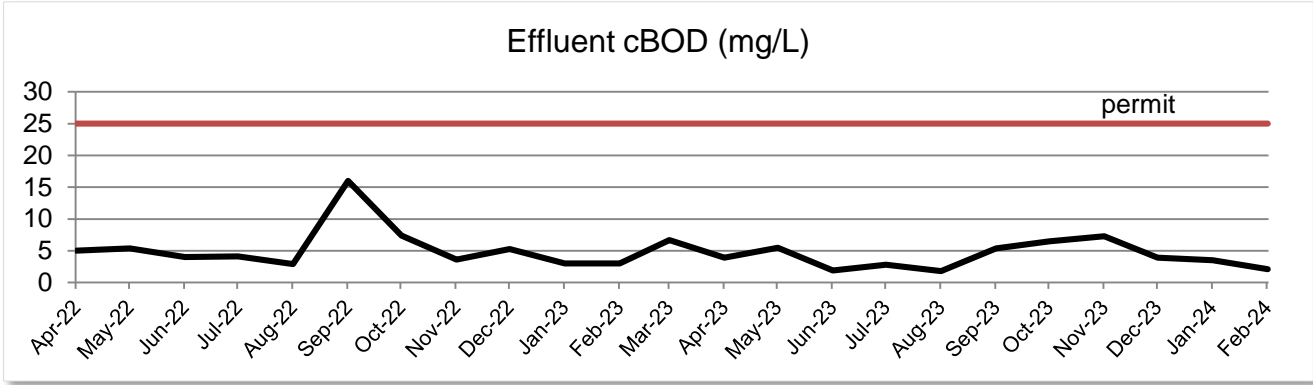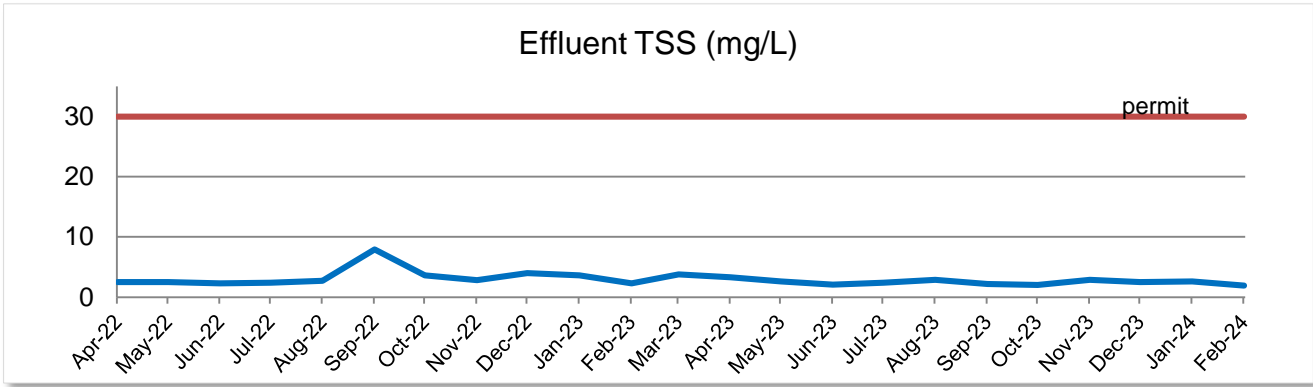

Sludge Landfill Operations

- 0.42 million gallons of leachate were hauled last month which is abnormally high.
- 2928 cubic yards of sludge solids were hauled to the landfill

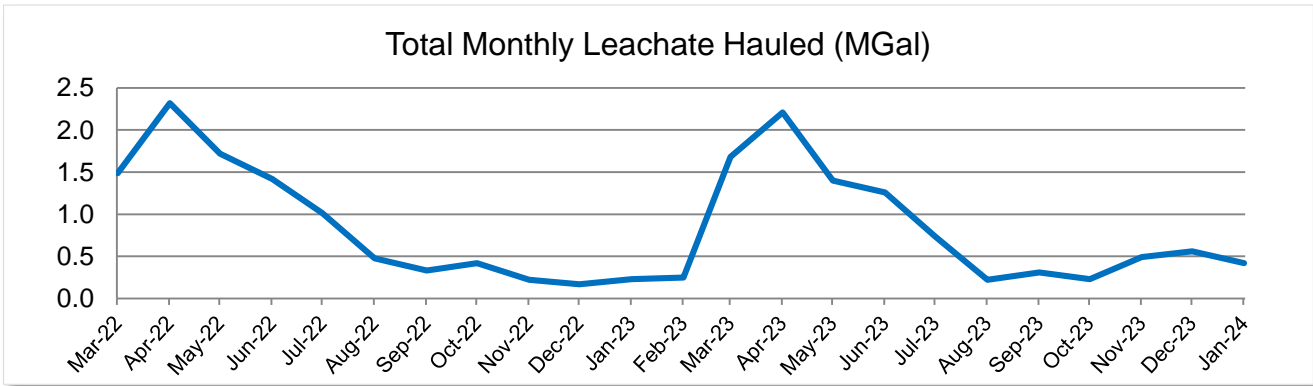

Capital and Operations Project Summary

COMMISSION REPORT CONTENTS									
Agency Lead	Dept	Proj Desc	Proj #	Budget	Amount Spent	Percent Spent (calc'd)	Percent Complet	Status	Noted Issues / Highlights
City	WWC	3rd Ave NE, 7th St NE	WWCO2002	\$270,000	\$0	0%	0%	Not Started	
GRPU	WWC	Jetting		\$150,000	\$0	0%	0%	Not Started	
GRPU	WWC	Lift Station 3 Controls Update	WWCO2403	\$25,000	\$0	0%	0%	Not Started	
GRPU	WWC	Lift Station Pumps	WWCO2005	\$35,000	\$0	0%	0%	Not Started	
GRPU	WWT	Septic Hauler Dump Station	WWDO2403	\$553,500	\$0	0%	2%	Not Started	
GRPU	WWT	Trash Compactor	WWDO2302	\$90,000	\$0	0%	5%	Not Started	

Status Definitions

- Not Started - no human or financial resources utilized
- In Progress - time or money spent on the project
- In Service - operational but final close out needed
- Completed - done and closed out
- On Hold - waiting on some type of significant action
