

**VILLAGE BOARD MEETING**

**From:** Chad Pelishek, Village Manager

**VILLAGE OF HARRISON**

**Meeting Date:** 9/30/2025

**Title:** Public Works/ Engineering/Parks/Trails Report


**Issue:** None

**Background and Additional Information:**

1. DPW staff completed removal of topsoil stockpile on Lot 6 in Crossroads Business Park.
2. DPW staff completed excavation for new playground at Harrison Athletic Complex (see attached photo)
3. DPW and Northeast Asphalt completed road asphalt wedging and patches around Village.
4. Completed removal of Buckthorn from Darboy Park Forest and spreading of wood chips from the approximate 270 ash trees removed from the forest.
5. Completed backfilling of the Farmers Field Shelter. Plumber will install plumbing on 10/27 and then slab will be poured by students and foundation contractor around 10/31. As of November 1, framing of the building will occur with the students.
6. Tree trimming of trees over Fire Lanes completed
7. Brush Pickups
8. Grinding preparation at Yard Waste Site.
9. Finished seeding and mulching at Rennwood Park.
10. Steel erection of the new DPW garage bays to begin 10/22. New garage bays should be turned over to the Village as of 1/30/2026.



New Playground Install at HAA

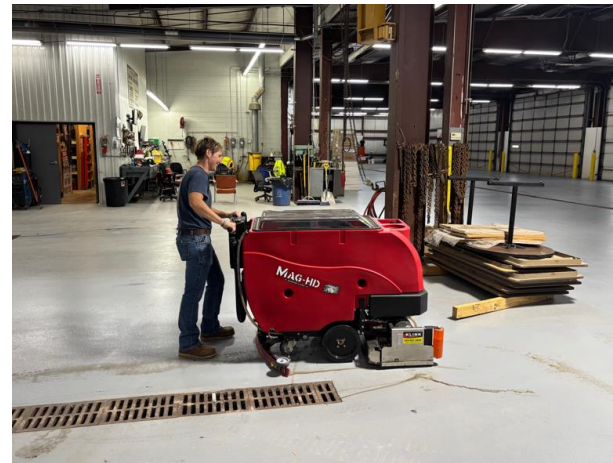

Floor Scrubber in Action



New DPW breakroom



New DPW supervisor workstations



Dirty vs. Clean floor from floor scrubber

---

**Budget Impacts:** None

---

**Recommended Action:** None

**Attachments:**
