

# Homer Public Safety Building

Grubstake Avenue Homer, Alaska 99603



Date Sat 01/04/2020

Job # 1809-2

Prepared By Carl Brinkerhoff



## Weather

6:00 AM	12:00 PM	4:00 PM
<p><b>12°</b> </p> <p><b>Clear</b></p> <p>Wind: 8 MPH   Precipitation: .01"   Humidity: 72%</p>	<p><b>14°</b> </p> <p><b>Clear</b></p> <p>Wind: 7 MPH   Precipitation: .01"   Humidity: 69%</p>	<p><b>13°</b> </p> <p><b>Clear</b></p> <p>Wind: 7 MPH   Precipitation: .01"   Humidity: 71%</p>

## Work Logs

Name	Description	Quantity	Hours	Hours To Date
Accel Fire		0	0	70
Alasco Insulation		0	0	91
Carl's Drywall & Paint	Finish hanging Sheetrock at janitors, mail copy room. Hung Sheetrock at walls control room. <small>Carl Brinkerhoff   01/04/20   04:55PM</small>	2	8	72
Consolidated Roofing		0	0	477
Duct or Sheet Metal		0	0	107
East Road Services		0	0	944
Eayrs Plumbing		0	0	689
Puffin Electric	Onsite working mainly lower level walls. <small>Carl Brinkerhoff   01/04/20   04:56PM</small>	1	7	1176.5
Tod Sharp, Ron Frazier, Tanner Stengel, Ryan Fox, Jim Pollock	Supervision, coordination and documentation. Continued framing walls on top of CMU at cells. Continued work associated with door frame repair. Stocked additional Sheetrock in rooms for hangers. Installed new oil pressure sensor in fork lift. Installed new pump in Cornerstone dehumidifier. Clean up. <small>Carl Brinkerhoff   01/04/20   04:59PM</small>	4	8	112
<b>Total</b>		<b>7</b>	<b>55</b>	<b>12177</b>

## Time Cards No entry

General Notes

- 1. Confirmed abuse rock is in town at Spenard. Set up Monday delivery

Carl Brinkerhoff | 01/04/20 | 05:02PM

Site Safety Observations

- 1. Site safety protocols were observed onsite today.

Carl Brinkerhoff | 01/04/20 | 05:03PM

Quality Control Observations

- 1. All materials and workmanship performed onsite today met or exceeded project specifications.

Carl Brinkerhoff | 01/04/20 | 05:03PM



Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Exterior door frames, exterior doors and hardware, both types siding. Lower level walls waiting on plumbers to rough in and get showers in locker rooms.
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	All terrain scissor lift.

Carl Brinkerhoff | 01/04/20 | 05:01PM

Carl Brinkerhoff | 01/04/20 | 05:01PM

Attachments

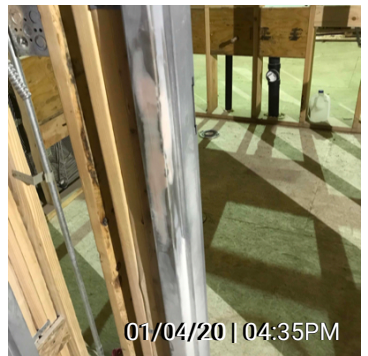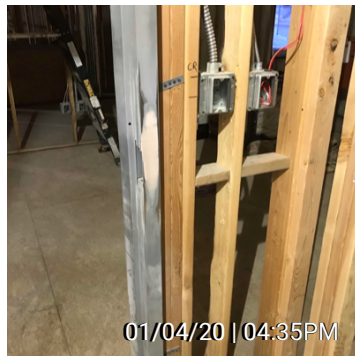



A handwritten signature in black ink, reading 'Carl Brinkerhoff'. The signature is written in a cursive style and is positioned above a horizontal line.

I, Carl Brinkerhoff, have reviewed and completed this report.

Carl Brinkerhoff | 01/04/20 | 05:03PM

# SUBCONTRACTOR REPORTS



Sat 01/04/2020

Homer Public Safety Building: Grubstake Avenue Homer, Alaska 99603

Name	Description	Quantity	Hours	Hours To Date
1. Puffin Electric	No Entry	0	0.0	0.0
2. Eayrs Plumbing and Mechanical	No Entry	0	0.0	0.0
3. PEI	No Entry	0	0.0	280.0
<b>Subtotal</b>		0	0	280.0
<b>Grand Total (Includes Cornerstone General Contractors Work Log Total)</b>		7	55	12457.0
