

### **CIP Project Update** June 17, 2024



## **CIP Projects Update Commitment**

#### Cadence

- Spring Upcoming fiscal year budget review and CIP project's status as well as a budget plan
- Fall Check in for summer project wrap ups, look ahead for Winter planning/design phases for future projects
- Mid Winter Design and planning focused for new projects in the Summer

### Content

- Scope Adjustments
  - Staff will identify any decreases in scope to allow for council input for reincorporation
  - Any significant scope expansions approved by council in the last quarter will be highlighted while any scope additions under the cost threshold (<\$50k) will also be noted for transparency
- Phase and Schedule Updates
  - Project phases: Concept4Design4Bid/Preconstruction 4Construction4Complete
  - Focus on community impacts for city public resources closures/openings (i.e., parks, streets, recreation)
  - Any schedule updates impacting budget
- Financial Status
  - Budgetary info will be brief and concise but special attention will be paid to any budgets that are believed to be at risk of substantial overages or savings



### **Main Street Rehabilitation**

- Phase CONSTRUCTION
  Schedule On track for cl
  - Schedule On track for completion of scope from River St through 5th St Intersections this Summer, 6th to 10th Spring 2025
    - Budget
      - Road construction has been identified to exceed ITD's budget, discussions with ITD on extending expenses into Spring underway. Final cost estimates pending completion in June
      - Contractor prices for the full pedestrian realm being finalized, full budget review planned for Council in July



#### **Forest Service Park**

- **Phase** CONCEPT Three current proposed concepts for park path forward
  - Long-Term Housing viable long term solutions for City employees or community members (depending on scope)
  - Sun Valley Museum of Art After School Programming, Public Programming/Community meetings, Music/Art/Literature Event Space, Artist-in-Residence site
  - Short-term Displaced Small Business Refuge landing space for small businesses who have been displaced by Ketchum core development projects
  - **Schedule** Preservation repairs (roof & siding) slated for completion Fall 2024
  - Budget Pending concept(s) direction from Council



影

## **CIP Project List and Status**

#### **Town Square Renovations**

- Phase CONCEPT Three current proposed concept levels to be presented
- Schedule Starbucks lease expires November 2026
- **Budget** Pending direction from Council

#### **Powerline Undergrounding Master Plan**

- **Phase** CONCEPT Working to get mapping from ID Power
- Schedule Complete Master Plan delivery expected winter of 2025
  - Budget TBD




#### **Pavement Management Program**

- **Phase** DESIGN pavement analysis ~70% complete Presentation update to follow
- Schedule Slated to begin executing year one of pavement management program in Spring 2026
  - Budget Pending completion of pavement analysis and Pavement Management Plan by Kimley Horn consultants, annually ~\$250k earmarked for execution of program

#### **Sidewalk Master Plan**

- **Phase** DESIGN {Prioritization Logic next slide}
  - All data is in house and initial physical assessment has been completed
  - Final physical assessment needed after council direction
  - **Schedule** Execution of repair work slated for Spring 2025
- **Budget** ~\$900k earmarked for annual allocation



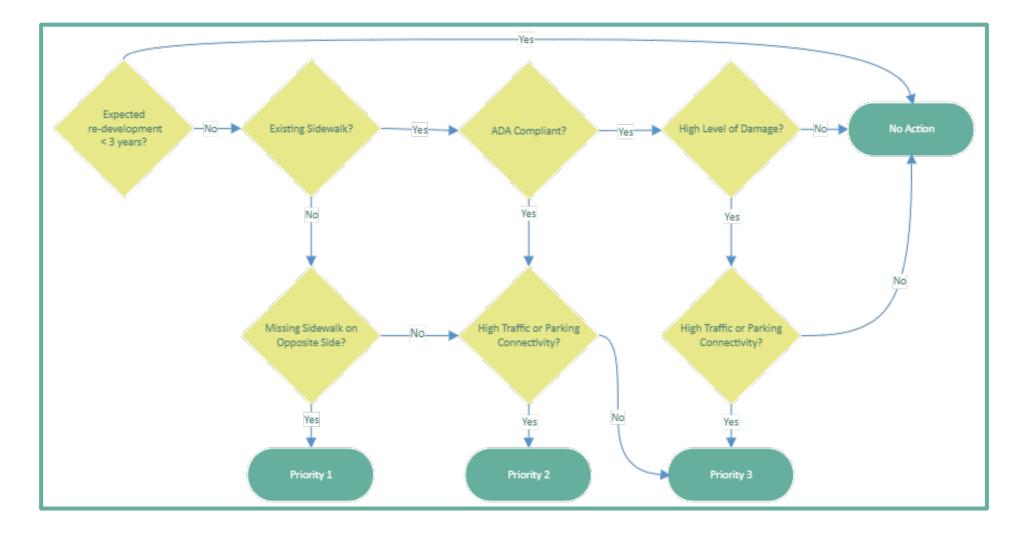



#### Warm Springs Preserve

- Phase DESIGN Building permit for building approved; Floodplain development permit resubmit in July 2024
- Schedule Bid for construction in Fall 2025; Slated for construction in Spring 2026
  - **Budget** Irrigation covered with existing donated funds, additional fundraising by Friends of WSP for Restrooms/Maintenance Building. Creek restoration and floodplain work funded via \$1.7M federal grant

### **Fire Station Solar**

- Phase DESIGN Finalizing design to go out to for bid
- Schedule Setbacks from design funding in the past have delayed progress. Construction expected in Spring 2026
  - **Budget** Estimated at ~\$200k



### **CIP Project List and Status**

#### **Ore Wagon**

- Phase DESIGN Architect of Record has supplied initial designs to use for phased approach
- Schedule Initial R&M activities planned for Spring 2026, additional phases will be based on council feedback
  - Budget Barn Doors R&M ~\$45k, Phase 1 ~\$125k, Future Phases TBD

#### **Bonning Cabin Stabilization**

- Phase DESIGN Structural assessment needed to determine when type of stabilization will be required
- Schedule Structural assessment being conducted in June with hopes to identify contractors for quotes and installation Fall 2024
  - Budget Initial structural assessment and design currently underway. Stabilization estimate will come from completed assessment



PROJECT NAME	PHASE	HEALTH	<b>FISCAL YEAR</b>
Fire Station Solar	DESIGN	•	2026
Forest Service Park Roofing	BID/PRECONSTRUCTION	•	2025
Forest Service Park Siding Renovations	CONCEPT	0	2025
Main St	CONSTRUCTION	0	2024
Final Main St Furnishings & Transit	CONCEPT	•	2025
Ore Wagon Museum Reno Phase I	DESIGN	•	2026
Ore Wagon R&M (Doors)	CONCEPT	igodot	2025
Bonning Cabin Stabilization	DESIGN	0	2025
Pavement Management Program	DESIGN	•	2025
Sidewalk Master Plan	COMPLETE	•	2025
Town Square Design	DESIGN	•	2024
Warm Springs Preserve Phase I	DESIGN	0	2024
City Hall Mechanical Upgrade Prep	CONCEPT	•	2024
