

Southern Outfall Initiatives Progress Update


Project 1: Southern Outfall Pipe Replacement

Progress on this project is ongoing, with the following key updates:

- **Material Staging:** All required materials have been staged on-site (see photos 1a and 1b).
- **Drainage Structure Installation:** The drainage structure adjacent to US-1 has been set, and multiple sections of the 60" pipe heading south have been successfully installed (see photos 2a and 2b).
- **Storm-Pipe/Sewer Conflict:** The contractor is currently addressing a conflict between the storm pipe and sewer infrastructure (see photo 3).
- **Water Main Relocation:** The relocation of the water main has been completed, and the required bacteria testing has been successfully passed (see photo 4).

Supporting Photos:

- Photo 1 – Material Staging
- Photo 2 – Drainage Structure Installation
- Photo 3 – Storm-Pipe/Sewer Conflict
- Photo 4 – Water Main Relocation

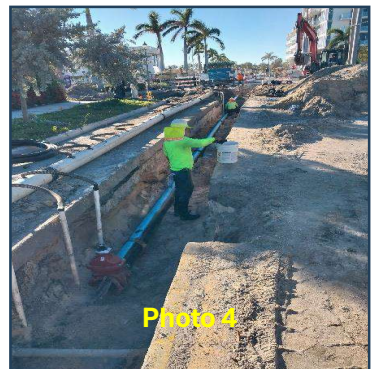

Project 2: Bert Bostrom Green Infrastructure

Significant progress has been made, including:

- **Drainage Piping:** Installation of new drainage piping along 6th Street and 7th Street has been completed.
- **Sidewalk and Drive Aprons:** Reconstruction of sidewalks and drive aprons is finished (see photos 5a and 5b).

- **Storage Chamber Installation:** Work on the storage chamber installation is underway.

Supporting Photos:

- Photo 5 – New drainage piping
- Photo 6 – Completed Sidewalks and Drive Aprons
- Photo 7 – Storage chamber installation



Project 3: Cured-In-Place Pipe Lining

- **Contractor:** The Hinterland Group has been selected to work the pipe lining.
- **Preparation Work:** The contractor has completed the cleaning and televised inspection of the pipes scheduled for the lining.
- **Next Steps:** Lining work is expected to commence the week of January 27, 2025.

Project 4: 10th Street Green Infrastructure Improvements

- **Procurement:** The selection process for a design firm has been completed, and submitted proposals are currently under review.
- **Project Timeline:** The design phase is expected to be completed by August 2025, after which the project will transition into the construction phase.
