


Public Works Project Update

1. Boca Ciega Street End Project Approval

- Contract Approved by BOC June 11, 2025
- Contract amount \$149,998.42
- Scope of Work includes
 - Installation of pervious paver walkways at all 5 locations and installation of planters and irrigation at 1-4 parks
 - Week of October 13, 2025
 - #1 – Pavers in progress and irrigation to start this week
 - #2 – Pavers and Irrigation complete
 - #3- Pavers and irrigation complete
 - #4- Pavers complete irrigation in progress set to be completed this week
 - #5 – Pavers complete, site cleanup needed
- Week of October 20th – finish pavers and start planting in raised planters

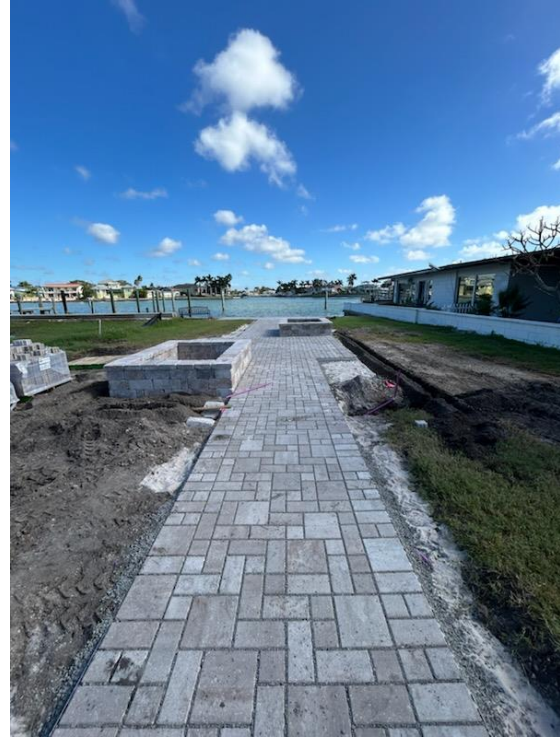

2. Patriot Park Military Court of Honor 424 150th Ave.

- Contract Approved by Board of Commissioners for \$225,812.43
- Groundbreaking Ceremony was held on June 20, 2025
- Scope of Work -Install decorative concrete consisting of a Shell aggregate and a pea pebble aggregate with a stained concrete star and install flag poles for all branches of the military and LED lights.
- 10-13-25 Week – Install circular pavers, complete flag pole installation, seal all concrete, and grade and resod around the construction area



3. Area 3 – E & W Parsley, Marguerite Dr., Lynn Way, A & B St., Pruitt, and S Bayshore Roadway and Drainage Improvement project

- Started June 9th
- The installation of the Pinellas County water line along S Bayshore, Pruitt Dr., and Marguerite Dr. have been completed. The contractor is working to install long line services along each roadway.
- Water line services have been installed across the road and contractor is working to pressure test and chlorinate the line to put in service.
- 10-13-25 Week – Tie in Pinellas County Water main on Pruitt Dr., Marguerite Dr., and S Bayshore Dr. Pressure test and chlorination test all passed.
- 10-20-25- Start stormdrain outfall at 708/704 Pruitt Dr.,



4. Johns Pass Dredging 10-13-25

USACE Permit: Permit issued.9-9-25

- Permit modification completed and waste disposal site updated

FDEP Permit: Permit issued.

FDOT Permit: Reissued because original was set to expired December 2025.

Pinellas County Permit: Application submitted to county 10-7-25

Bid – Bid has been placed on Demandstar 10-7-25.

Mandatory Pre Bid meeting – 10-22-25 10:30AM

Bid Opening – November 21, 2025 9:00Am


BOC Commission Approval – Special Meeting November 25, 2025

Contract start – November 26.

Pinellas County Project to dredge

Johns Pass Channel is scheduled for

November/December which will affect the original project timeline of December Dredge. Once the county has completed their portion the interior channel project will commence.

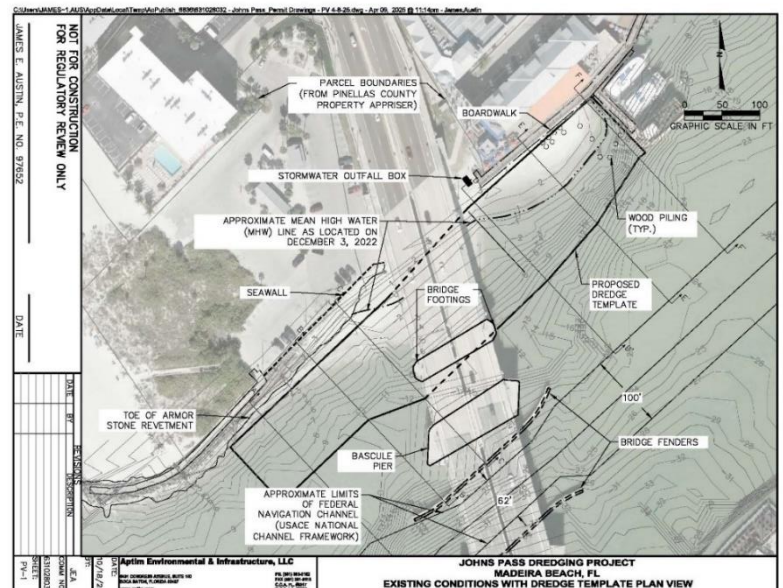

5. Area 5 – 131st Ave. and 129th Ave., Roadway and Drainage Improvement Project

Will include Pelican Ln., Village Blvd., Cities surface lot, and Boardwalk Pl.


- Plans in With Engineer for final review and to put together specification.

6. Area 6 – Municipal Dr., 153rd Ave E, 154th Ave E, 155th Ave E, 1st St. E., 2nd St. E., and Harbor Dr. Roadway and Drainage Improvement Project

- 90% Plans with Pinellas County Engineering Firm for review
- Working on Southwest Florida Water Management District Exemption Permit

7. Johns Pass Jetty

- Mobi Mat Installed 7-29-25
- Pre Application Meeting was held September 16th.
 - Staff is compiling information and coordinating with Army Corp.
 - Once Specifications are noted staff will work with Engineers on design for the new walkway.
 - Once design is completed staff/engineers will submit for permits from Amry Corp, 408 Division, FDEP, and Pinellas County.
 - Additional information sent to Army Corp. 9-24-25.
Staff followed up on 10-13-25 for update.
 - Waiting for Engineer proposal for Design, Permitting, and onsite construction engineering services.
 - Pinellas County has requested a sidewalk agreement to ensure the city is responsible for the walkway.

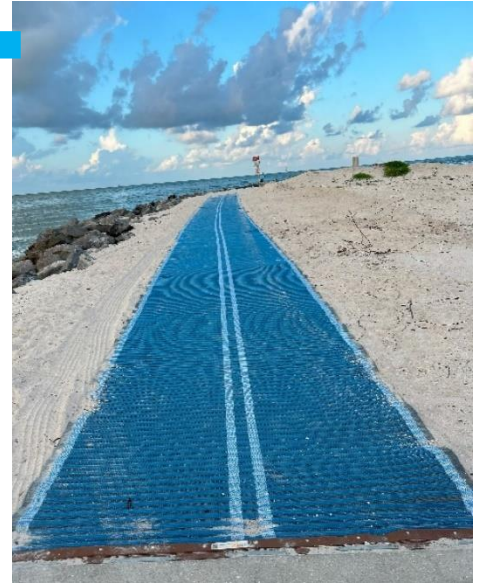

8. Tom & Kitty Stuart Park Hurricane Helene

- Seawall Plans completed
- Site Plan Proposal received 10-13-25, staff working to issue PO.
 - This will include coordination with Structural engineer and Restroom Fabricator.
- Working with CXT for Prefab restroom and City staff for requirements for elevation.
- Met with CXT 9-16-25 to discuss bathroom construction – Gave specifics on what will be needed for the slab.
 - Contracting a structural engineer to design an elevated slab for the restroom- waiting on proposal
- Once completed, design plans will be placed out to bid

9. Snack Shack Remodel Hurricane Helene

- Invitation to bid (ITB) 25-13 placed on Demandstar 10-10-25.
 - Mandatory Pre Bid meeting 10-16-25 9:00AM
 - Bid Opening November 4, 2025 9:30Am
 - BOC Workshop and Regular meetings for discussion / approval November 12, 2025 4PM
Workshop 6PM Regular meeting
 - Contract time of 90 Days starting November 13.

10. Bay Point Dr. Roadway Milling and Resurfacing – Mill 1.5in of current asphalt and place back 2in. Roadway drainage and improvement project scheduled to start design in FY2026 anticipated 3 years for design.

- BOC workshop on August 27th for discussion
- BOC Regular Meeting for Approval September 10th. – Staff error and amendment was not created for BOC approval to amend Area 3 contract to add Bay Point mill and resurface
- Due to issues and concerns with Area 3 staff has decided to pivot and add Bay Point Roadway Mill and Resurface to Area 5 Project which is intended to be placed out to bid by December 2025.

11. Public Works Building

- BOC approved Engineering proposal with Pennoni for \$150,660 April BOC Regular meeting
- 10-22-25 Staff request to change location from 505 150th Ave to 555 150th Ave.

12. Beach Groin Restoration Project - COMPLETED - 22 Groins restored and fortified- minor concrete repairs due to some concrete Spalding
