



August 15, 2025

Ms. Jessica Murphy
Manager, DWR Compliance and Enforcement Unit
Tennessee Department of Environment and Conservation
Davy Crockett Tower
500 James Robertson Pkwy, 9th Floor
Nashville, TN 37243

RE: Mount Pleasant May 2025 CAP/ER Status
Consent Order and Assessment, WPC 17-0004
City of Mount Pleasant

Dear Ms. Murphy:

In accordance with the requirements of the July 24, 2018, TDEC Consent Order and Assessment, WPC 17-0004, and the recently approved deadline extension request, a summary of the status of the corrective action plan / engineering report (CAP/ER) items is provided below.

As stated in previous consent order annual reports submitted to TDEC, the single CAP/ER item that remains for the City of Mount Pleasant to complete is the improvements at the wastewater treatment plant (WWTP). The WWTP construction project scope consists of rehabilitating a majority of the processes at the facility. A summary of the scope, broken down by facility area, is included in the attached table. The table also details the work that has been completed and the work remaining within that area.

During the last month, the project achieved substantial completion on July 21. The City and Barge conducted a punch list walkthrough on July 17 to identify remaining punch list items prior to final completion of the project. The list included 132 items of work to be completed or documentation to be submitted. The contractor has been progressing through the list with more than 90 items completed to date.

Over the next month from the date of this letter, the following construction progress is anticipated to be made:

- Contractor will complete most remaining items of work at the project site
- Contractor will continue working on project closeout documentation

Photos of construction completed progress are included with this letter.

If there are any questions regarding the attachments to this letter or if any additional information is needed, please contact me at 615-252-4236 or matthew.johnson@bargedesign.com.

Sincerely,

Barge Design Solutions, Inc.

A handwritten signature in black ink, appearing to read "Matthew Johnson".

Matthew Johnson, PE
Project Manager

c: Mr. Kareem Moxey, TDEC
Mr. Phillip Grooms, City of Mount Pleasant

Ms. Jessica Murphy
August 15, 2025
Page - 2



Mr. Ted Howell, City of Mount Pleasant
Mr. Dale Brown, City of Mount Pleasant
Mr. Luke Burris, PE, Barge Design Solutions

Enclosures

Barge project # 34808-00

Plant Area	Scope	Work Completed	Work Remaining
Site	Repair disturbed areas, demolish of four older structures, install new sidewalks, asphalt paving of the plant driveway.	<ul style="list-style-type: none"> • Disturbed areas have been repaired. • Demolition of one structure. • Final electrical and communication pull boxes and conduit. • General grading and site clean up. • Began demolition of one structure • Demolition of two structures. • New sidewalks. • Paving the driveway • Completed nine punch list items 	<ul style="list-style-type: none"> • Punch list items.
Influent Pump Station	Replace four pumps, select piping, and all associated instrumentation, controls, and electrical equipment.	<ul style="list-style-type: none"> • All new pumps are installed. • Piping associated with pumps • New electrical gear, control panels, and instrumentation are installed. • New piping for return from lagoon system, including flow meter. • Installed jib crane. • Painting new piping. • Completed three punch list items 	<ul style="list-style-type: none"> • Punch list items.
Headworks	Install new access platform, add overflow piping to screens, install concrete pad and trench drain for dumpster.	<ul style="list-style-type: none"> • All items completed. 	
Treatment Basin 1	Install mixer, baffle wall, diffusers, sluice gate, effluent weir, dissolved oxygen (DO) probes, slide gate, splitter box	<ul style="list-style-type: none"> • All items completed. • Completed four punch list items 	<ul style="list-style-type: none"> • Punch list items.
Treatment Basin 2	Install mixer, baffle wall, diffusers, sluice gate, effluent weir, DO probes, PH probes, and slide gate.	<ul style="list-style-type: none"> • All items completed. • Completed five punch list items 	<ul style="list-style-type: none"> • Punch list items.
Intermediate Mixed Liquor Recycle Pump Station	Replace existing pumps with new pumps, select piping, and all instrumentation, controls, and electrical equipment.	<ul style="list-style-type: none"> • All items completed. • Completed installation of piping to allow additional screening prior to membranes. • Completed five punch list items 	<ul style="list-style-type: none"> • Punch list items.

	Expand concrete area for valves and access.		
Membrane Bioreactor and Equipment Building	Construct new building (shared with administration and lab) with tanks for MBR and rooms for equipment and chemicals. Systems include permeate pumps, return activated sludge (RAS) pumps, membrane blowers, backpulse tank, compressed air, sodium hypochlorite and citric acid feeds, and instrumentation and controls.	<ul style="list-style-type: none"> • All equipment, piping, instrumentation is installed and tested. • MBR system commissioned and operational. • Conducted MBR system performance test • Completed installation of carbon feed system • Completed fifty-seven punch list items 	<ul style="list-style-type: none"> • Additional controls/programming items to be finalized. • Punch list items.
Administration and Lab Building	Construct new building (shared with MBR equipment) with lab, office, breakroom, bathroom, electrical room, and control room	<ul style="list-style-type: none"> • All items completed. 	<ul style="list-style-type: none"> • Punch list items.
Blower Building	Demolish existing blowers and generator. Install two process blowers, and two digester blowers. Replace main plant electrical feed and motor control centers (MCCs). Miscellaneous building improvements.	<ul style="list-style-type: none"> • All items completed. • Automation of aeration system. • Optimization of aeration system • Completed twelve punch list items 	<ul style="list-style-type: none"> • Punch list items.
Digester	Install new 4-inch diameter ductile iron air piping, diffusers, sluice gate, check valve, and decant piping.	<ul style="list-style-type: none"> • Air piping installed. • Check Valve installed. • Corrected sluice gate installation. • Decant piping • Completed six punch list items 	<ul style="list-style-type: none"> • Punch list items.
Lagoon Site	Install motor operated valve, piping to return flow to WWTP, SCADA panel.	<ul style="list-style-type: none"> • All items completed. 	<ul style="list-style-type: none"> • Punch list items.

Construction Progress Photos



1. Paved Driveway




2. Paved Driveway



3. Disconnects Labeled



4. RP Panel Label Added

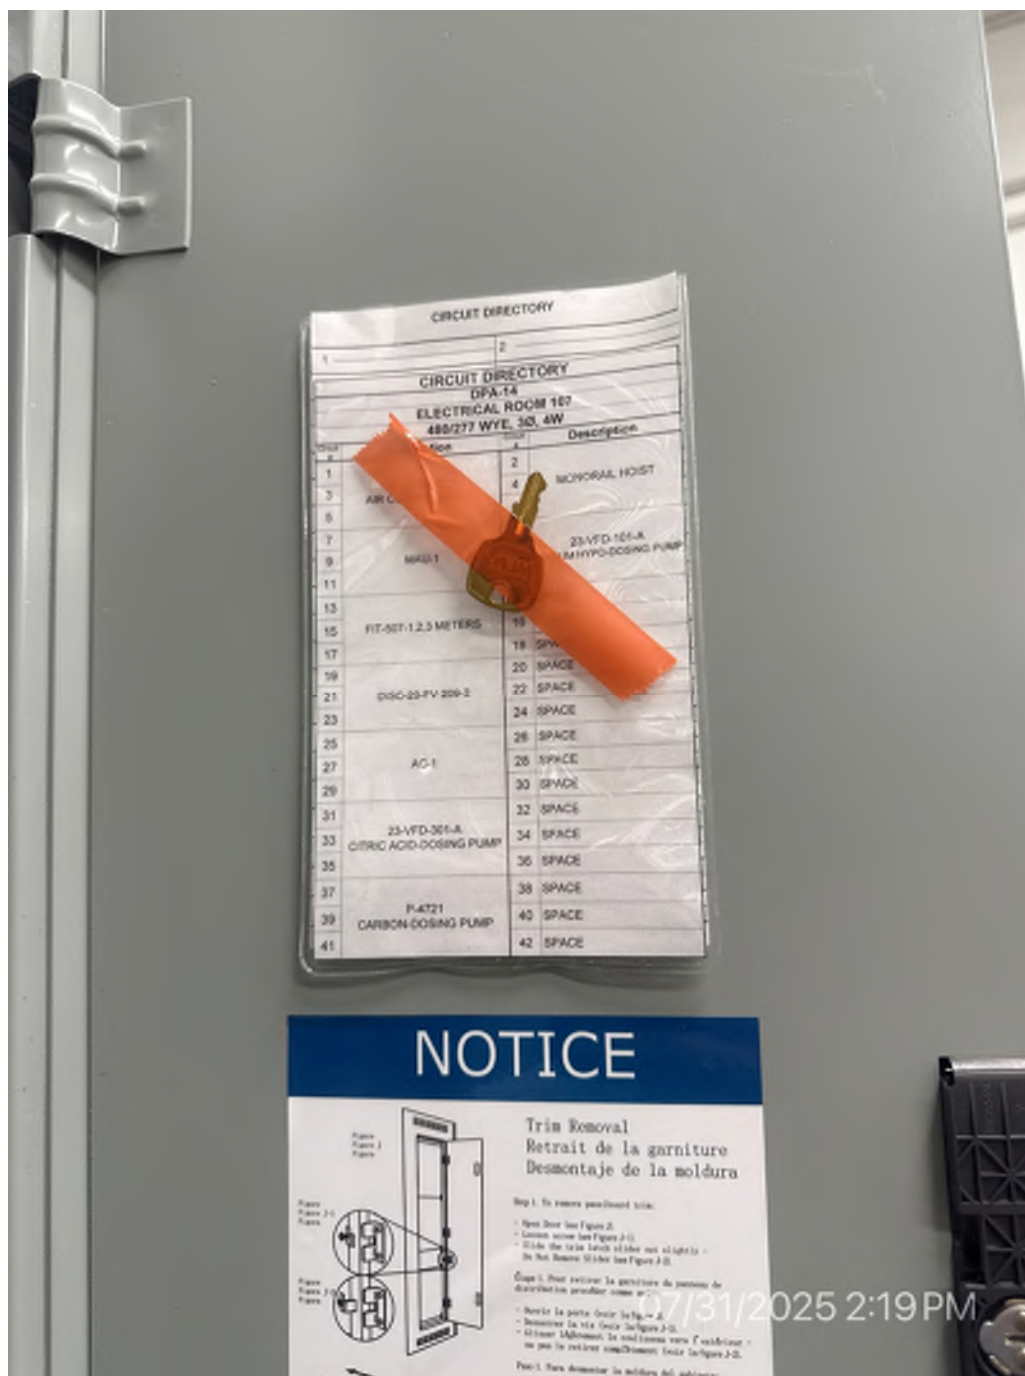

5. DP Panel Schedule Completed
