



2026 WEEKLY CONSTRUCTION UPDATE

June 16 through June 22

*Please note: Any indication of a project's schedule is only an estimate.
Construction work could be delayed by many factors, such as inclement weather.



PROJECT STATUS

YELLOW	- NOT STARTED	GREEN	- ACTIVE
RED	- STOPPED OR DELAYED	BLACK	- COMPLETE

COUNTY PROJECTS

Project: **NOVI ROAD RECONSTRUCTION/REHABILITATION (8 MILE TO 9 MILE ROADS)**

Prime Contractor: Dan's Excavating, Inc.

Start: April 15, 2025

End: November 15, 2026

Consultant: RCOC - In-House Project Management

Description: See attached link to the right for RCOC construction updates. <https://www.rcocweb.org/668/Novi-Road-8-Mile-Road-to-9-Mile-Road>

The Road Commission for Oakland County (RCOC), in partnership with the cities of Novi and Northville, will rehabilitate and reconstruct Novi Road, from 8 Mile to 9 Mile Roads. Phase 1 - relocate utilities (DTE, Consumers, AT&T, etc.) in spring of 2025 - **COMPLETE**; Phase 2 - reconstruct the 'curve' between 8 Mile Road and Allen Drive in summer/fall of 2025 - **COMPLETE**; and Phase 3 - **rehabilitate the remainder of Novi Road from Allen Drive to 9 Mile Road, in 2026. Plans are also to add a continuous center left turn lane throughout the entire section of Novi Road as well as the installation of a High-Intensity Activated Crosswalk or HAWK pedestrian signals, located just north of Galway Drive.**

Traffic Control/Detours: Pg 4 of 9 - Detour map attached as an appendix.

Phase 3 - the contractor will maintain one-way, southbound traffic only. Northbound traffic will be detoured to Beck, 10 Mile, and back to Novi Road.

Work Status:

Construction, closure and detour started on Monday, March 30th. Contractor is working on the southbound side first and have shifted southbound traffic on the northbound side for the first stage. A bulk of the storm sewer has been installed on the west side. The contractor is running into several underground utility conflicts that is significantly slowing progress.

Project: **BASE LINE OR 8 MILE ROAD/CSX RAILROAD BRIDGE DECK REPLACEMENT**

Prime Contractor: E.C. Kornfeil Co.

Start: March 2, 2026

End: August 15, 2026

Consultant: In-House WCDPS Project Management Staff

Description: See attached link to the right for WCDPS construction updates. <https://www.wcdps.org/231/12-Mile-Road-Novi-Road-to-Farmington-Road>

The Wayne County Department of Public Services (WCDPS) will be completing the final stage (Stage 3) of construction on 8 Mile Road between Haggerty and Novi Roads which is the bridge rehabilitation and bridge deck replacement at the CSX/Lake State Railway. Stage 1 was the concrete rehabilitation from Haggerty Road to just west of Meadowbrook Road. Stage 2 was completed late last year, milling the existing concrete and placing new asphalt pavement over the top from just west of Meadowbrook Road to the CSX bridge.

Traffic Control/Detours: Pg 5 of 9 - Detour map attached as an appendix.

8 Mile Road will be completely closed in both directions at the CSX/Lake State Railway bridge for the full duration of the project. The detour for westbound traffic will be Haggerty Road, south to 6 Mile Road, to Beck Road, and back to 8 Mile Road. Eastbound traffic will be in the reverse.

Work Status:

The closure and construction began on Monday, March 2nd. The contractor is progressing well.

Project: **12 MILE ROAD REHABILITATION (NOVI ROAD TO FARMINGTON ROAD)**

Prime Contractor: Cadillac Asphalt, LLC

Start: July 1, 2026

End: October 30, 2027

Consultant: Internal RCOC Design and Inspection Staff

Description: <https://www.rcocweb.org/733/12-Mile-Road-Novi-Road-to-Farmington-Road>

The Road Commission for Oakland County (RCOC) in cooperation with the cities of Novi and Farmington Hills will be rehabilitating 12 Mile Road from Novi Road to Farmington Road over the course of two years, in four, distinct stages (see attached 'Staging Plan'). Stage 1 will take place this summer on the concrete portion of 12 Mile Road between Novi and Meadowbrook Roads and the asphalt portion between just east of Halsted Road and Farmington Road. The plan is to repair the outer lanes first, then repair the inner lanes.

Traffic Control/Detours: Pg 6 of 9 - Staging plan attached as an appendix.

The contractor will maintain at least one lane, in each direction throughout the duration of the first stage.

Work Status:

Contractor has been selected and RCOC will be scheduling a pre-construction meeting soon to discuss specifics regarding Stage 1.

Project: **GLWA's 14 MILE TRANSMISSION WATER MAIN REPLACEMENT**

Prime Contractor: Ric-Man Construction, Inc.

Start: January 12, 2026

End: August 15, 2026

Consultant: Brown & Caldwell and DLZ Corporation

Description: <https://www.glwa.org/14miletransmission/>

The Great Lakes Water Authority (GLWA) in cooperation with the Road Commission for Oakland County (RCOC) and the cities of Novi, Walled Lake, Commerce Township, Wixom, and Farmington Hills will be replacing and/or rehabilitating the 42-inch water transmission main along 14 Mile Road from roughly East Lake Drive to M-5. This construction will constitute rehabilitation of certain portions with a Carbon Fiber Reinforced Polymer (CFRP) repair, mainly through the Walled Lake and Wixom areas. All other areas will be an outright replacement pipe.

Traffic Control/Detours: Pg 7 of 9 - Closure and Detour plans attached as an appendix.

14 Mile Road (East Lake Drive to M-5) is still currently closed to eastbound traffic while maintaining westbound traffic.

Work Status:

Northbound and southbound Novi and Decker Roads have been reopened to traffic at 14 Mile Road. Mainline pipe is installed, tested and officially back on line. Crews are now focused on preparations for the 14 Mile Road restoration. The new concrete curb and gutter has been poured between East Lake Drive and Novi Road. Mid this week, the contractor will be alternating construction of the entrances to the Maples of Novi (Centennial and Wakefield Drives), closing one at a time. Also, they will begin reconstruction of the Haverhill Farms entrance, Kingswood Boulevard, by building and closing one-half at a time.

Project: **2026 BRIDGE PREVENTATIVE MAINTENANCE PROGRAM - NOVI ROAD OVER THE CSX RAILROAD**

Prime Contractor: TBA

Start: July 15, 2026

End: August 15, 2026

Consultant: Internal RCOC Design and Inspection Staff

Description: See attached link to the right for RCOC construction updates. <https://www.rcocweb.org/668/Bridges-Preventative-Maintenance>

The Road Commission for Oakland County (RCOC) has developed a Preventative Maintenance Program for several of their bridges that does not warrant rehabilitation or replacement. These programs are less intrusive while also extending the usable life of the bridge which is more cost-effective in the long term. One of the bridges selected is the Novi Road bridge over the CSX Railroad tracks, just south of the Main Street/Bond Street intersection.

Traffic Control/Detours: N/A - Detour map is attached as an appendix.

The County's contractor will maintain one lane in each direction for the duration of the project.

Work Status:

The contract will go out to bid in June. Construction is slated for mid-summer (July to September).

CITY PROJECTS

Project: **BECK ROAD RECONSTRUCTION (GRAND RIVER AVENUE TO 11 MILE ROAD)**

Prime Contractor: Dan's Excavating, Inc.

Start: April 6, 2026

End: November 1, 2026

Consultant: AECOM-Great Lakes

Description:

Through MDOT's Local Agency Project office and federal funding program (\$3.6 Million), the City will be reconstructing and widening Beck Road from Grand River Avenue to 11 Mile Road to five lanes. The plan is to first locate and lower the existing 16-inch and 24-inch water mains in order to install a new large diameter culvert under Beck Road, just south of Heritage Drive. The contractor will begin installing a new storm sewer network along the western edge of Beck Road before construction begins on the road widening. There will also be improvements made to the signalized intersection to the hospital and ADA sidewalk upgrades throughout.

Traffic Control/Detours: Pg 8 of 9 - Detour map attached as an appendix

Most of the preparatory work will be performed off the edge of the roadway. Drivers can expect to see minor lane closures or lane shifts under flag control for this work. Once the actual road work begins, Beck Road will be open to southbound traffic only; most northbound traffic will be detoured using 10 Mile, Novi Road, and Grand River Avenue. **Local traffic will still be able to use northbound Beck Road north of 10 Mile, but there is a hard closure just south of 11 Mile Road.**

Work Status:

All the mainline paving of the southbound half of Beck Road from 11 Mile Road to Grand River Avenue is now complete. The contractor is waiting for the required 5 to 7 days of cure on the new concrete before going to work on the second halves of each drive approach on the west side (i.e., Providence Drive North, South, Heritage Drive, and Everbrook Drive). The contractor is in line to possibly switching traffic over to the newly paved southbound side and beginning construction on the northbound side by the end of this month.

Project: **NOVI ROAD MEDIAN ISLAND CONVERSION (12 MILE TO 13 MILE)**

Prime Contractor: TBD

Start: July 15, 2026

End: September 1, 2026

Consultant: Spalding DeDecker

Description:

The City will be providing improvements to the center median islands on Novi Road, between 12 Mile and 13 Mile Roads. Improvements will be to deconstruct the current, natural, sunken islands with newly raised, decorative concrete islands along with planter boxes for small bushes and trees.

Traffic Control/Detours: N/A - Detour map attached as an appendix

One lane of traffic in each direction (outer lanes) will be provided at all times during construction. No closures or detours are expected for this work.

Work Status:

The City of Novi had to terminate the contract with the previous awarded contractor, Santos Cement, for they were unable to supply the required bonds and insurance. We are currently looking into the second lowest bidder. We will be taking a new contract award to City Council for approval at the June 22nd meeting.

Project: **VILLAGE WOOD ROAD RECONSTRUCTION (CRANBROOKE DRIVE TO HAGGERTY ROAD)**

Prime Contractor: Fanson Company, Inc.

Start: June 8, 2026

End: September 30, 2026

Consultant: AECOM-Great Lakes

Description:

The City's contractor, Fanson Company, Inc., will reconstruct Village Wood Road from Cranbrooke Drive to Haggerty Road with new asphalt, concrete curb and gutter, enclosing the ditches, improved storm sewer network, and adding a new, 6-foot wide concrete sidewalk along the north side of the roadway.

Traffic Control/Detours: Pg 9 of 9 - Detour map attached as an appendix

Eastbound traffic will be maintained at all times, no matter which side of the roadway is being worked on. Westbound traffic will be detoured south on Haggerty Road, west on 9 Mile Road, north on Cranbrooke Drive, and back to Village Wood Road for the duration of the project.

Work Status:

The contractor began setting up the westbound detour and demolition work on Monday, June 8th. It should take about a week for the pavement removals on the eastbound side and then the contractor will begin installation of new storm sewer. Overall, construction is expected to take approximately 4 months to complete.

Project: **2026 NEIGHBORHOOD ROAD PROGRAM - ASPHALT STREETS (CONTRACT #1)**

Prime Contractor: TBD

Start: July 1, 2026

End: November 15, 2026 (Overall Program Completion)

Consultant: OHM-Advisors

Description:

This will be the first contract and the first year of a 2026-27 program whereby the City of Novi will be performing asphalt road work (full reconstruction, rehabilitation, and/or repair) on the following asphalt street segments: **full list of streets forthcoming.**

Traffic Control/Detours: N/A - detour map attached as appendix

Work Status:

Project: **2026 NEIGHBORHOOD ROAD PROGRAM - ASPHALT STREETS (CONTRACT #2)**

Prime Contractor: TBD

Start: July 1, 2026

End: November 15, 2026 (Overall Program Completion)

Consultant: OHM-Advisors

Description:

This will be the second contract and the first year of a 2026-27 program whereby the City of Novi will be performing asphalt road work (full reconstruction, rehabilitation and/or repair) on the following street segments: **full list of streets forthcoming.**

Traffic Control/Detours: N/A - Detour map attached as an appendix

Work Status:

CITY PROJECTS

Project: CEDAR SPRING ESTATES WATER MAIN LINING

Prime Contractor: FER-PAL Construction USA, LLC

Start: June 15, 2026

End: August 15, 2026

Consultant: OHM-Advisors

Description:

The Cedar Spring Estates subdivision has experienced numerous water main breaks over the last decade due to corrosion and deterioration of the existing ductile iron pipe. Instead of a full replacement of the water main which would involve significant excavation and disturbance to the adjacent lands and roadways, the City will be undertaking a placement of a cured-in-place pipe (CIPP) lining of approximately 5,000 feet of 8-inch and 600 feet of 12-inch water main. The project will also involve the replacement of existing valves and hydrants. A temporary water service will be provided to the residents prior to and during construction.

Traffic Control/Dehors: N/A - Detour map attached as an appendix

Depending on the locations of work which will vary, there may be some minor lane closures, but two-way traffic will be maintained at all times.

Work Status:

The contractor is setting up the temporary water services for the whole project which should be complete this week. Next week, the contractor will start excavating the bore pits needed for the entry points of the lining process.

Project: SOUTHWEST WATER MAIN LOOP (BECK, 8 MILE & NAPIER)

Prime Contractor: TBD

Start: June 15, 2026

End: October 15, 2026

Consultant: OHM-Advisors

Description:

The 2014 Water Master Plan Update identified a large area of the southwest quadrant of the City as having low or insufficient water pressure and fire protection. Therefore, this project will expand the "Island Lake Pressure District" by providing a "looped" water main connection between 8 Mile Road, Napier Road, 10 Mile Road, and Beck Road. The project will involve constructing approximately 16,800 feet of 12-inch ductile iron water main between 8 Mile Road and 10 Mile Road, through the ITC Sports Park, along Beck Road, and Napier Road.

Traffic Control/Dehors: N/A - Detour map attached as an appendix

No detours will be necessary for this project, but will involve a moving or "rolling" lane closure as the work progresses along the roadway. The lane closures will be protected along with flagging personnel.

Work Status:

Plans are currently being finalized and still negotiating easements with a few property owners. Plan is still to go out to bid this summer.

Project: 2026 CONCRETE PANEL REPLACEMENT PROGRAM

Prime Contractor: TBD

Start: July 1, 2026

End: October 15, 2026

Consultant: OHM-Advisors

Description:

The City has identified several neighborhood concrete streets with discrete areas or singular panels exhibiting severe cracking or deterioration that is need of replacement, rather than rehabilitating or reconstructing the roadway at great costs.

Traffic Control/Dehors: N/A - Detour map attached as an appendix

No detours will be necessary for this project, but may involve a small, distinct lane closure at the specific work area. The lane closures will be protected with traffic cones and barrels along with flagging personnel while the work is actively in progress.

Work Status:

The approved list of streets are being finalized and the project will go out to bid in the coming months.

Project: VILLA BARR PARK CONCRETE PATHS

Prime Contractor: Mattioli Cement Company, Inc.

Start: June 17, 2026

End: June 30, 2026

Consultant: AECOM-Great Lakes

Description:

City Council requested the paving of the pathways at Villa Barr Park to increase accessibility. Concrete will be placed over the existing aggregate paths as well as providing a new concrete loop around the existing pond.

Traffic Control/Dehors: N/A

No detours will be necessary for this work. The park will be closed during the duration of this project which is approximately 30 to 45 days.

Work Status:

The contractor will mobilize to the site this Tuesday and begin removing the topsoil in the locations of the proposed pathway. The overall project is anticipated to take approximately two weeks to complete.

Project: ITC PATHWAY AND BOARDWALK CONNECTION TO BOSCO FIELDS

Prime Contractor: L.J. Construction Company

Start: April 25, 2026

End: July 31, 2026

Consultant: AECOM-Great Lakes

Description:


Through MDOT's Local Agency Project office and federal funding program through SEMCOG (\$230,000), the City will be constructing a pathway between the existing ITC Trail and Bosco Fields Park. Construction will involve the placement of a hot-mix asphalt shared use path from the existing ITC Trail, south of 11 Mile Road, easterly to Bosco Fields Park, connecting to Beck Road, including approximately 600 feet of a 14-foot-wide boardwalk.

Traffic Control/Dehors: N/A - Detour map attached as appendix

No detours or closures will be necessary for this project. A small area of the southwestern portion of Bosco Fields will be quartered-off for staging of contractor equipment.

Work Status:

The tree subcontractor has completed the removal of all trees, stumps and roots within the proposed pathway/boardwalk limits. The helical pier subcontractor has installed roughly half of the piers to date and should be complete by the end of this week.

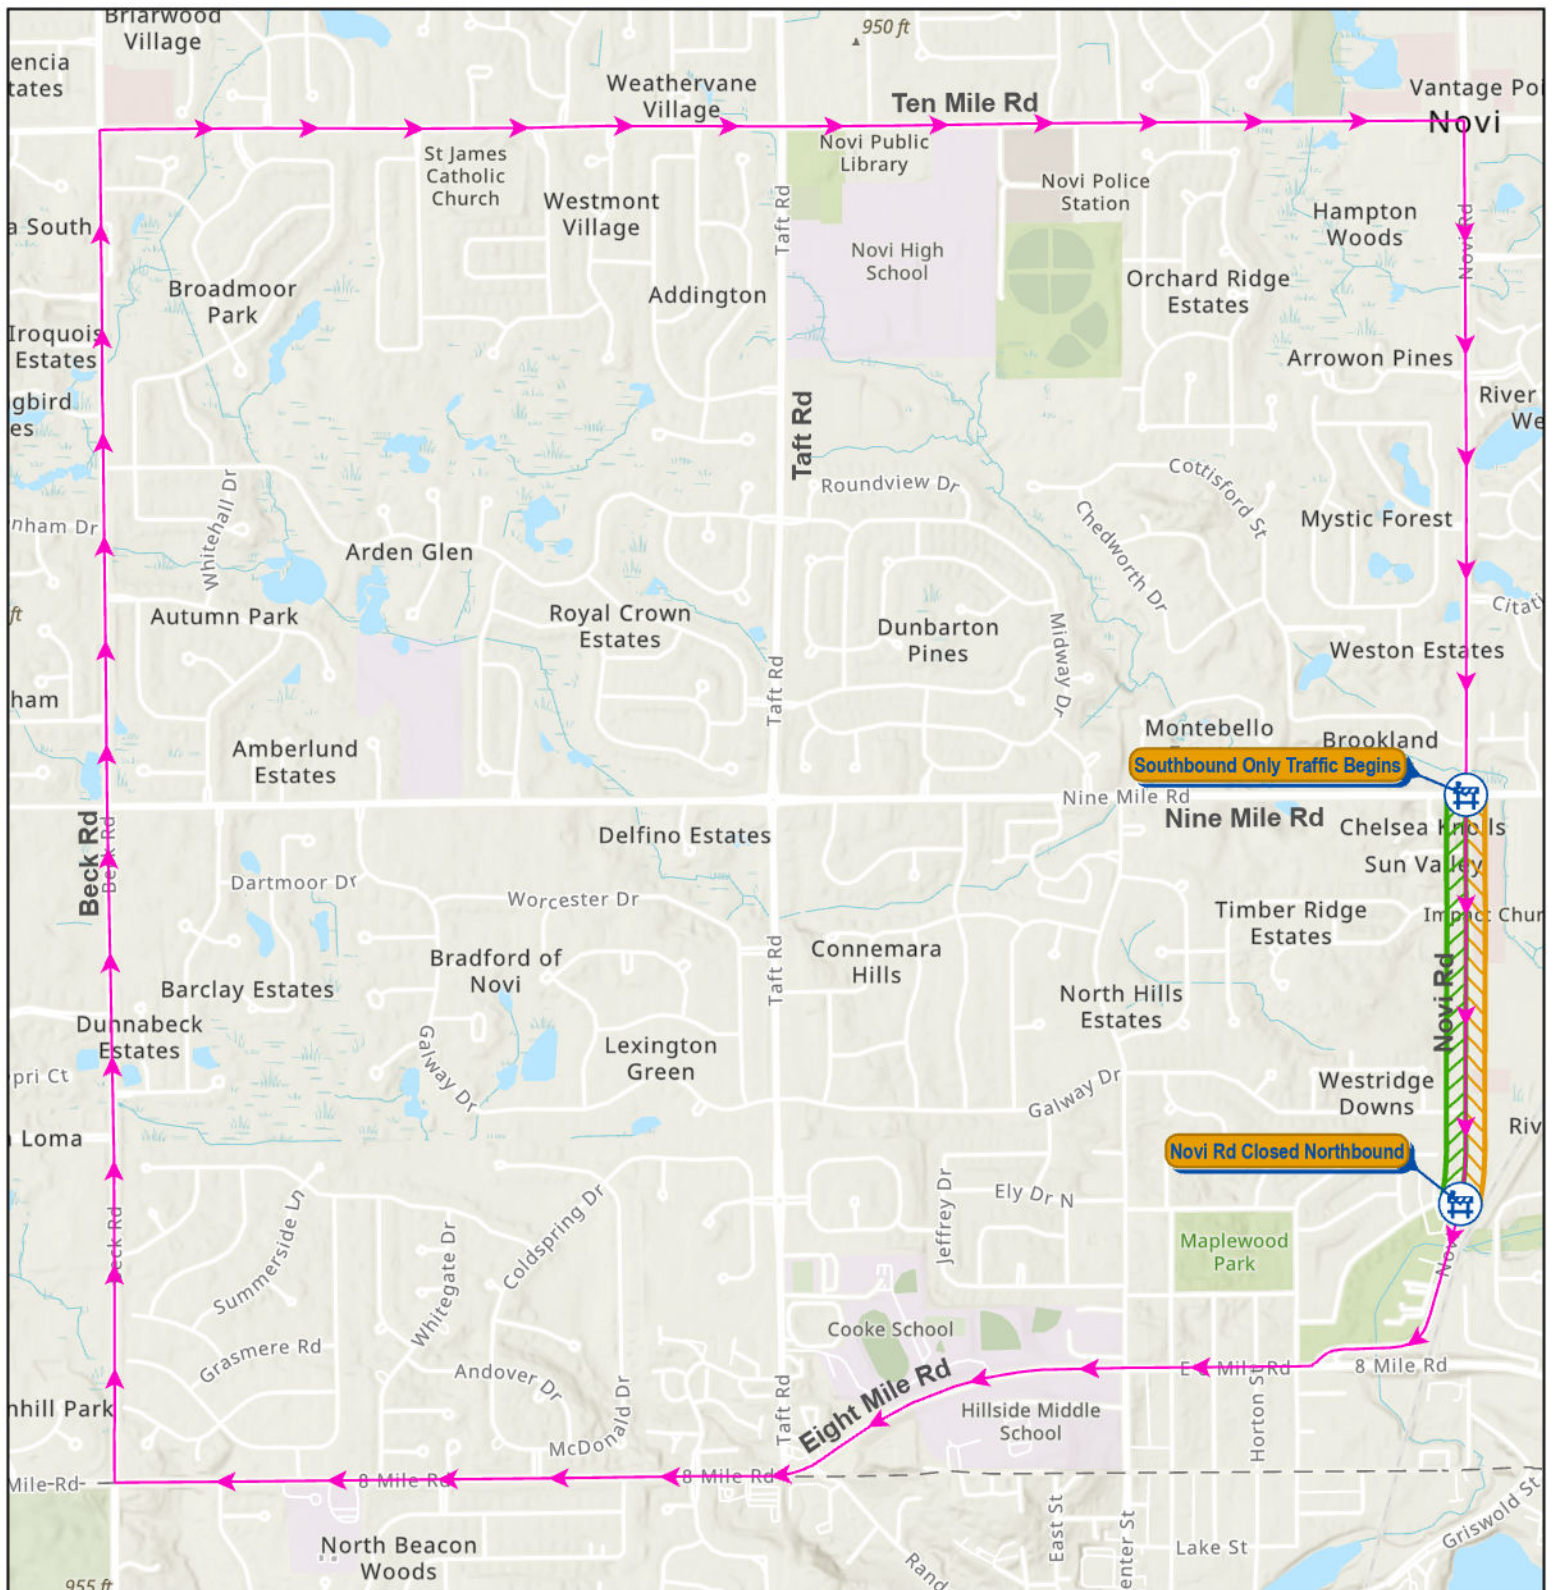

Novi Rd is **closed to northbound traffic** from Allen Dr to 9 Mile Rd for the duration of this project.

Northbound traffic should navigate around this closure using 8 Mile Rd to Beck Rd to 10 Mile Rd and back to Novi Rd.

- Detour Route
- CLOSED to Traffic
- OPEN to Traffic




Novi Rd Reconstruction Allen Dr to Nine Mile Rd

0 750 1,500 3,000 4,500 Feet



Map Print Date: 2/24/26
Map Author: K. Blough

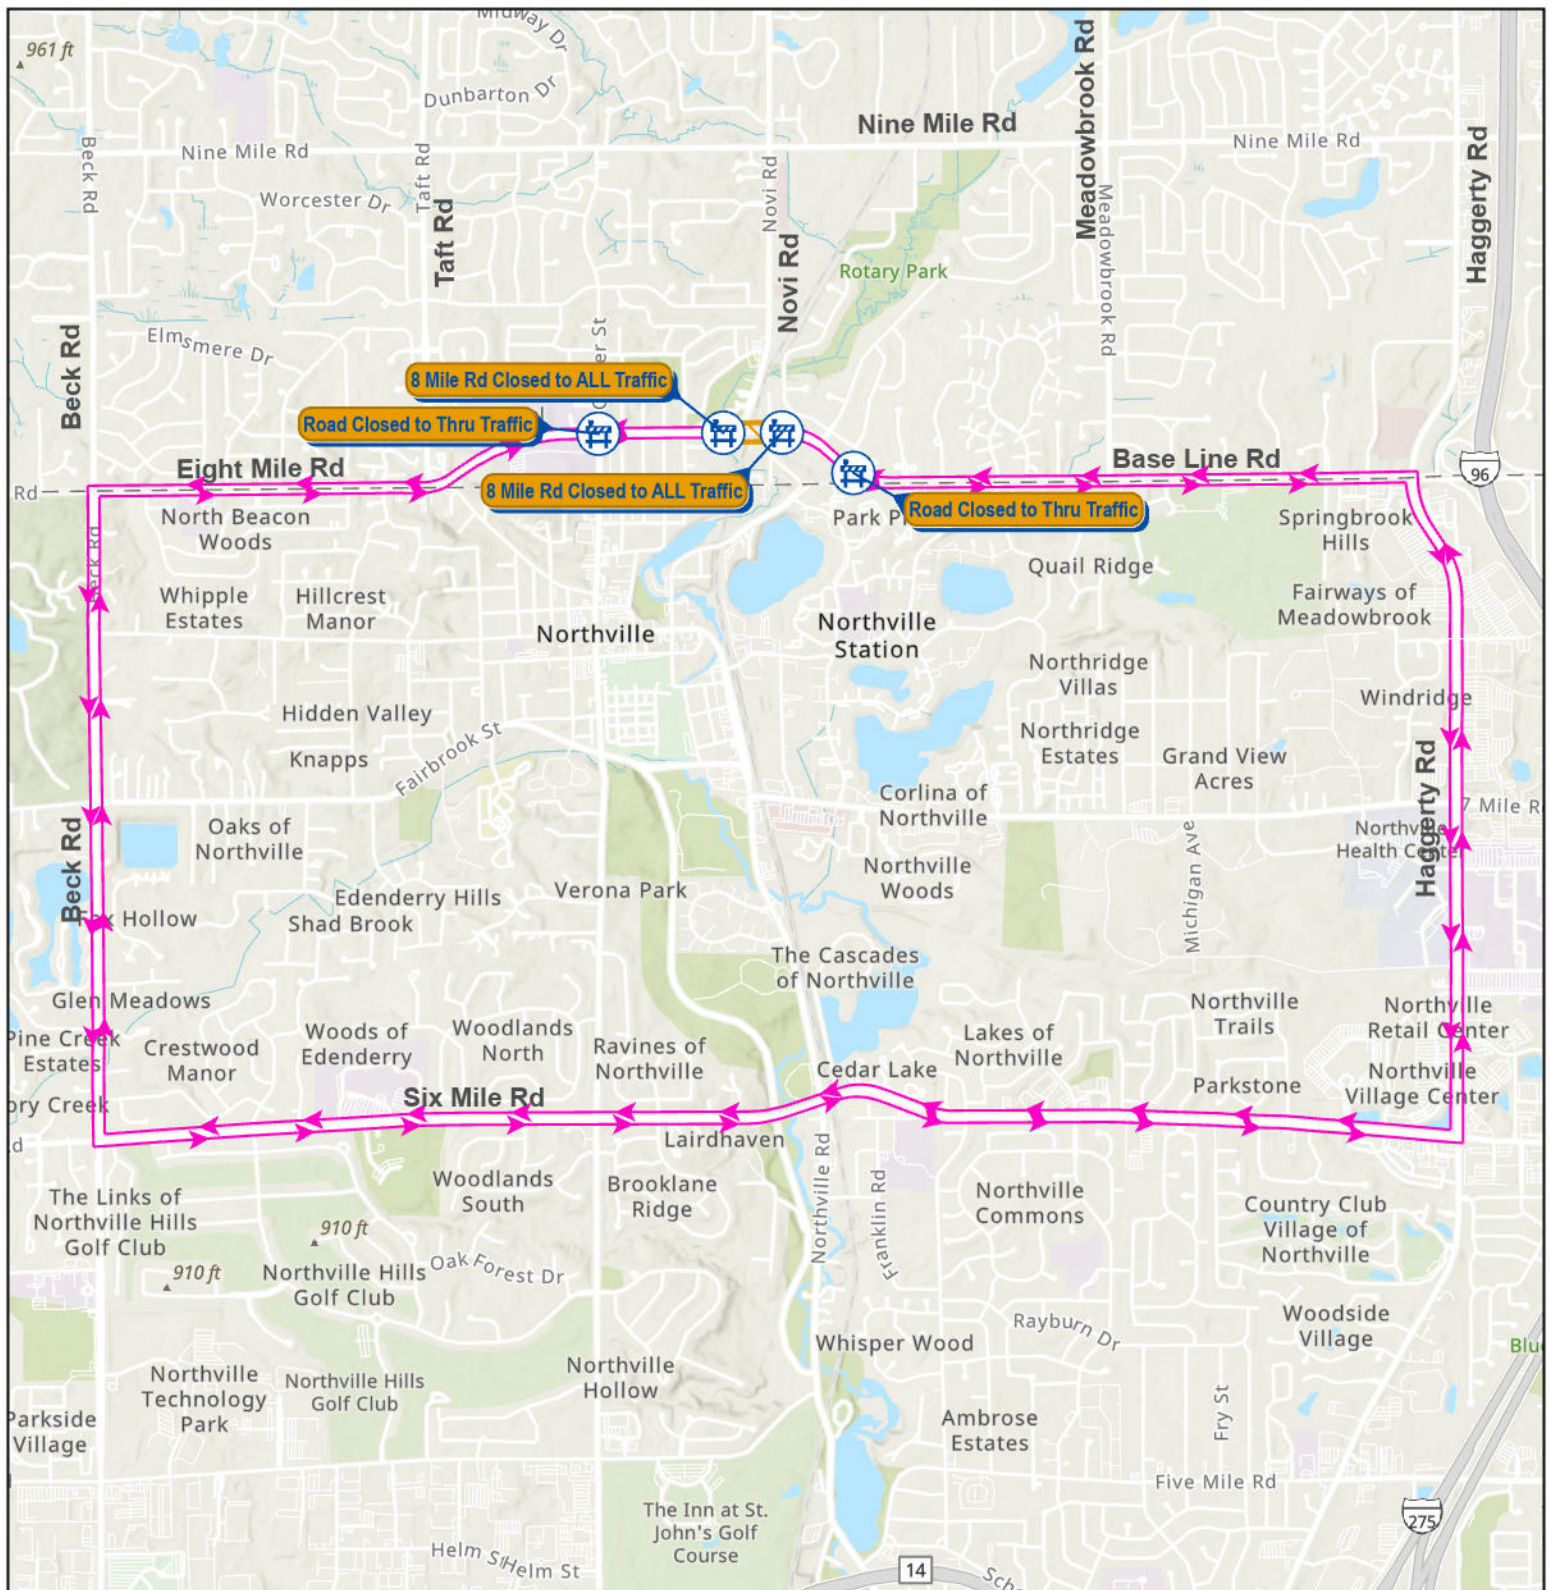

8 Mile Rd/Base Line Rd over the CSX railroad tracks will be **closed to ALL traffic** for the duration of the project while the bridge repairs are underway.

The designated detour is 8 Mile Rd to Haggerty Rd to 6 Mile Rd to Beck Rd back to 8 Mile Rd and vice versa.

 Detour Route
 CLOSED to Traffic




8 Mile Rd at CSX Railroad Bridge Novi Rd to Brickscape Dr

0 1,500 3,000 6,000 9,000 Feet



Map Print Date: 3/14/25
Map Author: K. Blough

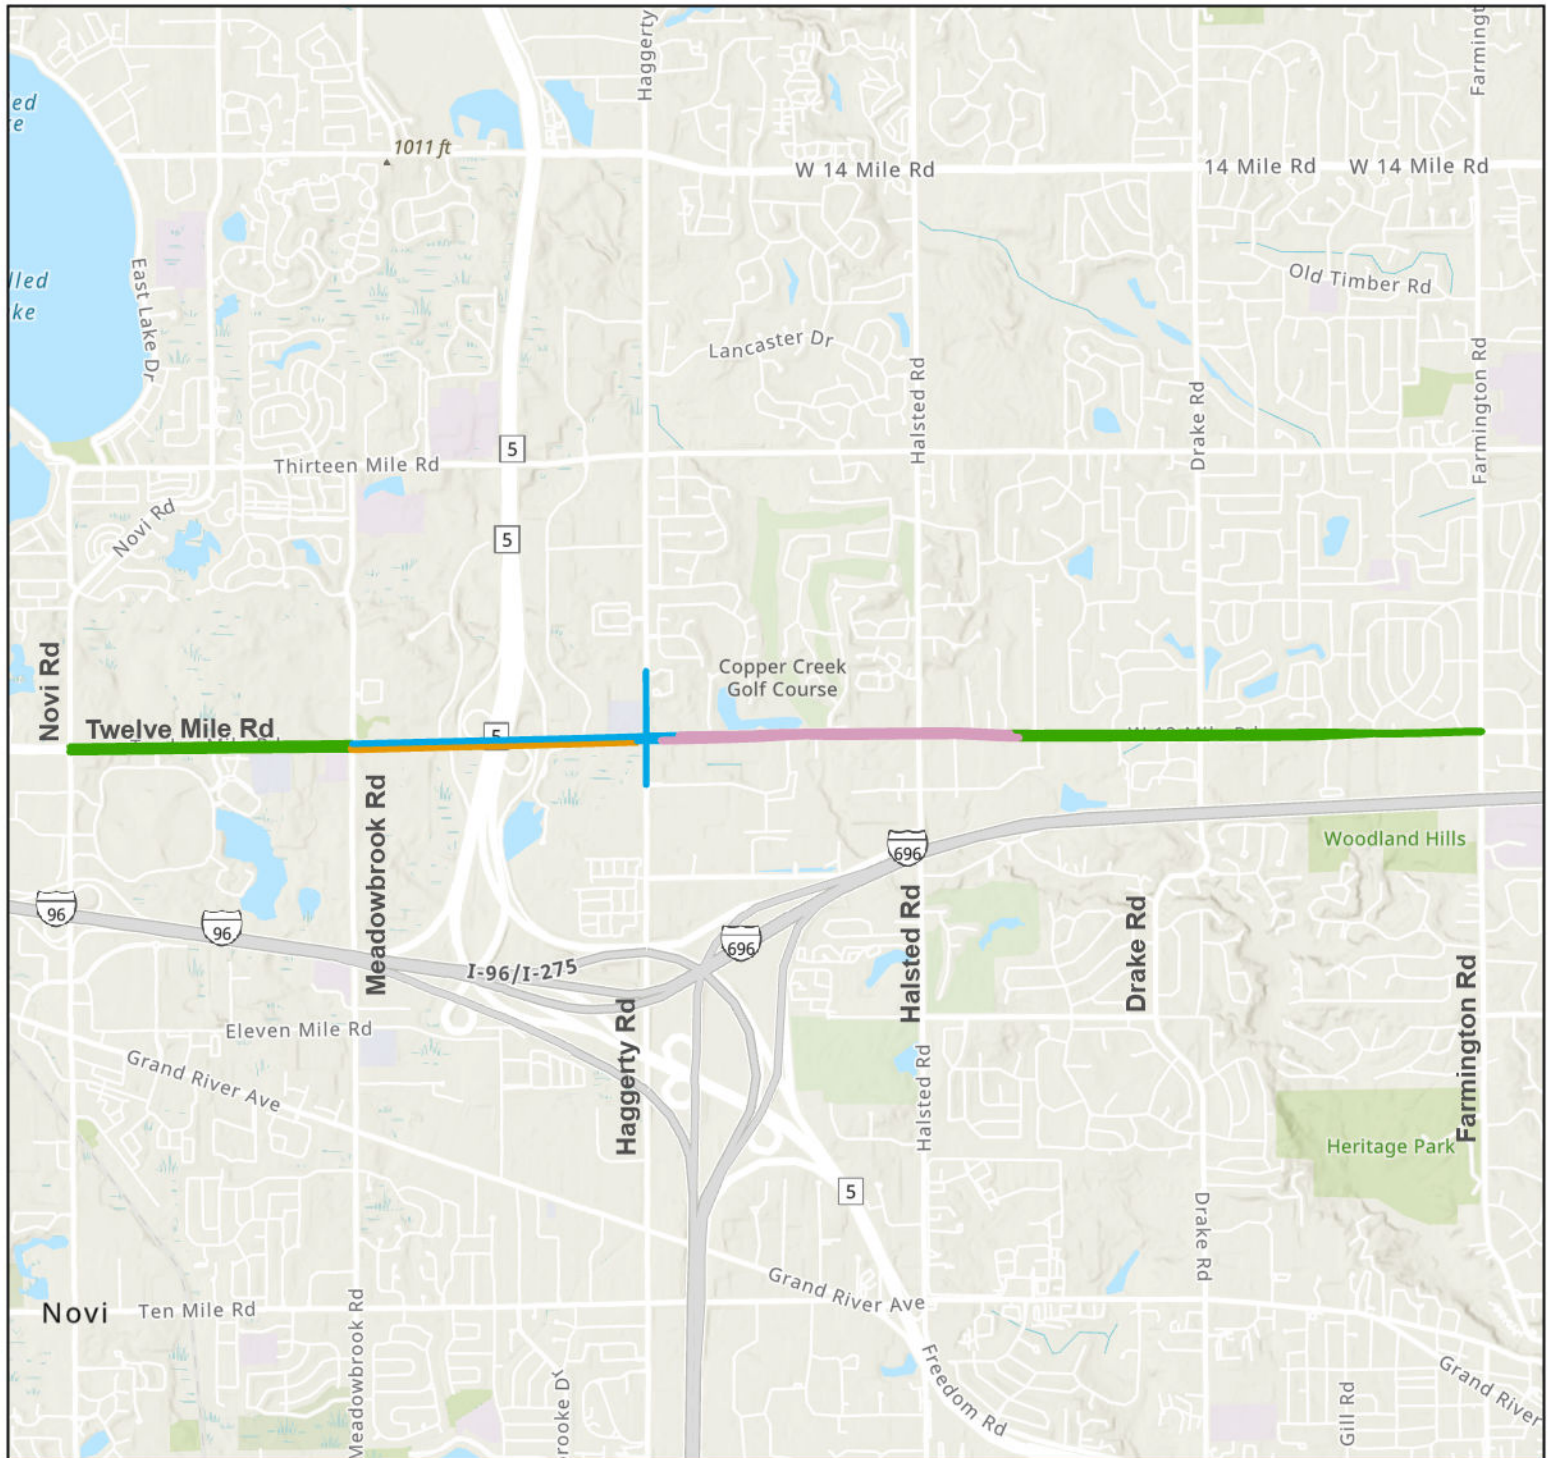

Staging Plan


- Stage 1 (Summer 2026): Novi Rd to Meadowbrook Rd & Investment Dr to Farmington Rd
- Stage 2 (Fall 2026): Eastbound from Meadowbrook Rd to Haggerty Rd
- Stage 3 (Spring & Summer 2027): Westbound from Meadowbrook Rd to Haggerty Rd & Haggerty Rd Intersection
- Stage 4 (Fall 2027): Haggerty Rd to Investment Dr



Twelve Mile Rd Rehabilitation Novi Rd to Farmington Rd



Map Print Date: 2/24/26
Map Author: K. Blough

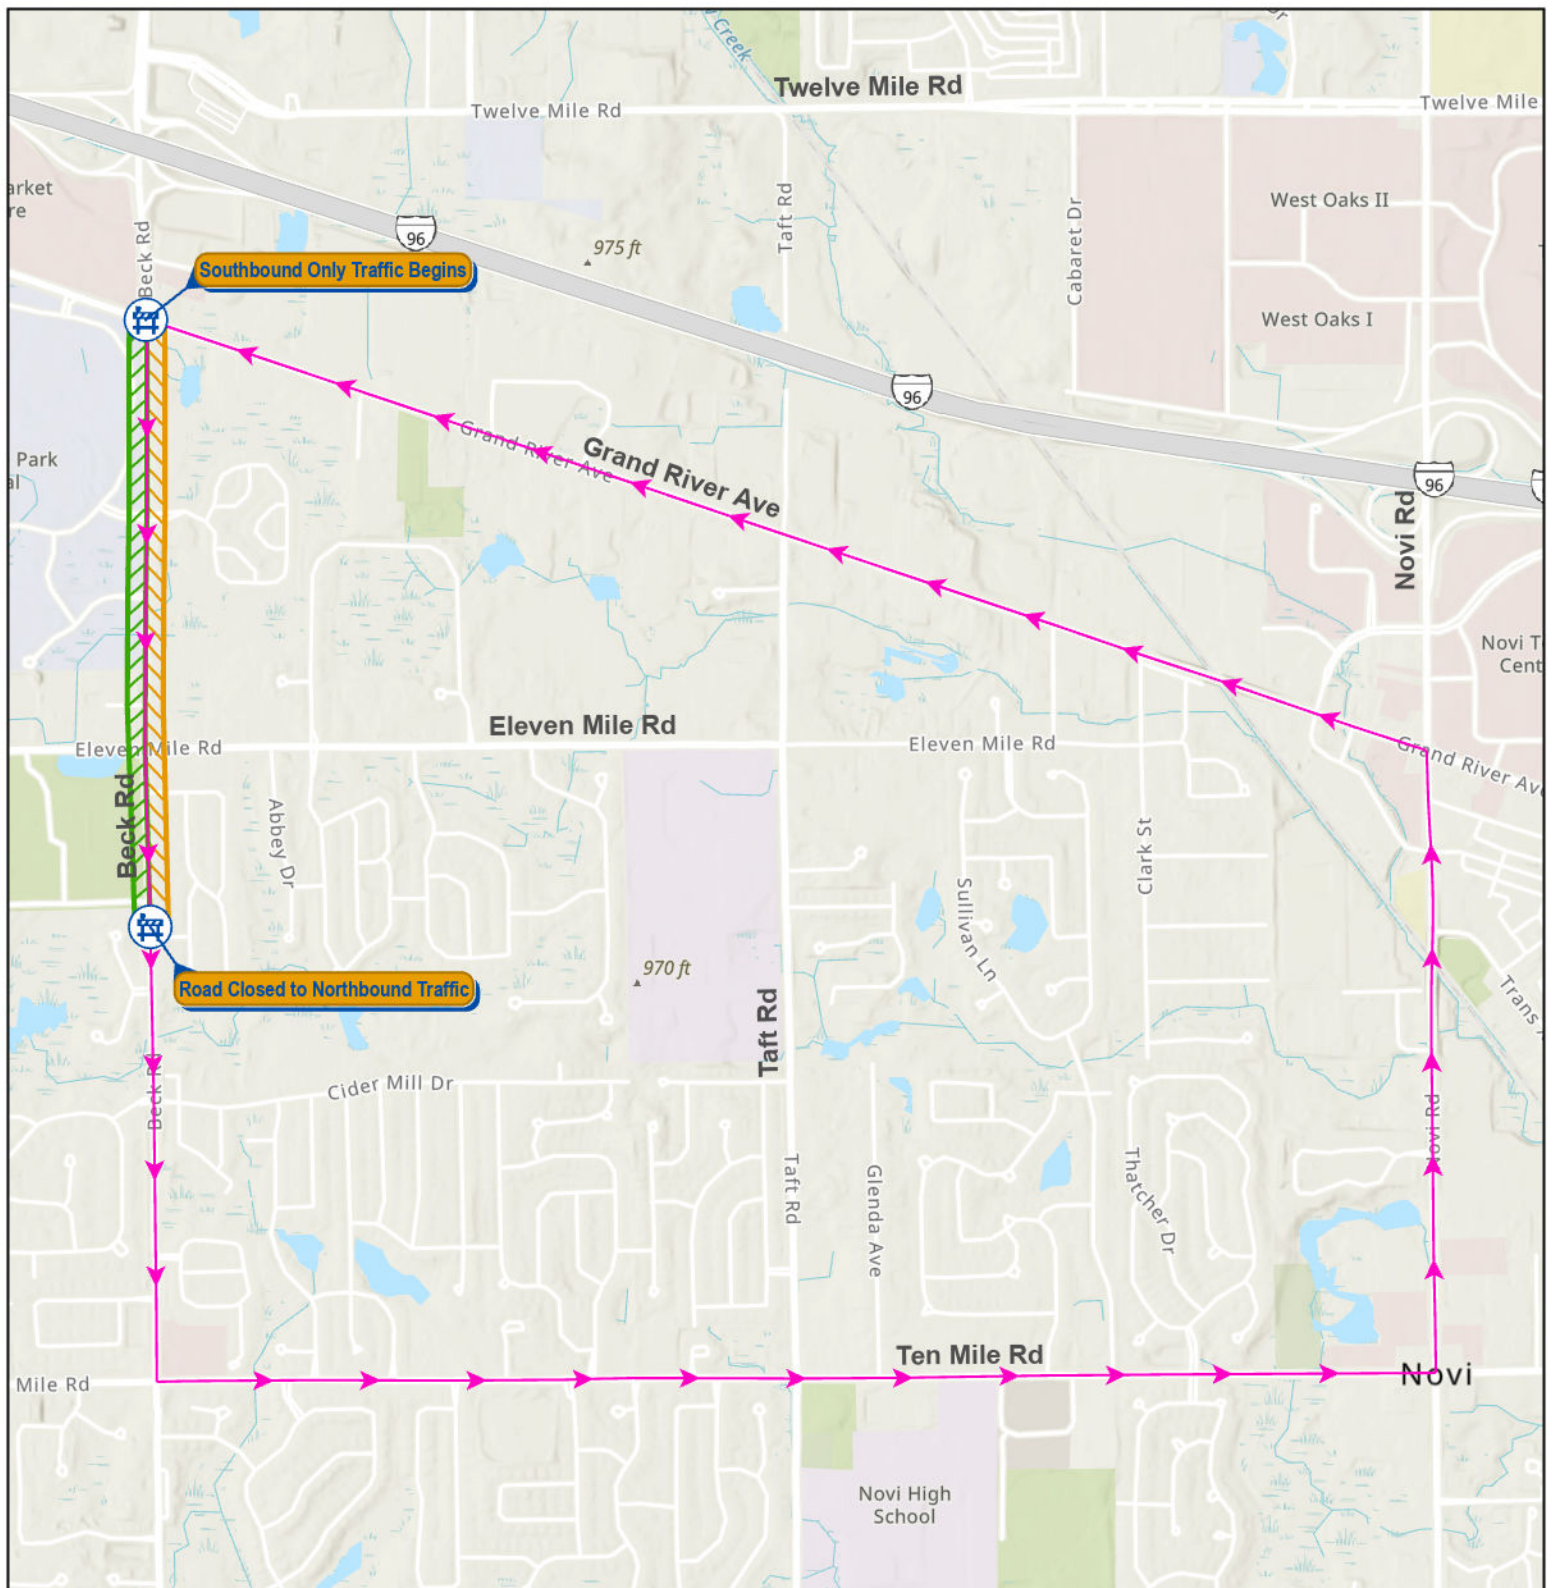

Beck Rd is **closed to northbound traffic** from Sanford Dr to Grand River Ave for the duration of this project.

Northbound traffic should navigate around this closure using 10 Mile Rd to Novi Rd to Grand River Ave and back to Beck Rd.

-  Detour Route
-  CLOSED to Traffic
-  OPEN to Traffic




Beck Road Widening 11 Mile Rd to Grand River Ave

0 800 1,600 3,200 4,800 Feet



Map Print Date: 4/7/26
Map Author: K. Blough

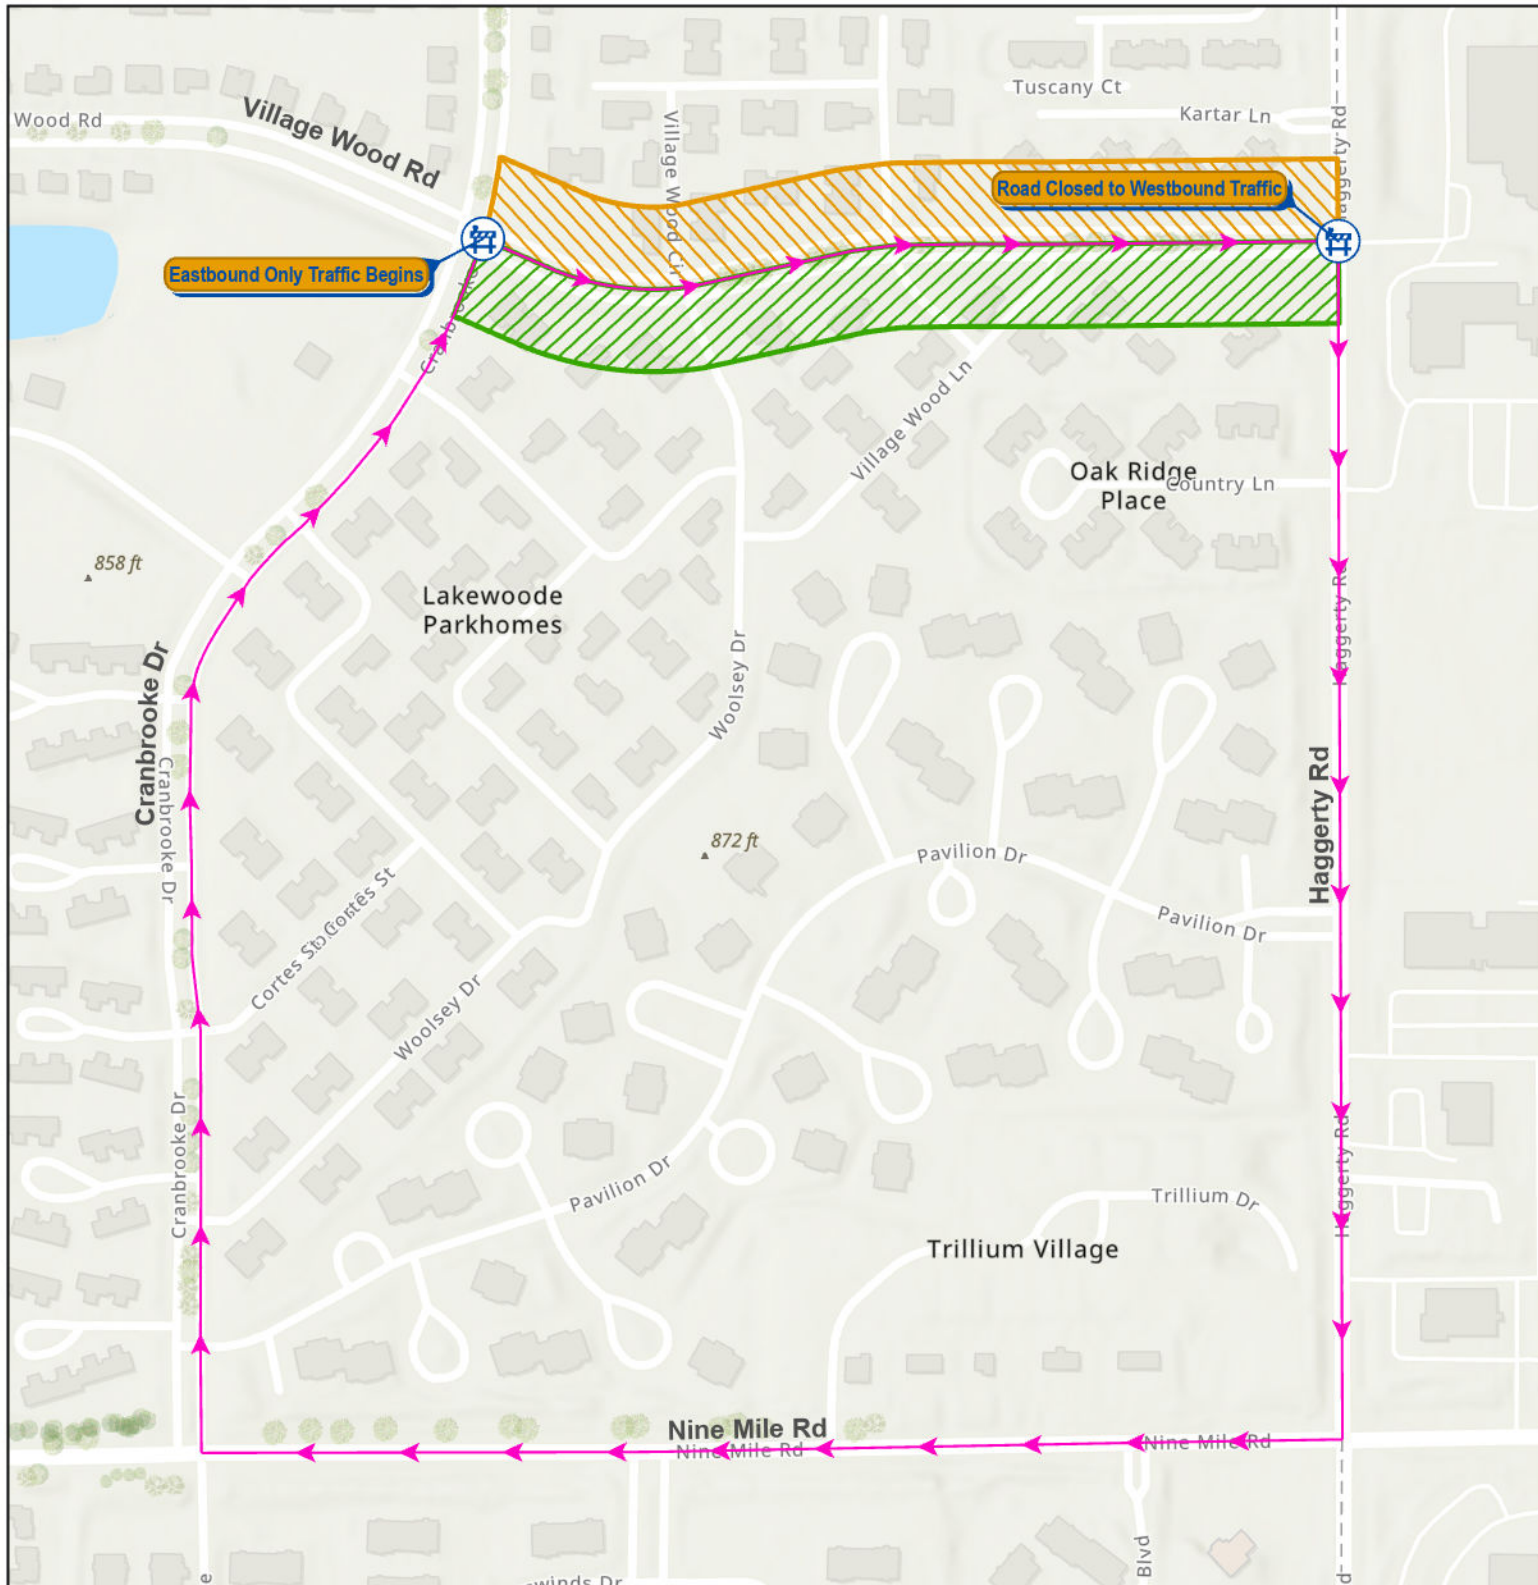

Village Wood Rd is **closed to westbound traffic** from Haggerty Rd to Cranbrooke Dr for the duration of this project.

Westbound traffic should navigate around this closure using Haggerty Rd to 9 Mile Rd to Cranbrooke Dr and back to Village Wood Rd.

-  Detour Route
-  CLOSED to Traffic
-  OPEN to Traffic



Village Wood Rd Reconstruction Cranbrooke Dr to Haggerty Rd

0 175 350 700 1,050 Feet



Map Print Date: 2/23/26
Map Author: K. Blough
