


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	May 2024												June 2024											
							30	2	4	6	8	10	12	14	16	18	20	22	24	26	28	30	1	3	5	7	9	11	13	15
1		<b>McCullough Creek Greenway (365 Days)</b>	262 days	Mon 1/8/24	Tue 1/7/25																									
2		Mobilization	5 days	Mon 1/8/24	Fri 1/12/24																									
3		Survey and Layout	2 days	Thu 12/21/23	Fri 12/22/23																									
4		Temp. Erosion Control	3 days	Thu 12/21/23	Mon 12/25/23																									
5		Demolition	1 day	Mon 4/1/24	Mon 4/1/24																									
6		Clearing and Grubbing	7 days	Wed 3/20/24	Thu 3/28/24																									
7		Rough Grading	20 days	Fri 3/29/24	Thu 4/25/24																									
8		Aggregate Base Course	3 days	Fri 4/26/24	Tue 4/30/24																									
9		Geogrid	3 days	Fri 4/26/24	Tue 4/30/24																									
10		Temporary Seeding	1 day	Wed 5/1/24	Wed 5/1/24	8,9																								
11		Prefabricated Bridge Pile Installation	20 days	Mon 8/19/24	Fri 9/13/24	8																								
12		Pile Encasement / CIP Concrete Abutments	15 days	Mon 2/17/25	Fri 3/7/25																									
13		Class B Rip Rap	1 day	Mon 3/10/25	Mon 3/10/25	12																								
14		Site Prep / Crane Pad	5 days	Wed 6/12/24	Tue 6/18/24																									
15		Bridge Delivery	1 day	Wed 6/19/24	Wed 6/19/24	14																								
16		Prefabricated Bridge Installation	2 days	Mon 3/24/25	Tue 3/25/25																									
17		CIP Bridge Deck	7 days	Wed 3/26/25	Thu 4/3/25	16																								
18		Boardwalk Framing (Neighborhood Side)	10 days	Tue 4/1/25	Mon 4/14/25																									
19		Galv. Angle / Deckpan	2 days	Tue 4/15/25	Wed 4/16/25	18																								
20		CIP Concrete Deck	2 days	Thu 4/17/25	Fri 4/18/25	19																								
21		Boardwalk Handrail (Neighborhood Side)	10 days	Tue 4/29/25	Mon 5/12/25																									
22		Boardwalk Framing (Park Side)	10 days	Tue 4/15/25	Mon 4/28/25																									
23		Boardwalk Handrail (Park Side)	20 days	Tue 5/13/25	Mon 6/9/25	21																								
24		6" Concrete Fiber Reinforced	2 days	Tue 6/10/25	Wed 6/11/25	23																								
25		Condition ABC	5 days	Thu 6/12/25	Wed 6/18/25	24																								
26		Asphalt Surface Course	3 days	Thu 6/19/25	Mon 6/23/25	25																								
27		Fine Grading and Backfill	5 days	Tue 6/24/25	Mon 6/30/25	26																								
28		Permanent Seeding	2 days	Tue 7/1/25	Wed 7/2/25	27																								
29		Pavement Marking Lines	1 day	Thu 7/3/25	Thu 7/3/25	28																								
30		Collapsible Bollard	1 day	Thu 7/3/25	Thu 7/3/25	28																								

Project: McCullough Greenway  
Date: Mon 2/10/25

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			




Project: McCullough Greenway  
Date: Mon 2/10/25

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			



Project: McCullough Greenway  
Date: Mon 2/10/25

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

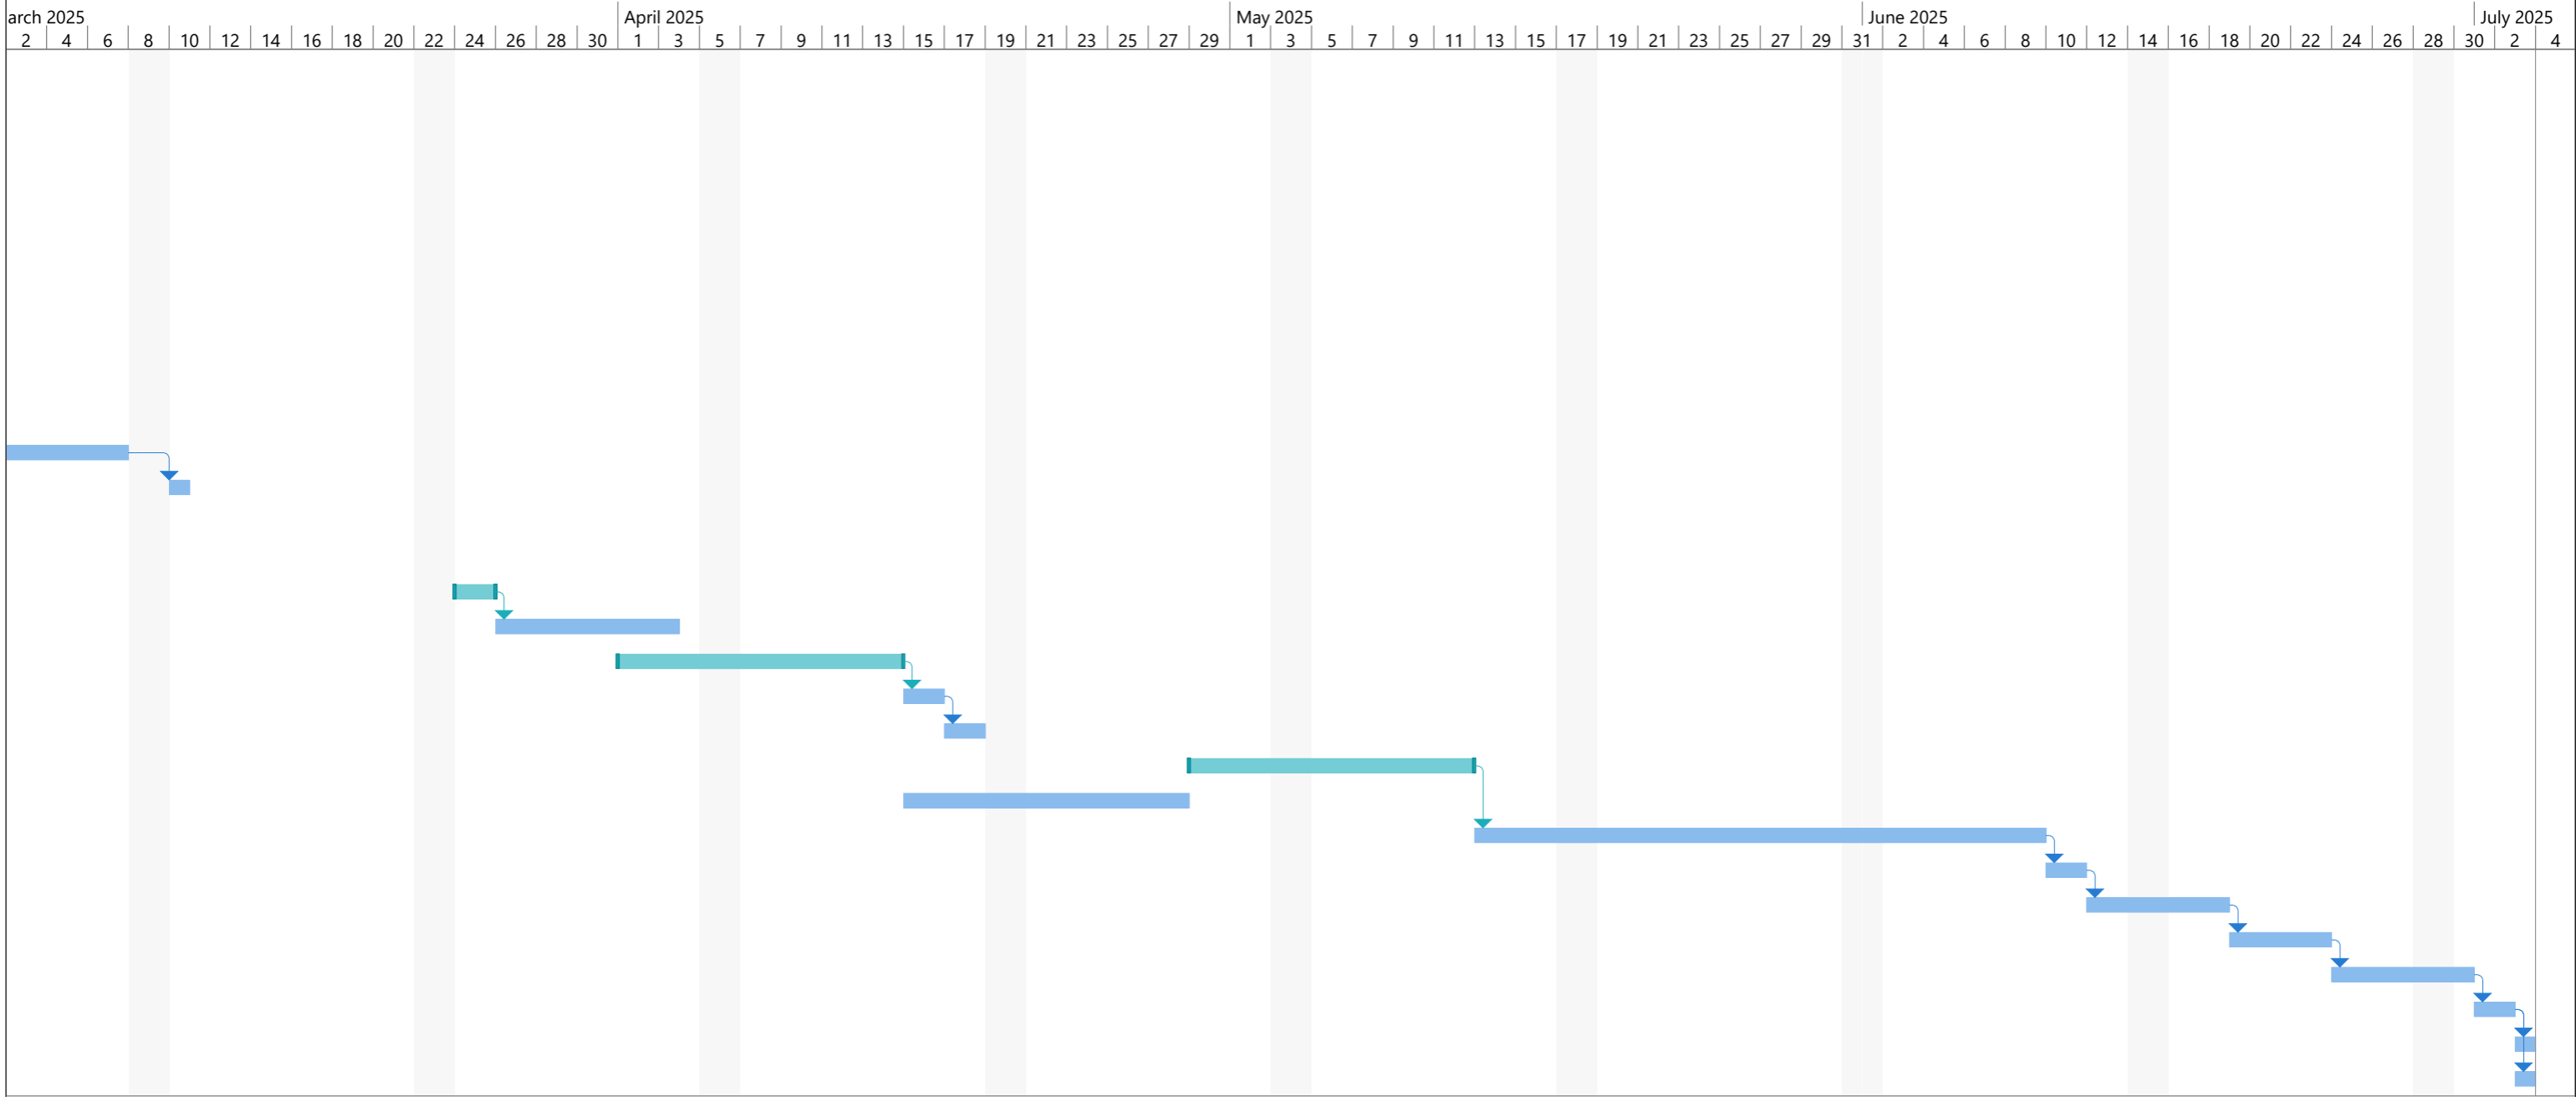

Project: McCullough Greenway  
 Date: Mon 2/10/25

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
