


Jane's Place Construciton Schedule

ID	Task Mode	Task Name	Duration	Start	Finish	3rd Quarter Jul Aug Sep Oct Nov Dec	4th Quarter Jan Feb Mar Apr May Jun	1st Quarter Jul Aug Sep Oct Nov Dec	2nd Quarter Jan Feb Mar Apr May Jun	3rd Quarter Jul Aug Sep Oct Nov Dec	4th Quarter Jan Feb Mar Apr May Jun	1st Quarter Jul Aug Sep Oct Nov Dec	2nd Quarter Jan Feb Mar Apr May Jun
1		Entitlements/Permitting	1 day?	8/22/22	8/22/22								
2		Land Closing (Title Change)	1 day	8/22/22	8/22/22								
3		City Council Approval (DIA/Mylars)	1 day	9/6/22	9/6/22								
4		Building Permit Submittal	1 day	9/9/22	9/9/22								
5		Building Permit Review	6 wks	9/12/22	10/21/22								
6		Bldg. Permit Issued	1 day	10/24/22	10/24/22								
7		Preconstruction	67 days	8/4/22	11/4/22								
8		Contractor RFP	27 days	8/4/22	9/9/22								
9		Contractor Selection	3 wks	9/12/22	9/30/22								
10		VE Pricing & System/Material Input	4 wks	10/3/22	10/28/22								
11		Finalize GMP w/ Contractor	1 wk	10/31/22	11/4/22								
12		Construction	403 days	11/7/22	5/22/24								
13		Notice to Proceed	1 day	11/7/22	11/7/22								
14		Mobilize to Site	1 day	11/22/22	11/22/22								
15		Construction Activity	18 mons	11/23/22	4/9/24								
16		Substantial Completion	1 day	4/10/24	4/10/24								
17		Final Completion	30 days	4/11/24	5/22/24								

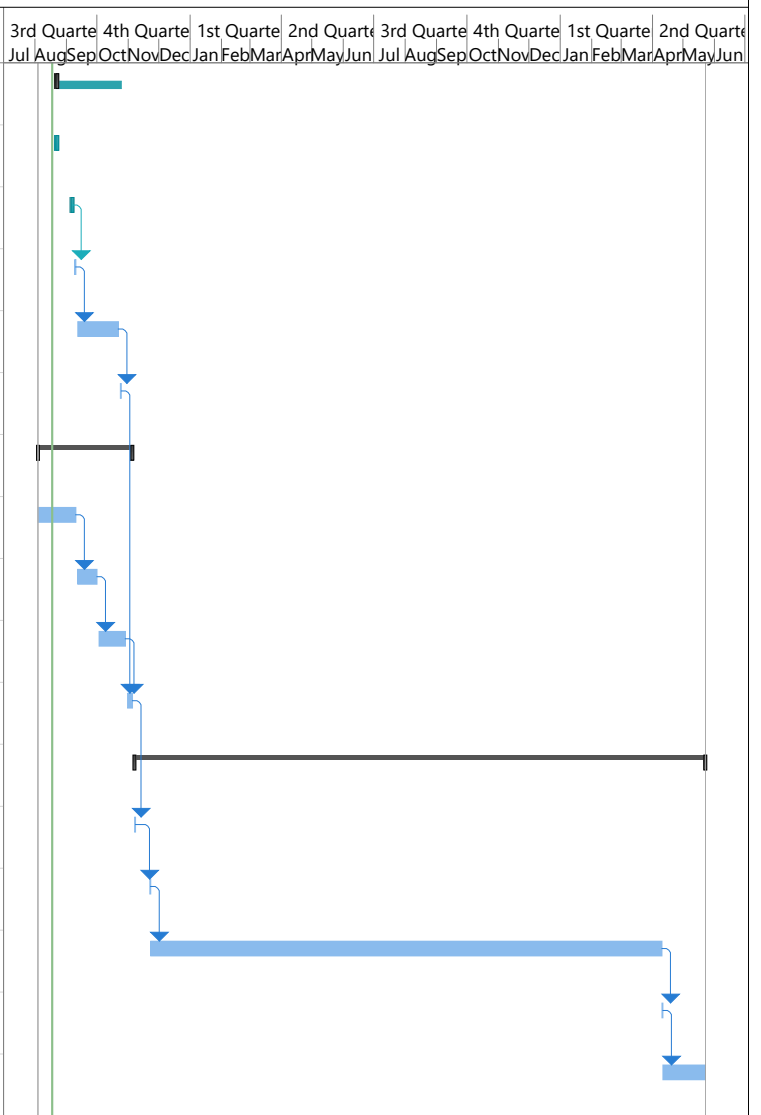

Project: 22.08.18 Jane's Place P Date: 8/18/22	Task		Inactive Task		Manual Summary Rollup		External Milestone	
	Split		Inactive Milestone		Manual Summary		Deadline	
	Milestone		Inactive Summary		Start-only		Progress	
	Summary		Manual Task		Finish-only		Manual Progress	
	Project Summary		Duration-only		External Tasks			
