



Council Work Session City Engineer Update

March 14, 2022

Street Paving Update

- **2021 Paving**
 - All Streets Paved
 - Permanent striping pending (03/11/22)
 - Street loop installation pending (03/11/22)


- **2022 Paving**
 - ITB Released on 03/10/22
 - Bids Due on 04/11/22
 - Anticipated Council Agenda on 04/25/22
 - Anticipated NTP 05/09/22

Transportation Master Plan Update

- **Freight Cluster Study Update**
 - Application to ARC: 07/16/2021
 - Awarded by ARC: 08/31/2021
 - Anticipated NTP from ARC: April or May 2022
 - Total Cost: \$312,500
 - ARC Grant: \$250,000
 - City Match (20%): \$62,500 (2022 SPLOST)
 - Anticipated RFQ Release by City: April 2022

Transportation Master Plan Update

■ Freight Cluster Study Update

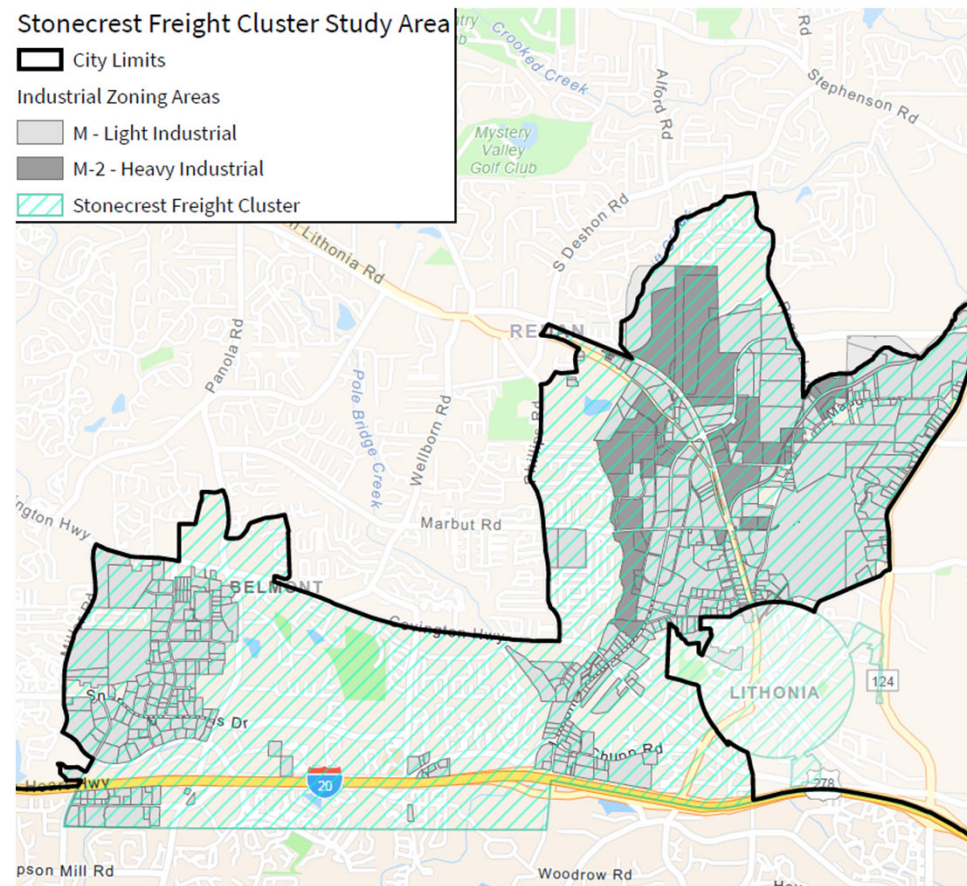

Transportation Master Plan Update

- **Panola Road Scoping Study**
 - Browns Mill Road to Fairington Road
 - DeKalb County will manage the Study
 - Council Agenda: 03/11/22
 - Study Cost: \$290,000
 - Stonecrest Cost (50%): \$145,000 (2022 SPLOST)
 - Anticipated NTP from County: 03/15/2022
 - Anticipated completion: 03/15/2023

City Maintenance

- **Continue to send work orders to the City, several pending**
(Potholes, Guardrails, Signals, Signs, Ponds & Litter)
- **Managing City Maintenance Contractor**
(Mowing & Litter pick-up)
- **Right-of-way Maintenance service bids pending**
(Mowing, Pond Maintenance, Trash removal)
- **Keep DeKalb Beautiful Work orders are current**

Other Updates

- **Working on SPLOST allocation updates**
- **Supporting Land Development activities**
 - Pre-Application Meetings**
 - February – 6**
 - March - 6**

Questions:

Hari Karikaran, PE
City Engineer
(770) 316-1076
