

# Animal Services Renovation Update




**Phase one was completed on March 3, 2025**


**Phase two is anticipated to take 4 weeks.**

# Animal Services Phase One Renovation

ORIGINAL FLOOR PLAN

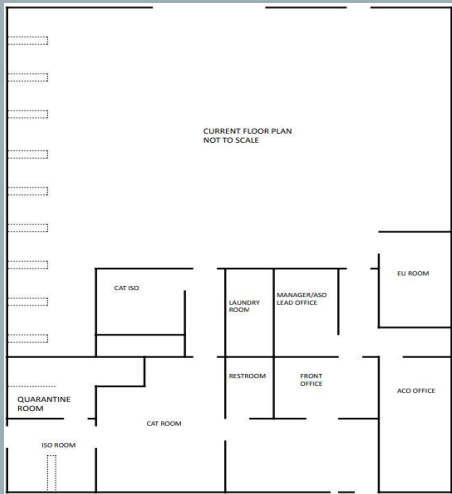

NEW FLOOR PLAN

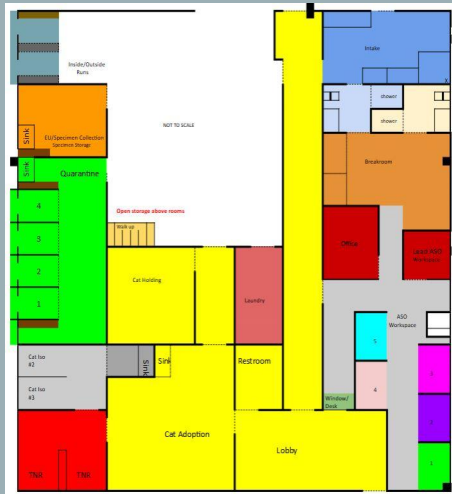

Demolition began September 16, 2024. Phase one was the most complex portion of the project.

Extensive demolition, HVAC, and plumbing were required.



Phase One Areas of Construction



# Animal Services Phase One Renovation



- Garage Door Resize
- Create a Public Walkway from the Lobby to the Dog Building
- Create Staff Workstations and Private Office
- Create Staff Break Room and Bathrooms
- Create Animal Intake Room
- Maintain and expand the project's connectivity, fire, and security.



Walkway Lobby to Kennels



Staff Workstations Reception Desk




Breakroom



Phase one was stalled entirely due to a fire safety plan submission error between the contractor and vendor. To limit the time required for the project to be completed, areas of phase two have been started, expanding the pre-defined construction area of phase one.



# Animal Services Phase Two Renovation Scope

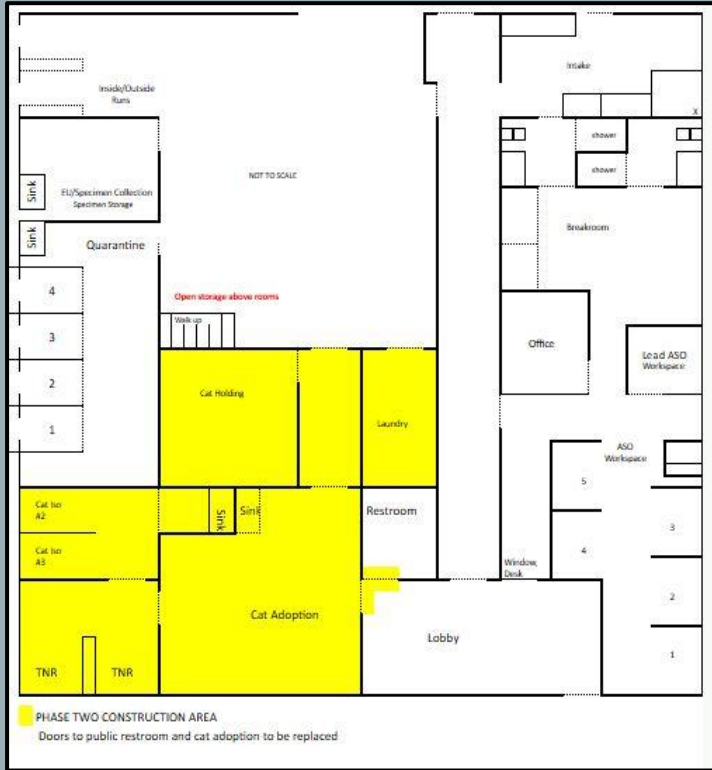

## Cat Adoption

- Replace Wooden Entry Door
- Remove FRP
- Epoxy Paint Walls, Grind Floors, Stain and Seal Concrete Floors
- Install Hot and Cold Water Deep Sink
- Remove Large Exposed Water Heater & Relocate to Laundry Area

## Cat Holding & Walkway

- Epoxy Paint Walls, Grind Floors, Stain and Seal Concrete Floors

## Trap Neuter Release Program Area

- Create Two Isolated and Designated TNR Program Kennels
- Install Custom Doors for Disease Control
- Remove and Replace FRP
- Grind and Seal Concrete Floors

## Cat Isolation

- Create Two Sick Isolation Kennels with Designated Air System
- Install Hot and Cold Water Deep Sink in Room
- Install Two Custom Doors for Disease Control
- Grind and Seal Floors

- Replace/Reconfigure Key Card Access and Video Security
- Refresh all areas

Phase two is anticipated to be completed by  
April 1, 2025.
