


# ANIMAL SHELTER ADVISORY COMMITTEE

August 9, 2022

## ANIMAL ISOLATION AREA EXPANSION



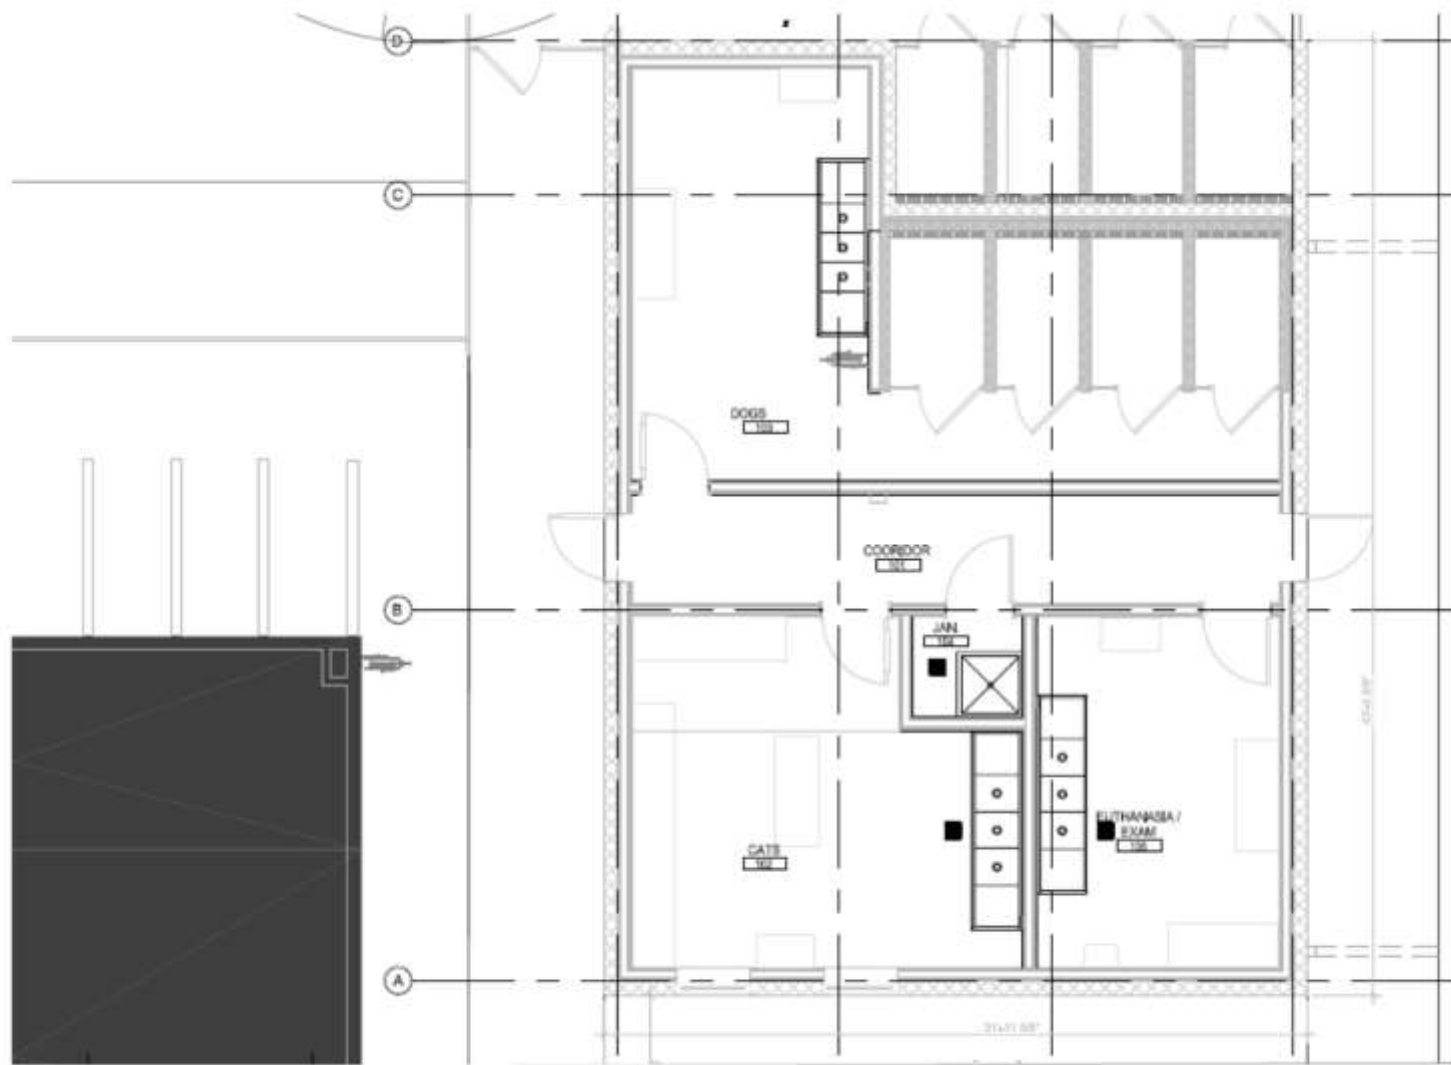



# STATUS OF CONSTRUCTION



MARCH

Foundation complete



APRIL - MAY

Materials back ordered



JUNE

Exterior walls complete



JULY

Interior walls framed

# TIMELINE





# PROGRESS PHOTOS



16 PIERS



PLUMBING



FLOOR DRAINS



ROOM STRING LINES

# PROGRESS PHOTOS



**FOUNDATION  
PREP**

February 28, 2022



**FOUNDATION  
CARDBOARD VOID  
FORMS**

March 1, 2022



**FOUNDATION  
REBAR AND SLIP  
PLASTIC SHEETING**

March 2, 2022



**FOUNDATION  
TROWELING**

March 4, 2022



**COMPLETED  
FOUNDATION**

March 4, 2022



# PROGRESS PHOTOS



**CMU BLOCK GOING UP**

June 15, 2022



**KENNELS BEING BUILT**

June 30, 2022



**KENNELS INSIDE**

July 3, 2022



**INSULATION INSTALLED**

July 8, 2022



**INSULATION**

July 8, 2022



# PROGRESS PHOTOS



**PLUMBING IN WALLS**

July 12, 2022



**PLUMBING**

July 12, 2022



**ELECTRICAL**

July 25, 2022



**OUTSIDE**

July 25, 2022

## QUESTIONS/COMMENTS



LISA DUELLO  
NEIGHBORHOOD SERVICES DIRECTOR  
817-426-9841  
[lduello@burlesontx.com](mailto:lduello@burlesontx.com)

