




NW Astor St / NW 23rd Sidewalk Improvements Project Summary

Project Type: Street

Total Project Cost: \$135,042.85

Project Timeline: December 2022-January 2023

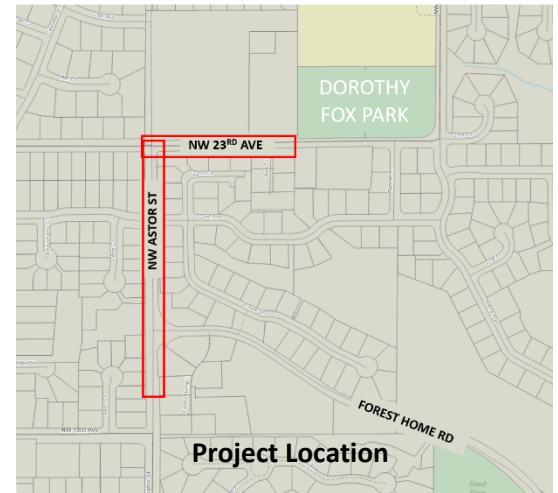

Project Description

Work consisted of the removal and replacement of uneven and steep sidewalks along NW Astor St. and NW 23rd Ave. Sidewalks had been affected by tree roots outgrowing the existing narrow planter strip. Work included removal of invasive trees and planting of new trees with root protection system.

Project Details and Benefits

- Design of the project was completed by in-house Engineering staff.
- Sidewalk conditions had been a safety hazard for many years.
- New sidewalks benefit all pedestrians through the neighborhoods, especially those with mobility challenges.
- Tree selection and root protection installed will increase longevity of sidewalks.

Project Funding

Project Phase	Year	Street Fund	Total
Design (By City Staff)	2022		
Construction	2022-2023	\$135,043	\$135,043
Total		\$135,043	\$135,043
Original Budget Estimate (Construction Only)		\$157,123	



Before



After
