




# NW Sierra Street Pavement & ADA Improvements

NW 43<sup>rd</sup> AVE to NW 36<sup>th</sup> AVE  
 NW 28<sup>th</sup> AVE to NW 23<sup>rd</sup> AVE

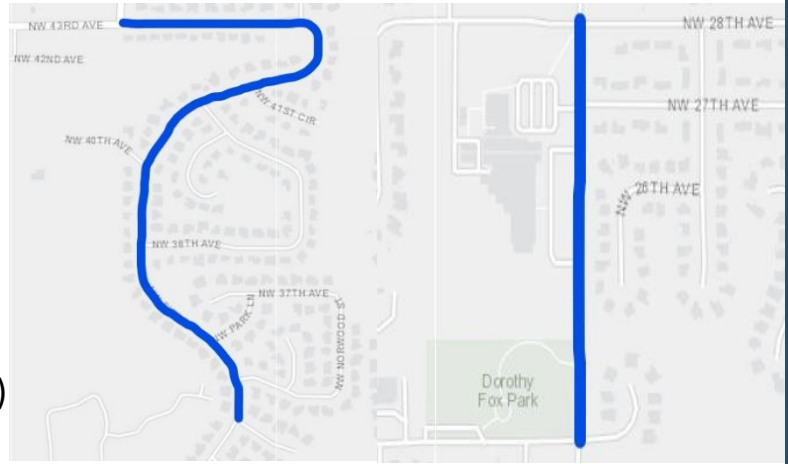

NW 43<sup>rd</sup> AVE to NW 36<sup>th</sup> AVE

NW 28<sup>th</sup> AVE to NW 23<sup>rd</sup> AVE

Project Type: Pavement Preservation (Streets)  
 Total Project Cost: \$1,414,035  
 Project Timeline: July 2022-Oct 2022

## Project Description

This project was part of 2022 Pavement Preservation Program. Two segments of NW Sierra Street’s asphalt surfacing were replaced while bringing pedestrian facilities up to current ADA Standards.

## Project Details and Benefits

- Extended life of a major collector route.
- Improved ADA curb ramps and pedestrian access.
- Revised roadway marking layout improves sight distance and assists with speed control.
- Value Engineering principals utilized on NW 43<sup>rd</sup> AVE to NW 36<sup>th</sup> AVE equated to \$76,400 bid item savings on asphalt while increasing roadway structural section to current arterial standards.
- Remaining section (NW 36<sup>th</sup> AVE to NW 28<sup>th</sup> AVE) of Sierra will be completed summer of 2023.

## Project Funding

Project Phase	Year	Street’s Pavement Preservation	Total
Design (HHPR Inc.)	2022	\$114,315	\$114,315
Construction	2022	\$1,299,720	\$1,299,720
<b>Total</b>	<b>2022</b>	<b>\$1,414,035</b>	<b>\$1,414,035</b>
Original Budget Estimate		\$1,205,213	\$1,205,213

