

City Council Meeting
June 20, 2023

COLUMBUS CITY HALL UPDATE




COLUMBUS CITY HALL

PHASE I TIMELINE

- Certificate of Occupancy obtained June 9, 2023
- Final cleaning, furniture relocation, and closeout activities ongoing.
- Moving activities tentatively scheduled to begin the week of June 19, 2023. All departments tentatively scheduled to be relocated by the end of July 2023.

Department	Current Location	Relocating to	1 st Day in New Location (Subject to Change)
Information Technology	5th Floor, Government Center	Development Resource Center - 2nd Floor	June 21st
Finance	5th Floor, Government Center	Development Resource Center - 1st Floor	June 23rd
UGA Cooperative Extension	Annex	Development Resource Center - 1st Floor	June 29th
Job Training Division	Annex	Development Resource Center - 2nd Floor	June 28th
Parks & Recreation	Citizen Service Center	Development Resource Center - 2nd Floor	June 29th
Human Resources	East and West Wing Government Center	Human Resources Building - 1st Floor and 2nd Floor	July 5th
Mayor's Office	6th Floor, Government Center	Development Resource Center - 3rd Floor	July 18th
City Manager's Office	6th Floor, Government Center	Development Resource Center - 3rd Floor	July 18th
City Attorney's Office	6th Floor, Government Center	Development Resource Center - 3rd Floor	July 18th
Clerk of Council's Office	6th Floor, Government Center	Development Resource Center - 3rd Floor	July 18th
311 Citizen Services Center	Citizen Service Center	Development Resource Center - 1st Floor	July 18th

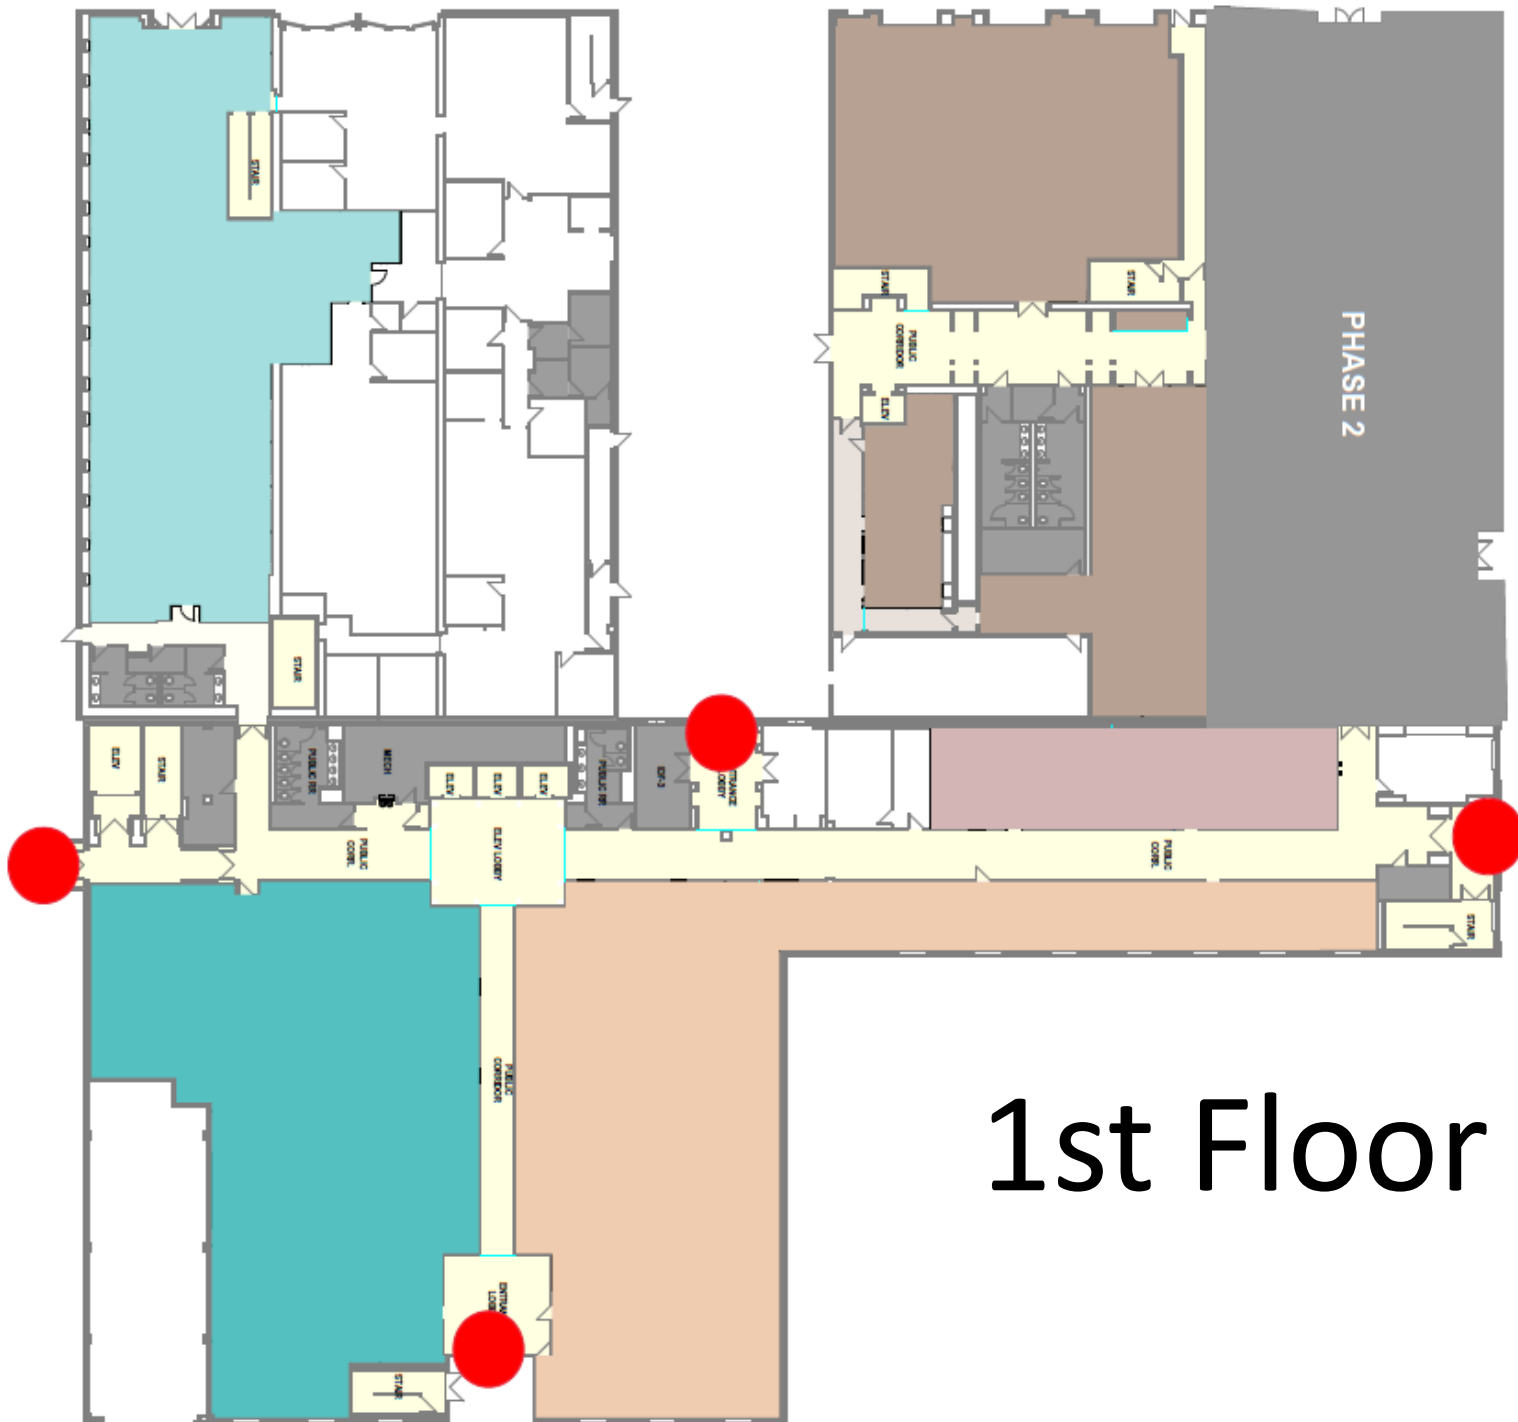


DEPARTMENT

-  PUBLIC CIRCULATION
-  BUILDING SUPPORT
-  311 Citizen Service Center
-  HUMAN RESOURCES
-  FINANCE
-  COOPERATIVE EXTENSION
-  WELLNESS CENTER
-  FOR FUTURE USE



1st Floor

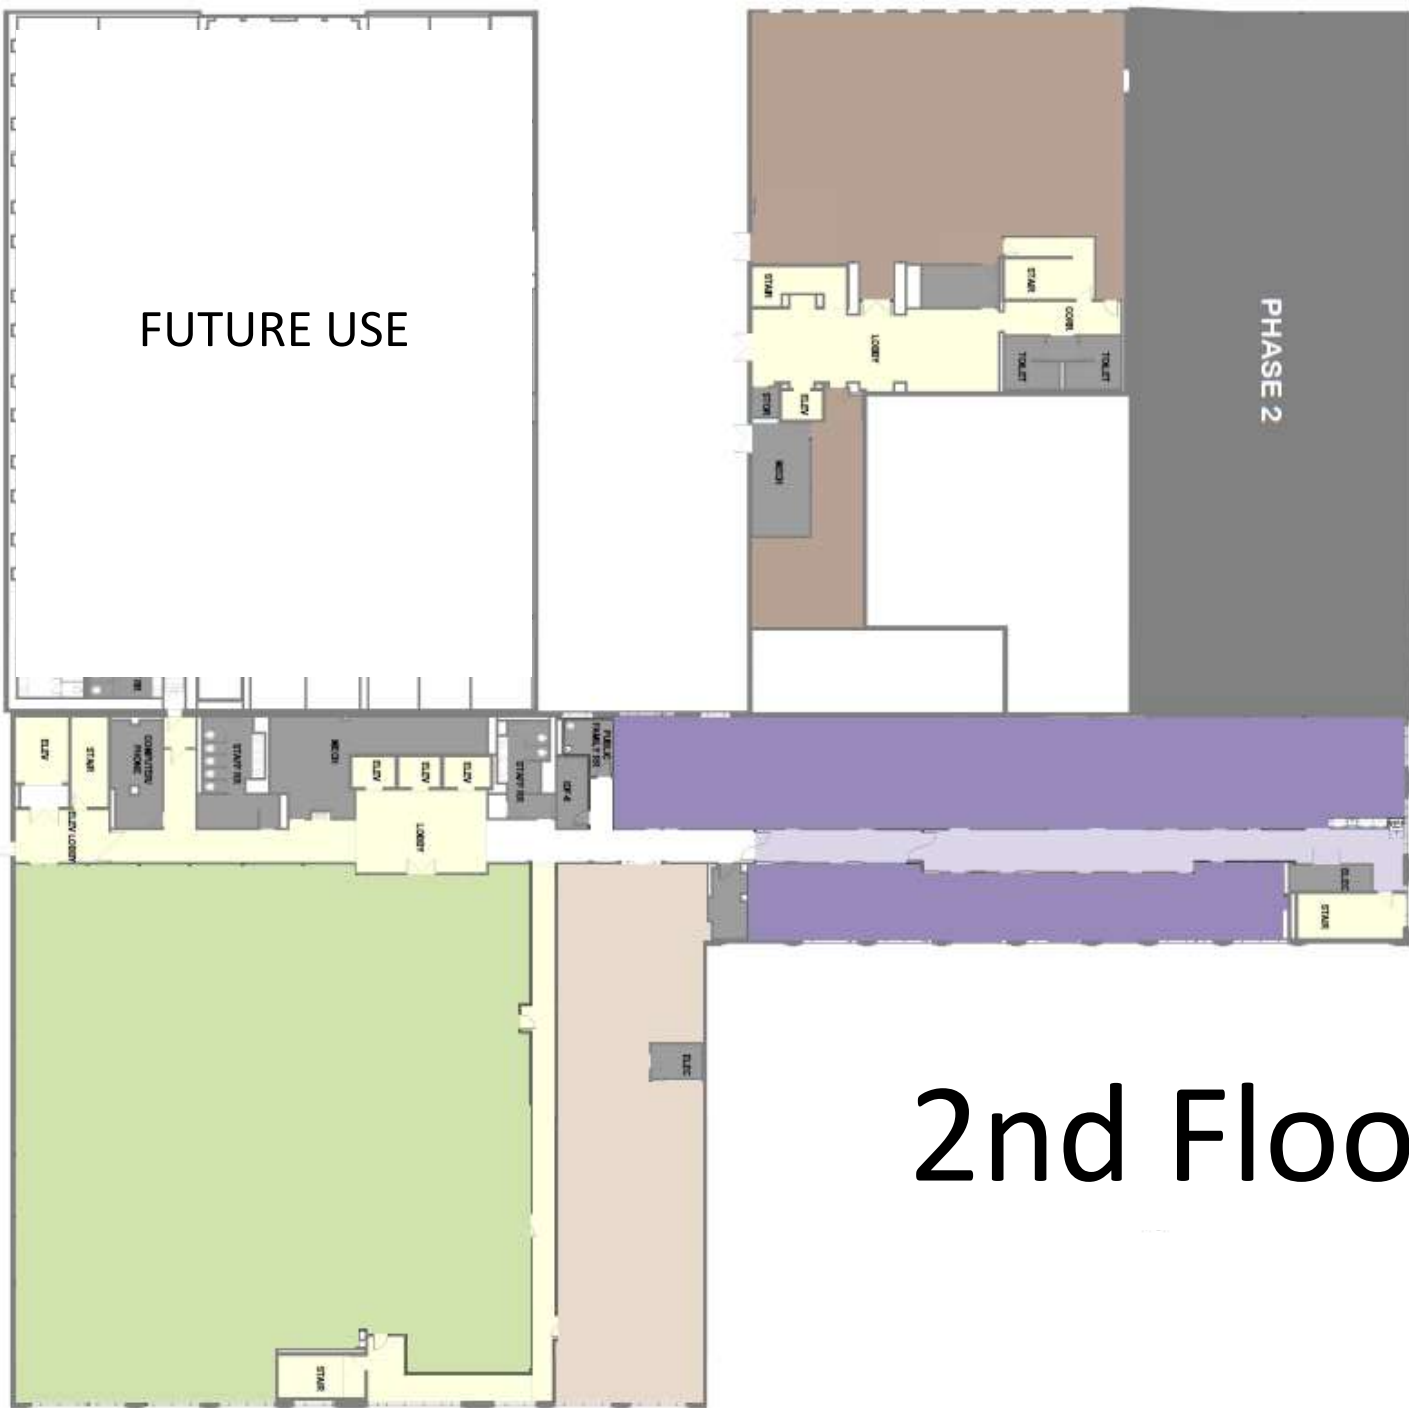

DEPARTMENT

- PUBLIC CIRCULATION
- BUILDING SUPPORT
- INFORMATION TECHNOLOGY
- HUMAN RESOURCES
- JOB TRAINING
- PARKS & RECREATION

2nd Floor





3rd Floor

- DEPARTMENT
- PUBLIC CIRCULATION
 - BUILDING SUPPORT
 - City Attorney's Office
 - Mayor's Office
 - City Manager's Office
 - Clerk of Council's Office

















PHASE II TIMELINE

- Synovus vacates Executive Building – July 31, 2024
- Renovation of Executive Building – August 2024 – March 2025
- Phase 2 Relocations - 2025
 - Mayor’s Office – 5th Floor of the Executive Building
 - City Manager’s Office – 4th Floor Executive Building
 - City Attorney’s Office – 3rd Floor Executive Building
 - Clerk of Council’s Office – 2nd Floor Executive Building
 - Engineering Department, Inspections & Code Department, Planning Department, Community Reinvestment Department - 3rd Floor Development Resource Center
 - Finance Department-Revenue Division – 1st Floor Executive Building
 - Print Shop – Basement of Broadway South Building

QUESTIONS
