

**COlumbus**

**GEORGIA**



**We do amazing.**


# GOLDEN PARK UPDATE

April 9, 2024

# GOLDEN PARK TIMELINE

- ▶ February 27, 2024 – City Council authorized execution of Design-Build Contract with Brasfield & Gorrie. City Council also authorized the issuance of a limited notice to proceed not to exceed \$750,000.
- ▶ February 29, 2024 – Brasfield & Gorrie was issued the notice to proceed to begin design and construction service activities.
- ▶ March 11, 2024 – Demolition permit applied for the selective demolition of portions of two structures in right field as well as parts of the existing stadium. Demolition permit was issued 03/13/2024
- ▶ March 26, 2024 - Site Development permit was applied for; application remains under review.

# SITE PLAN

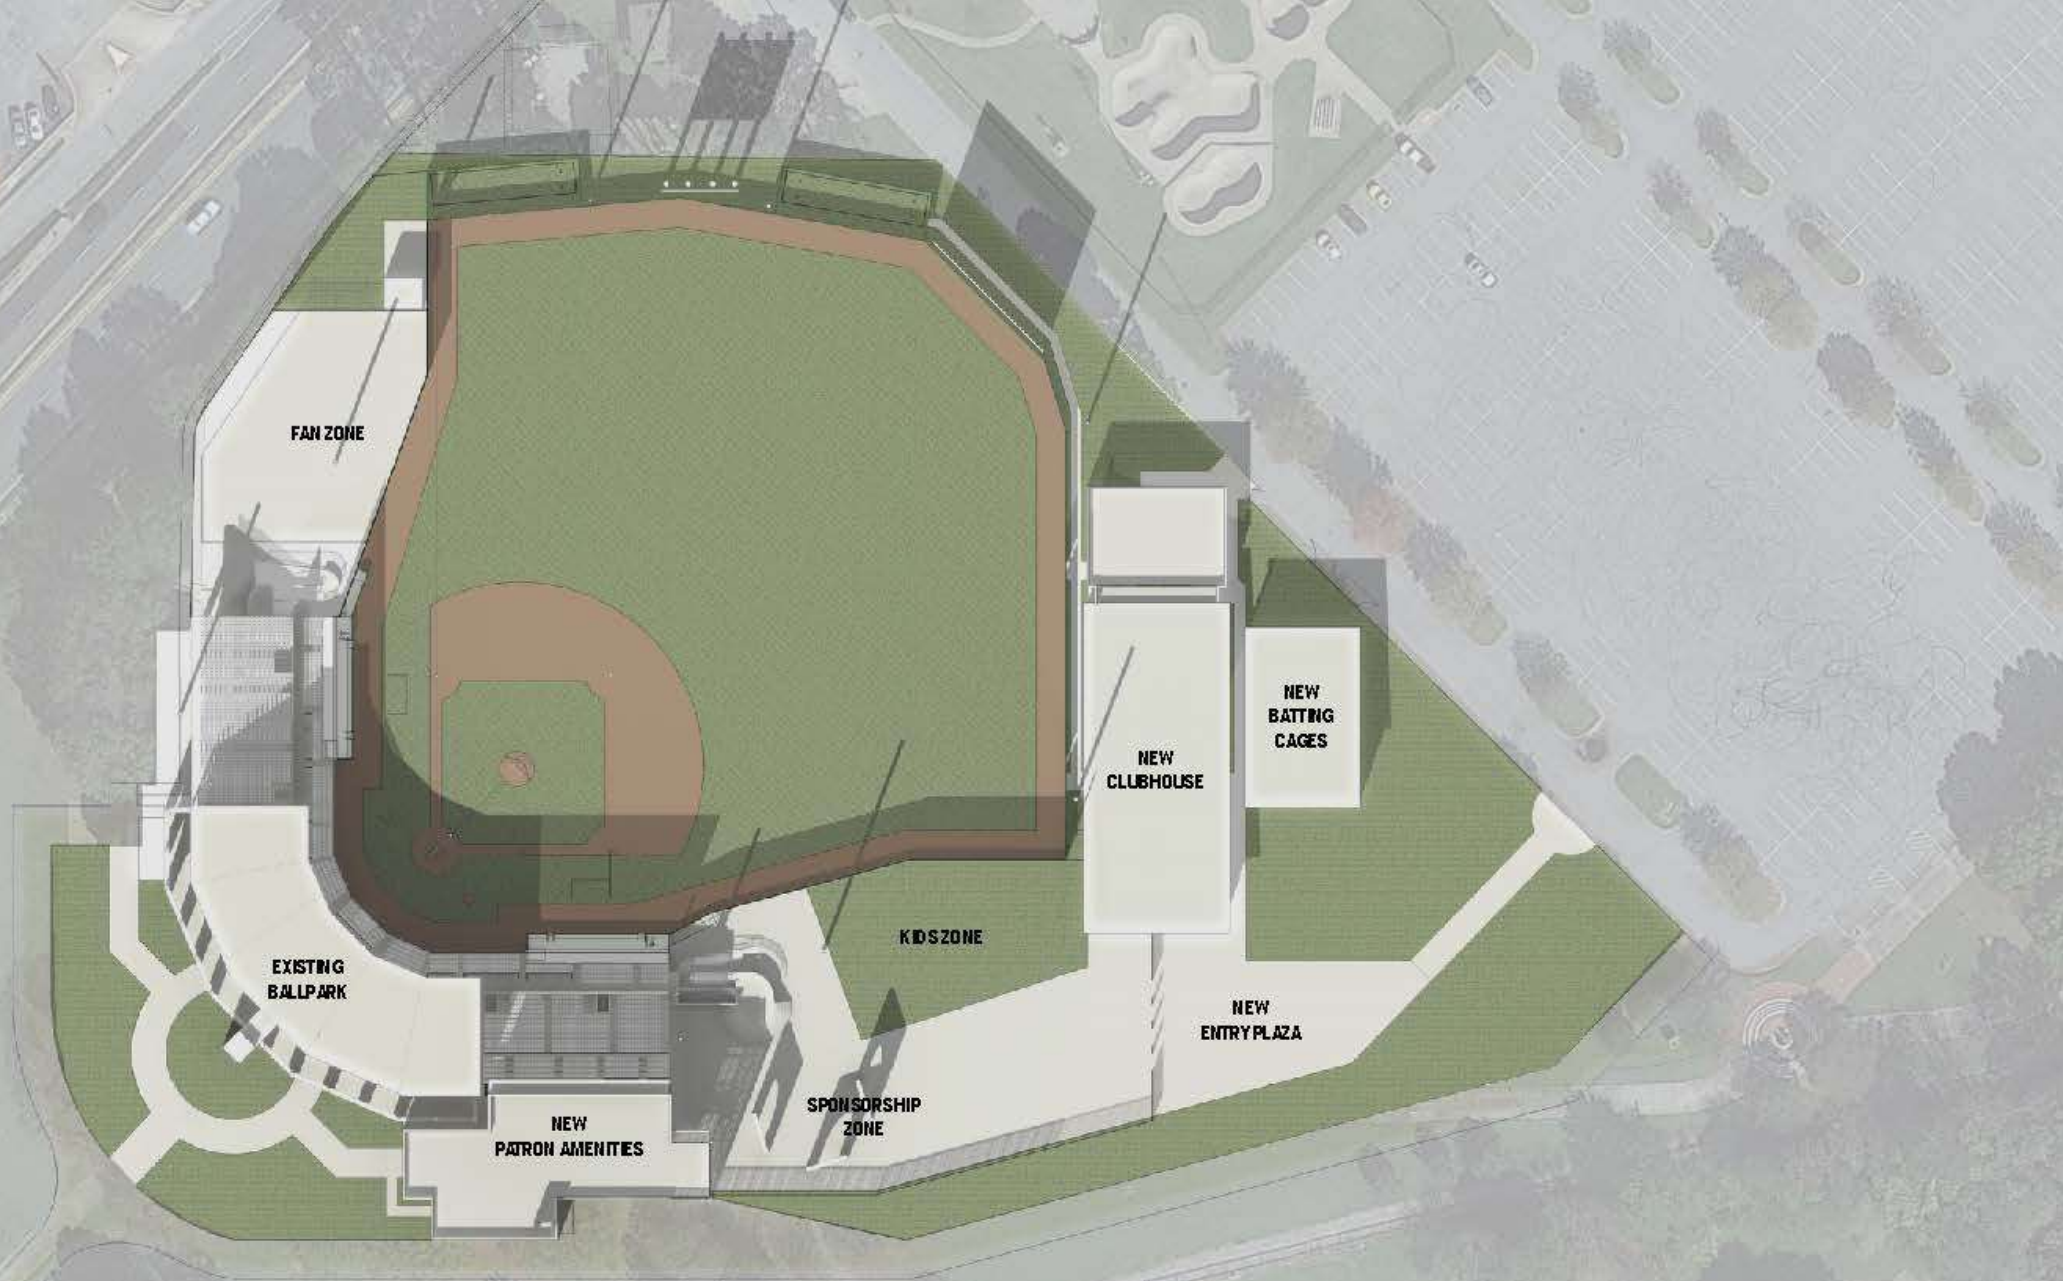


CONCEPT ONLY; SUBJECT TO CHANGE



# GOLDEN PARK TREE PLAN

- ▶ A tree plan has been developed and submitted as part of site development application.
- ▶ Plan is being reviewed by City Staff and revisions will be made, as necessary.
- ▶ Final location of trees will be updated after final completion of other design activities.

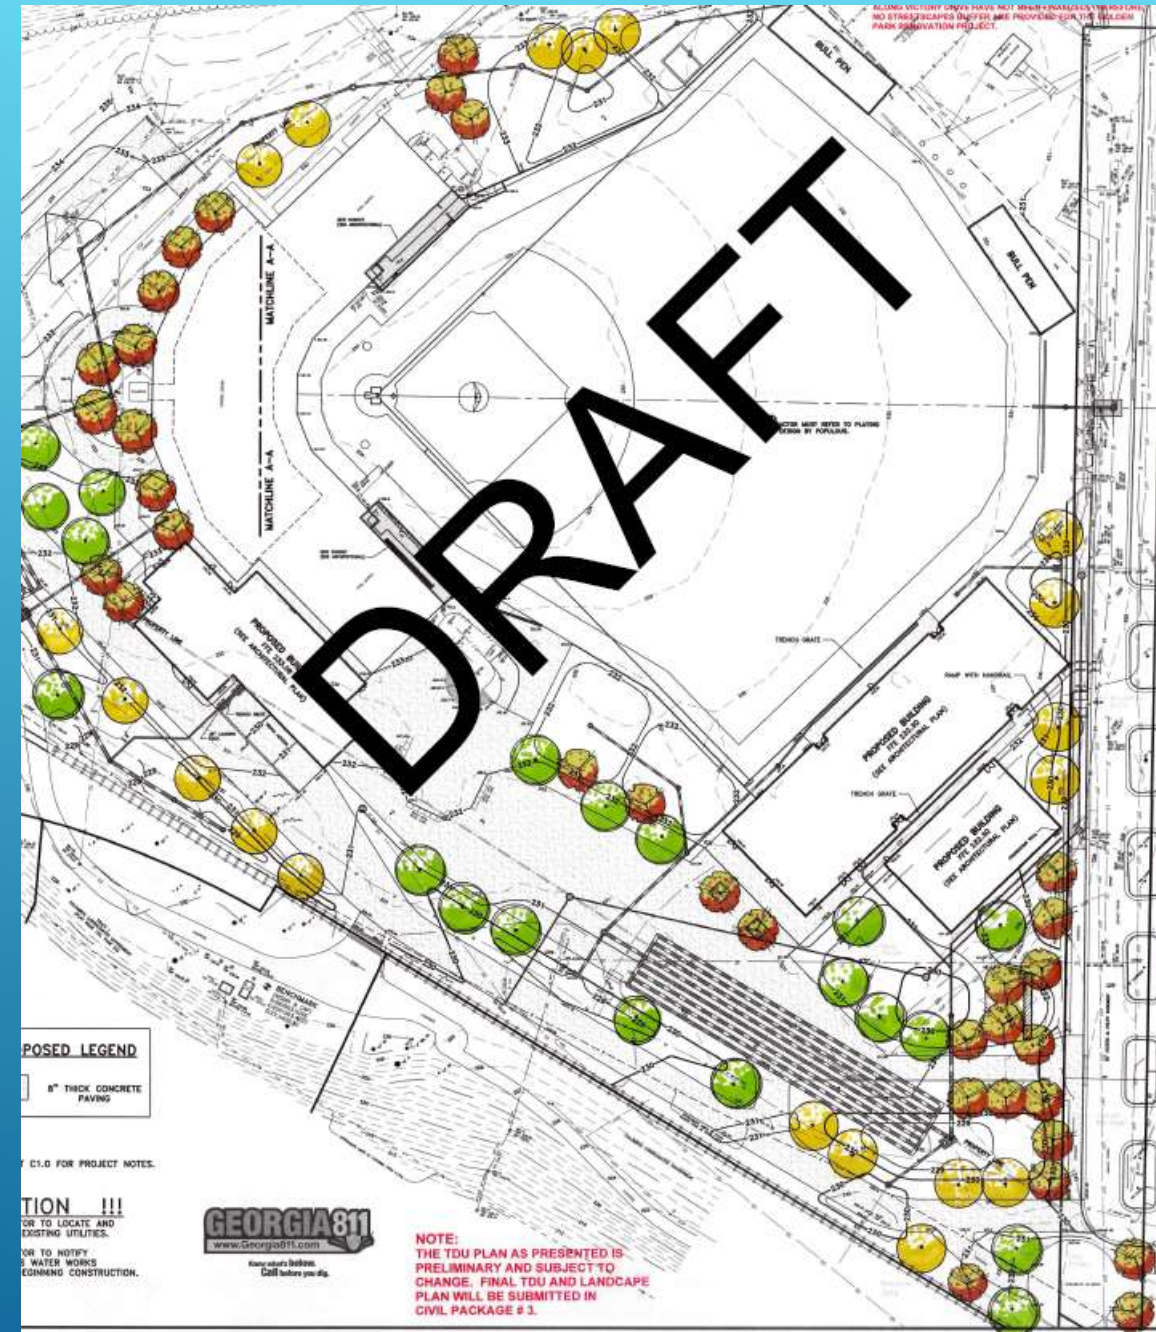

# GOLDEN PARK UPCOMING MILESTONES

- ▶ April 10, 2024 – Begin selective demolition of existing structures
- ▶ April 25, 2024 – Obtain Site Development Permit
- ▶ April 29, 2024 – Begin land clearing activities
- ▶ June 1, 2024 – Begin foundation activities for new structures
- ▶ April 2025 – Play Ball!

QUESTIONS?

