


500 SE Fourth Street • Grand Rapids, Minnesota 55744


WATER UTILITY MONTHLY REPORT September 2023 Commission Meeting

Water Operations

The water plant pumped an average of 1.15 million gallons of water per day (MGD) with a peak of 1.38 million gallons during last month which is a little higher than typical for this time of the year.


Mississippi Headwaters watershed is still in the Drought Warning Response Phase. All water suppliers in this watershed are required to implement water conservation measures. Customers are encouraged to please continue to reduce non-essential water use.

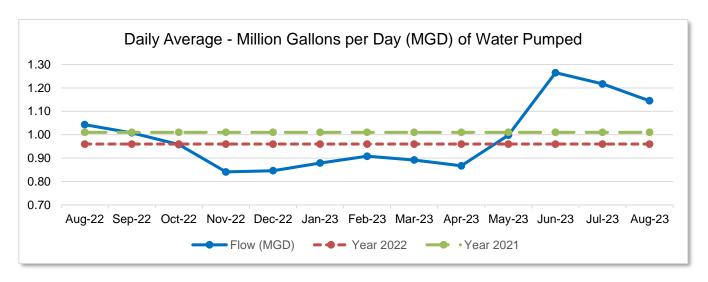






All water quality analysis was normal for the month as seen in the graphs below.

Phone: 218-326-7024 • Fax: 218-326-7499 • www.grpuc.org









Capital and Operations Project Summary

WTP Renovation Project Update:

The City Council approved the purchase of property immediately to the east of the water plant, contingent on rezoning. The application request to rezone the property has been submitted to the City. The request will be on the Planning Commission agenda on October 5 for their recommendation to the Council. The Council will hold a public hearing which, tentatively, will likely be on their October 23 agenda. That public hearing will be noticed in the paper and all property owners within 350' will receive a letter notification, a minimum of 10 days prior to the meeting.

We have completed are internal review of the top three engineering firms and plan to tour a recent project of the preferred firm in the coming weeks.

COMMISSION REPORT CONTENTS															
Agency Lead	~	Dept	Ţ		olioli:	Proi#	₩	Budget	-1	Amount Spent	Percent Spent (calc'd)	Percent Complet ▼	Status	-	Noted Issues / Highlights
GRPU		WATE		Water Plant Renovations		WATR221	_	\$4.943.400		\$0	0%	1%	In Prog	Mede	Hoteu issues / Highlights
City		WATE		Sylvan Overlays		WATR230	_	\$1,202,000		\$20.000	2%	100%	In Prog		
GRPU		WATE		Category 1 - Piping Repairs		WATR231	-	\$350,000		\$0	0%	0%	Not Sta		
GRPU		WATE		South Tower Coating Repairs		WATR231		\$150,000		\$0	0%	0%	Not Sta		
GRPU		WATE		Curb Stop Replacements		WATR230		\$100,000		\$15.000	15%	5%	In Prog		
City		WATE		Paradise Park		WATR231	-	\$85,000		\$0	0%	0%	Not Sta		
City		WATE		River Road Roundabout		WATR231	-	\$82,455		\$0	0%	100%	In Prog		
GRPU		WATE		High Service Pump Controls		WATR200		\$60,000		\$2.000	3%	25%	In Prog		
GRPU		WATE		Well 2 Rehabilitation		WATR200		\$55,000		\$20.055	36%	5%	In Prog		
GRPU		WATE	R	WTP Security		WATR210		\$43,000		\$20.874	49%	50%	In Prog		
GRPU		WATE	R	Mid-Tower Coating Repairs		WATR210)7	\$38,000		\$0	0%	60%	In Prog		
GRPU		WATE	R	Fire Hydrant Repairs		WATR220)9	\$35,000		\$0	0%	0%	Not Sta	rted	
GRPU		WATE	R	Radio Communication Upgrades		WATR230)8	\$30,000		\$0	0%	0%	Not Sta	rted	
GRPU		WATE	R	Booster Station Panel View		WATR230)2	\$30,000		\$0	0%	10%	In Prog	ress	
GRPU		WATE	R	WTP Turbidity Meters		WATR220)7	\$30,000		\$26,238	87%	50%	In Prog	ress	
GRPU		WATE	R	WTP Flow Meters		WATR220)4	\$30,000		\$22,030	73%	50%	In Prog	ress	
GRPU		WATE	R	WTP Main Valve		WATR221	12	\$22,500		\$13,403	60%	50%	In Prog	ress	
GRPU		WATE	R	WTP Valve Updates		WATR230)4	\$20,000		\$0	0%	35%	In Prog	ress	
GRPU		WATE	R	WTP Sewage Ejector System		WATR220)6	\$20,000		\$11,834	59%	25%	In Prog	ress	
GRPU		WATE	R	Replace Fiber (SH to City Hall)		WATR230)9	\$15,000		\$0	0%	0%	Not Sta	rted	
GRPU		WATE	R	WTP Communication with Wells		WATR221	11	\$15,000		\$0	0%	0%	Not Sta	rted	
GRPU		WATE	R	WTP Aerator Media		WATR220)8	\$12,000		\$4,800	40%	75%	In Prog	ress	
GRPU		WATE	R	WTP Sludge Pump		WATR220)5	\$11,000		\$9,923	90%	50%	In Prog	ress	
GRPU		WATE	R	Hydrant Meters		WATR220)3	\$8,700		\$2,800	32%	40%	In Prog	ress	
GRPU		WATE	R	WTP Backwash Valve		WATR230)7	\$5,000		\$0	0%	50%	In Prog	ress	

Status Definitions

Not Started - no human or financial resources utilized

In Progress - time or money spent on the project

In Service - operational but final close out needed

Completed - done and closed out

On Hold - waiting on some type of significant action
