

• FY2025 Q4



Overview


- ☐ Program Status through July 2025
- ☐ Performance & Accomplishments for each line of business








FY 2025 Capital Projects



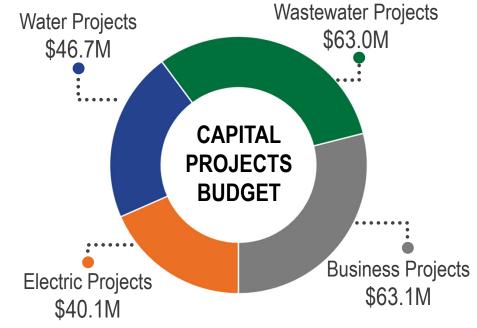

BUDGET

Developed in February 2024 based on expected project costs

\$217,821,466

SPENDING

Year-to-date project spending through July 2025

\$151,340,636

YTD %

Year-to-date project spending versus budget (July 2025)

69%


VARIANCE

Difference between budget and year-end actual costs

\$66,480,830

FY 2025 Spending vs Budget

YTD Actual Spending vs Budget

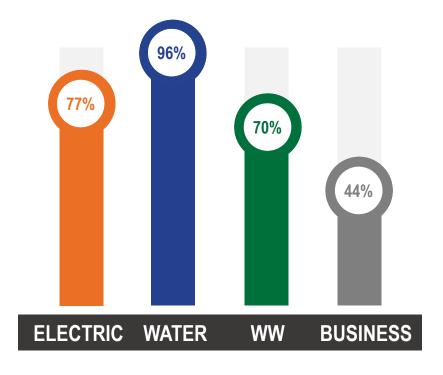

- All lines of business averaged 69% of the budget
- NBU HQ came in at 41% of the budget, but exceeded the beginning-of-year baseline by \$8M
- Design changes and delays led to lower spending on Electric and Waste Water

Project Stage

NOT STARTED PLANNING OR STUDY

DESIGN & LAND ACQ.

OR EXECUTION

COMPLETE












WATER	3	→	2	→	17	→	16	→	4
WASTEWATER	3	→	1	→	10	→	12	→	4
ELECTRIC	0	\longrightarrow	1	→	7	→	5	→	9
SUPPORT	6	→	7	→	4	→	8	→	3
Q4 TOTAL	12	\longrightarrow	11	→	38	\longrightarrow	41	→	20
Q3 TOTAL	12		11		46		43		10

Capital Projects (FY25 5-Year Plan)

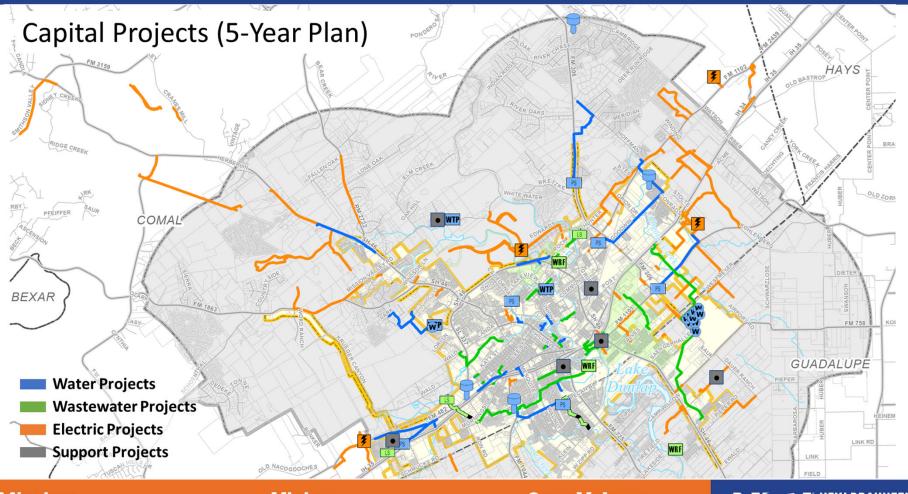

Mission
Strangthaning our community by providing raciliant assanti

Vision
Be a trusted community partner dedicated to excellence in serv

Core ValuesSafety, Team, Integrity, Culture, and Stewardship



Traffic Impacts



CIP Performance and Accomplishments












Electric – Spending vs Budget

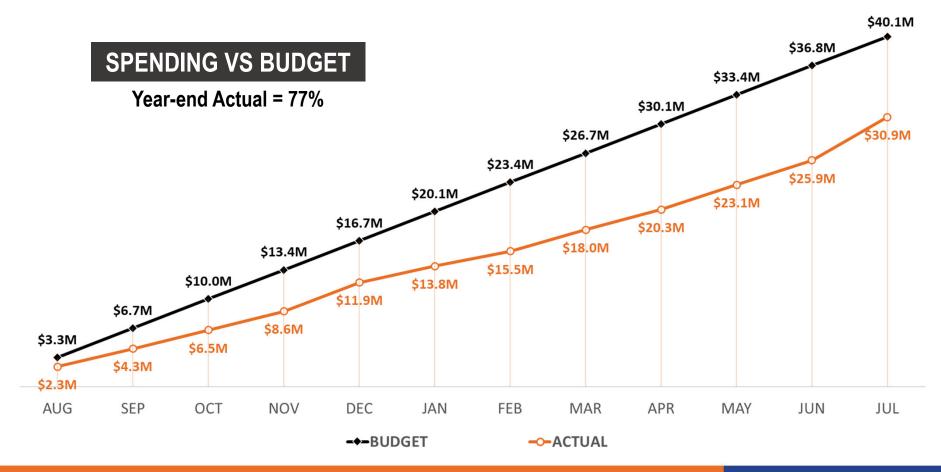



Q4 Electric Accomplishments

- Added 792 metered customers Q4 FY25, within previously completed developments and wholly new developments.
- FY25 ended at 3,866 metered customer additions (6.33% growth), second most all-time high (only to FY24).
- Energized service to 2 single-family projects and 2 multi-family projects. Major projects include:
 - Town Creek Townhomes, Phase 1
 - The Landing
 - Clear Spring Meadows Unit#2
 - Prose Apartments




Q4 Electric Accomplishments (continued...)

- Completed 1,600' of three-phase bulk overhead line adjustment on the FM 482 side of the NBU HQ, whilst also providing a new three-phase temporary service to the site-contractor.
- Completed 2,100' of three-phase bulk overhead construction along Westmeyer Rd. to serve The Landing and Sky Ranch, Lennar Homes.
- Underground Distribution Feeder exit civil work is proceeding well at the Hueco Springs Substation site, River Rd. & Edwards Blvd.



Feature Projects - Electric






HE13 Kyndwood Feeder

Completion: July 2025

Purpose: HE13 is the sixth feeder served from Henne Substation and the 51st distribution feeder. It is a semi-dedicated feeder and will serve all load of the Kyndwood master plan, totaling 1,052 residential lots and two large IH-35 commercial lots. The feeder crosses Mayfair West property, with the easement secured for NBU by Lennar Homes. Feeder exit civil work was constructed by contract crews, while all electrical OH & UD work was completed in-house.

Water - Spending vs Budget

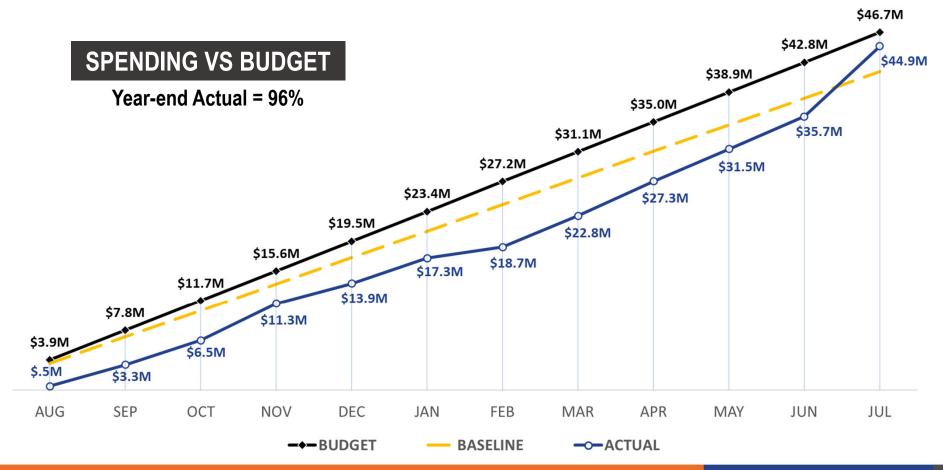


Q4 Water Accomplishments

- Admin:
 - Nearly 800 Invoices Processed
 - 40 Board Items
 - 55 Executed Contracts
- Bid Process Complete:
 - Broken and Critical Valve Replacement
 - San Antonio St Rehabilitation Phase 3 (CNB)
- Successfully Rehabilitated and brought online the County Line Standpipe and Loop 337 GST
- Conrad's EST brought online



Feature Projects - Water

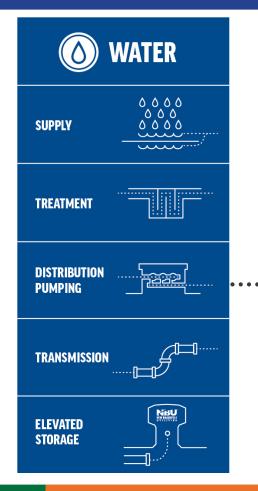




FM 1044 EST

Expected Completion: Fall 2026

Scope: 2 million gallon elevated storage tank within the Morningside Pressure Zone (MPZ).

Purpose: Maintains and exceeds regulatory compliance and enhances water service and reliability for all nearby customers.

Wastewater - Spending vs Budget

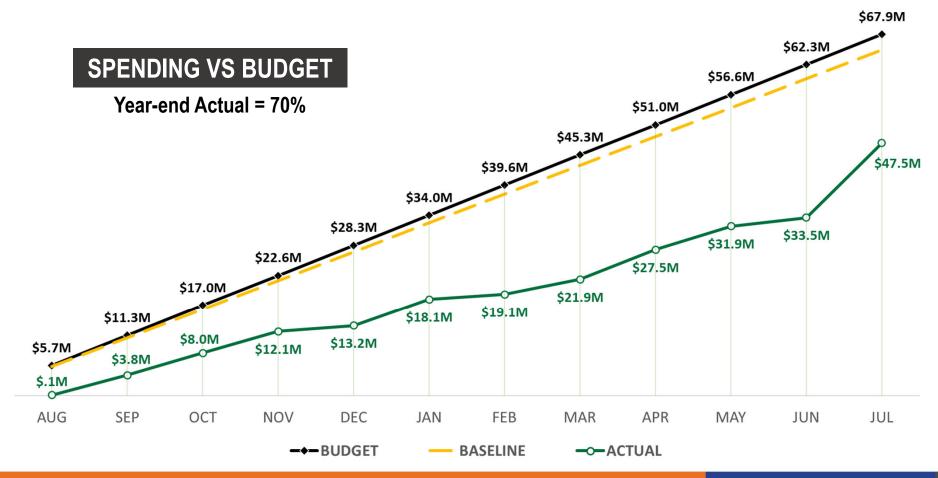


Q4 Wastewater Accomplishments

- Design Complete
 - Kuehler WRF Rehabilitation
- Construction Complete
 - Kuehler Clarifier Rehabilitation
- Heavy Construction Ongoing on McKenzie Interceptor and McKenzie WRF Expansion
 - Expected completion in Fall 2026
- Gruene WRF Expansion RFQ & Scoping



Feature Projects - Wastewater






McKenzie Interceptor

Status: Construction Ongoing. Currently working on bored road crossings and pipeline installation.

Purpose: Replace the existing 18"/21"/24" with a 36" interceptor to accommodate future growth in the McKenzie sewer basin.

Business Services – Spending vs Budget

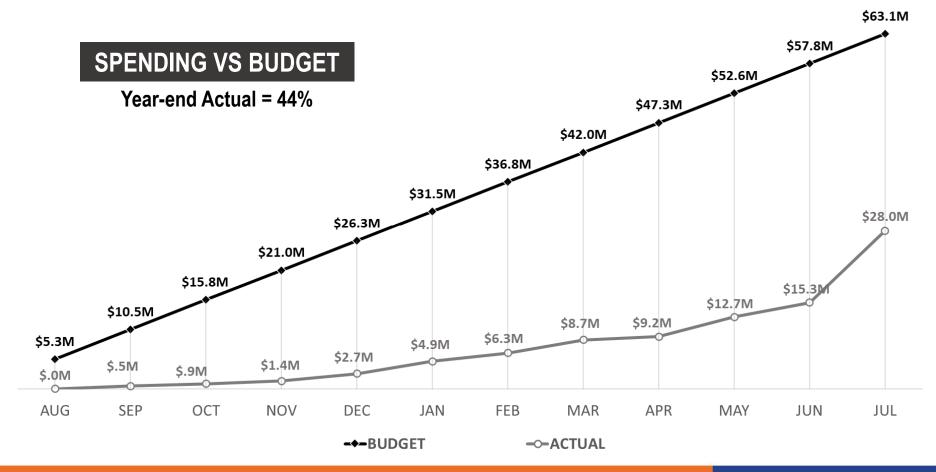

Q4 Support Accomplishments

- Windows 11 Upgrade:
 - Phase I complete
- Mobile Device Replacement:
 - 50% complete
- NetExtender VPN Client Upgrade:
 - 100%
- Migrated all .pst files in preparation for upcoming M365 migration



Feature Projects - Support





Feature Project: BDAP Server Cluster Replacement

Completion: June 16, 2025

Purpose: Upgrading our BDAP cluster to a HyperV server management platform provides more resilience and additional storage while reducing physical hardware and saving over \$100k annually in licensing costs.



QUESTIONS?
