



Recent and Upcoming Projects Overview

State Grant, Beneficial Reuse, FEMA, Corps Projects

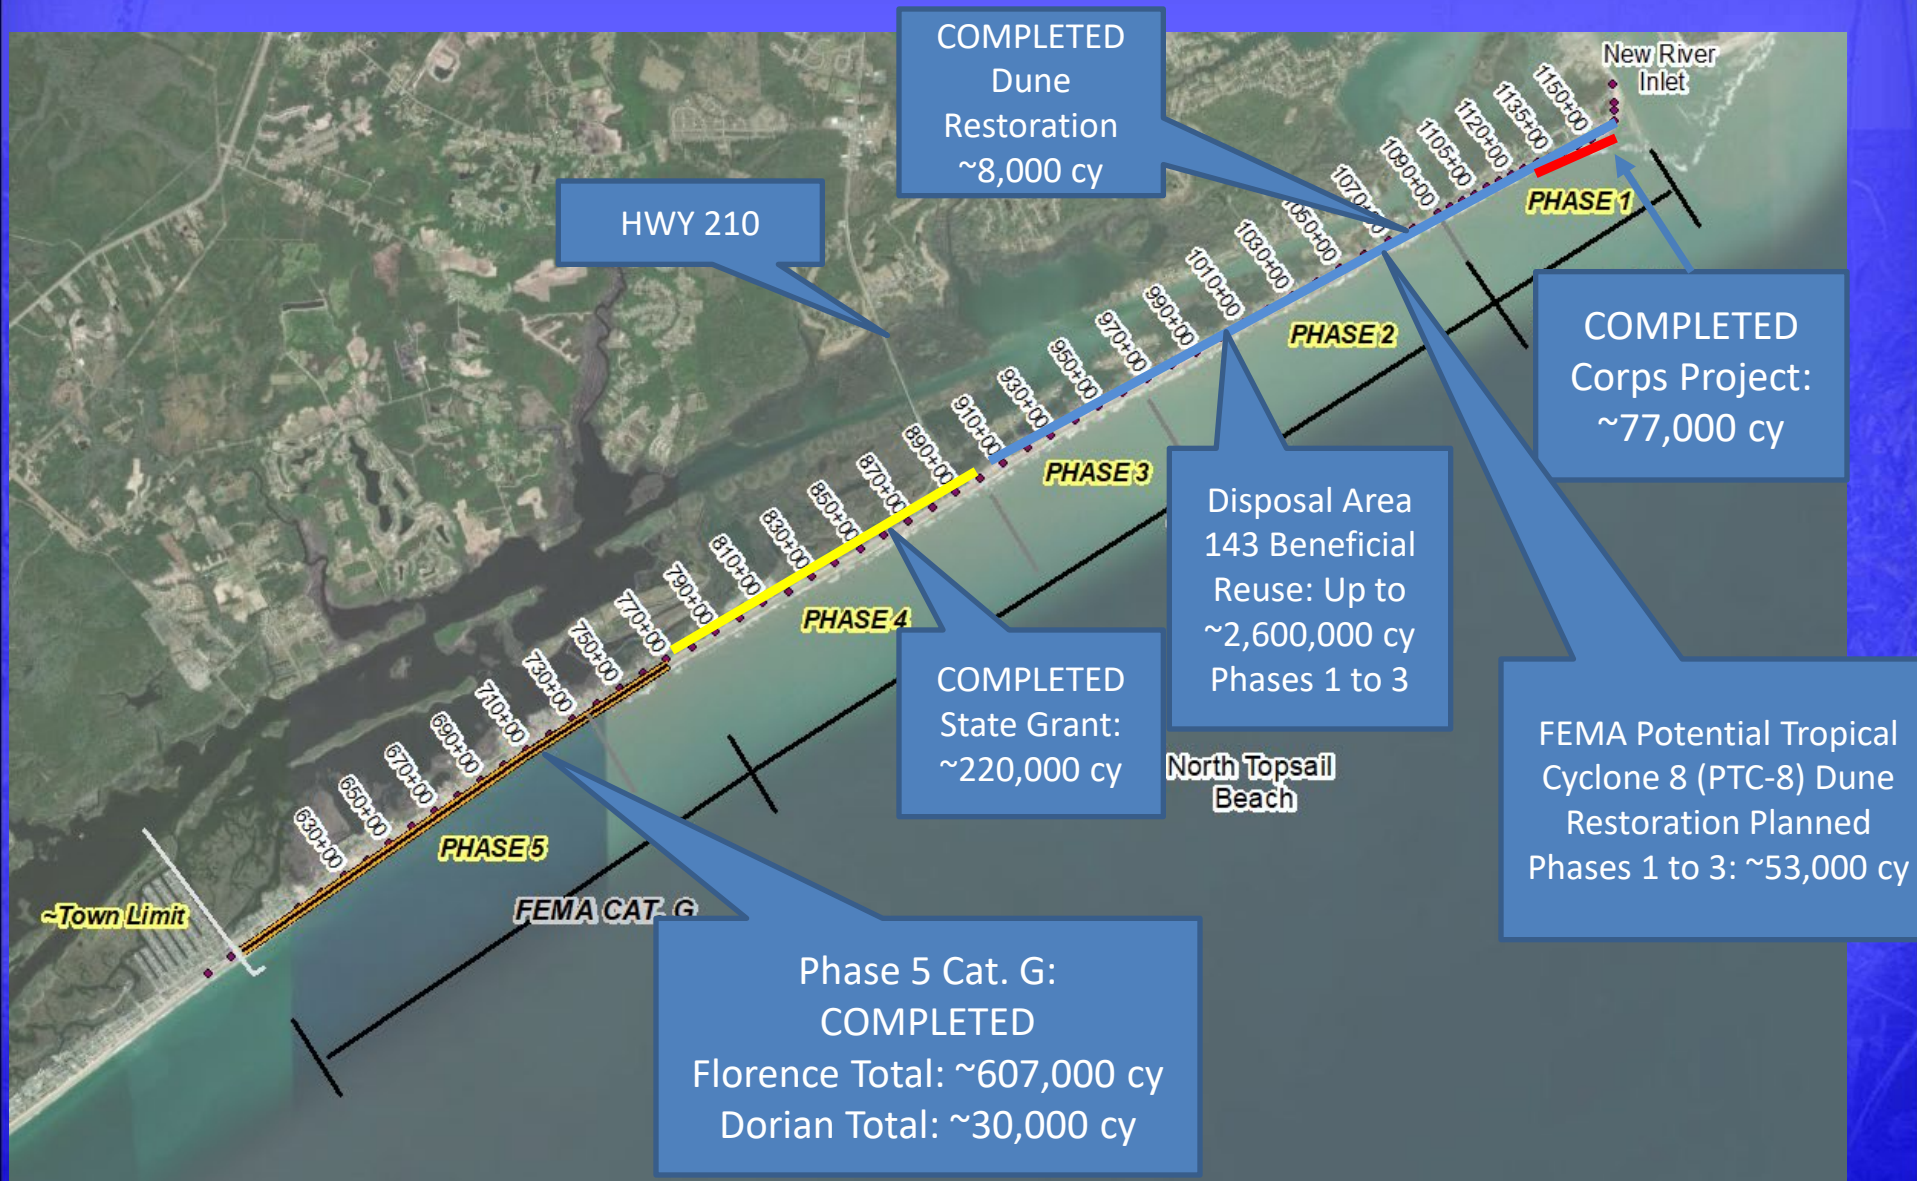

USACE Navigation Dredging and Placement Phase 1 Corps Beneficial Reuse Project

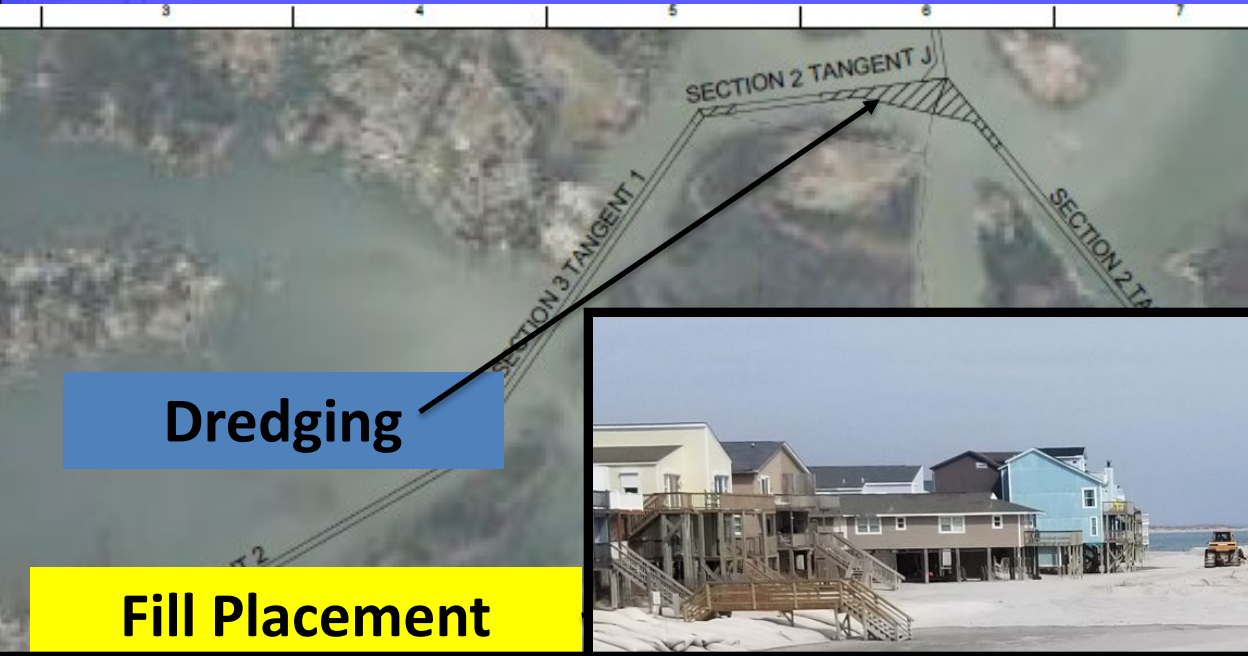

**Completed at end of February.
Long pumping distance
presents a challenge for
dredgers.**




**77,000 cy
Placement North of Topsail
Reef Condos**

**No USACE Intracoastal
Waterway dredging planned
for this winter**


**Completed FEMA Mitigation Nourishment in Phase 5 (and some Phase 4)
Beach (not Dune) Nourishment. ~3.5 Miles of Restored Beach. Held up well to PTC-8 and
other recent storms (including Hurricane Erin and recent wave/surge events).**



Completed State Grant Phase 4 Beach Nourishment – Held up well to Hurricane Erin and recent wave/surge events.

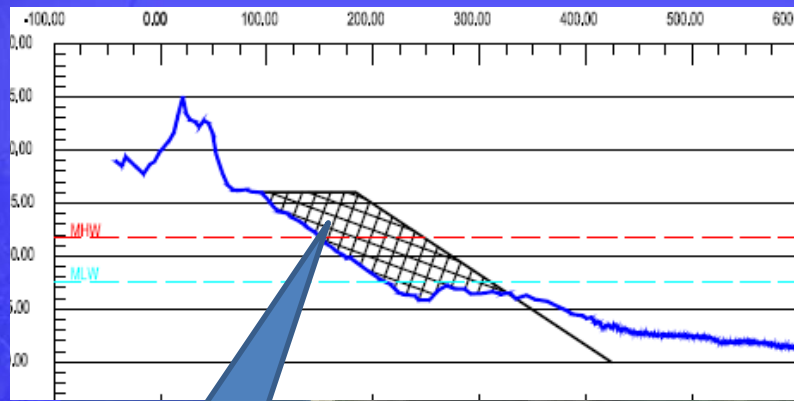

~80 to 100
Feet of Beach
Width

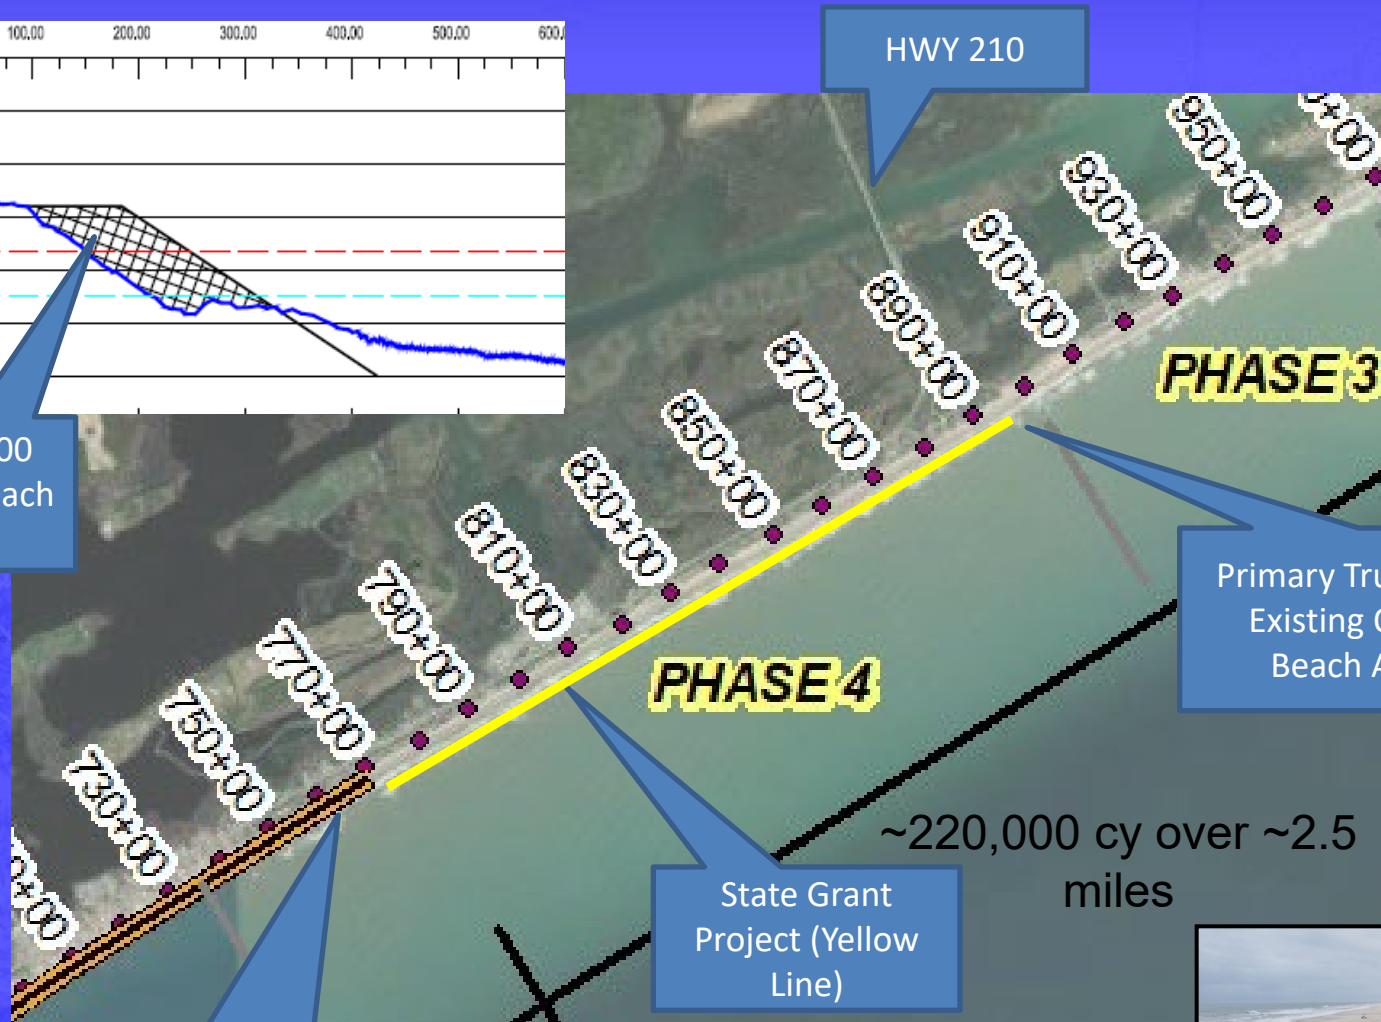

HWY 210

PHASE 3

PHASE 4

Primary Truck Access at
Existing Opening at
Beach Access 33

~220,000 cy over ~2.5
miles



State Grant
Project (Yellow
Line)

Secondary Truck Access
at Existing Opening at 2nd
Avenue



Phase 4 Nourishment


~220,000 cy Placed

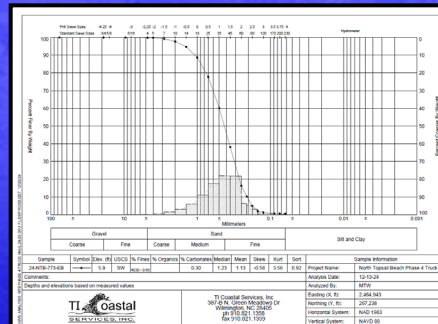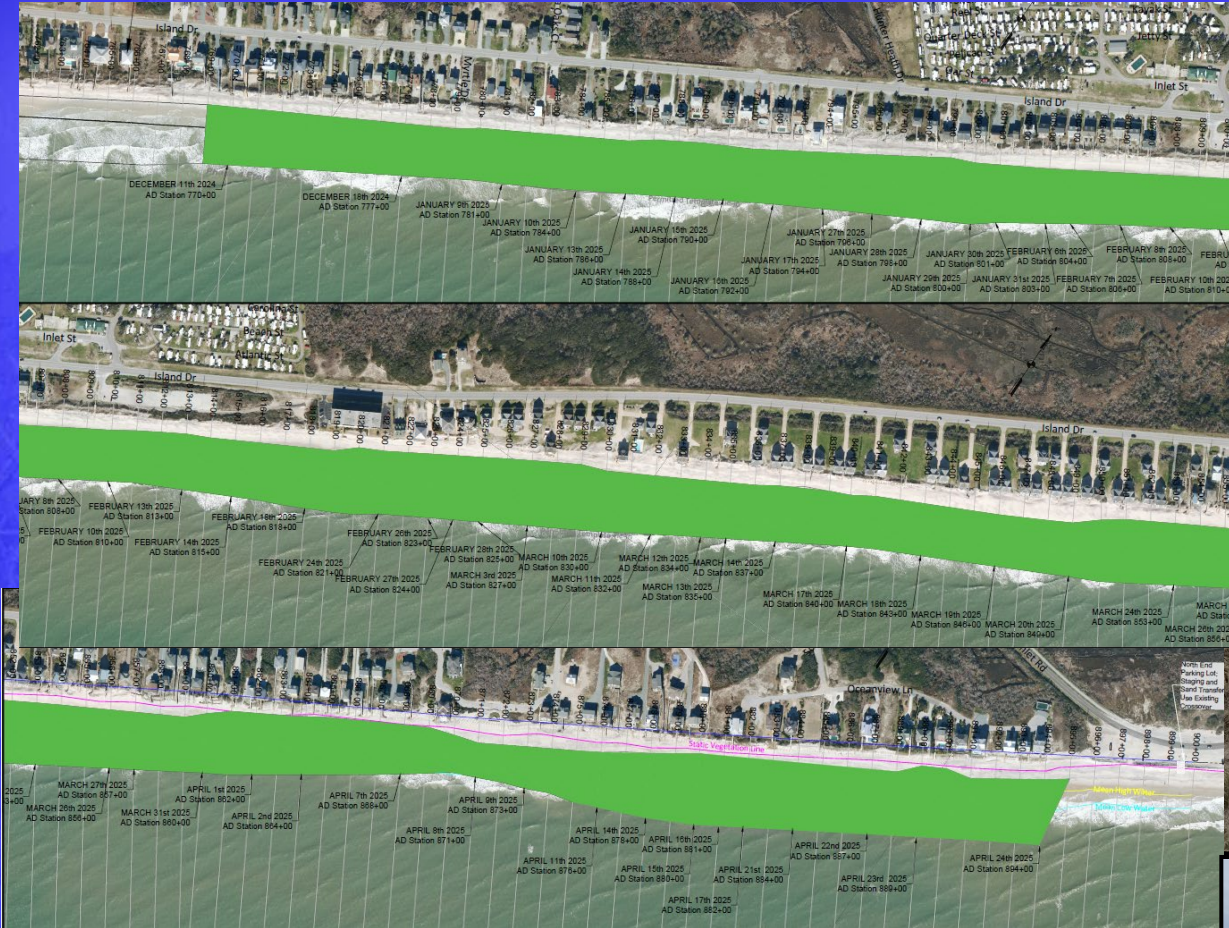

Disposal Area (DA) 143 Beneficial Reuse and Placement in Phases 1, 2, and 3



- Had “One-Stop” Pre-App Meeting with Agencies in June
- Based on Agency Feedback, ~1.9 to 2.6 Million CY at DA 143
- Easement coordination continues with state agencies
- Permit Application Submission Follows Easement.

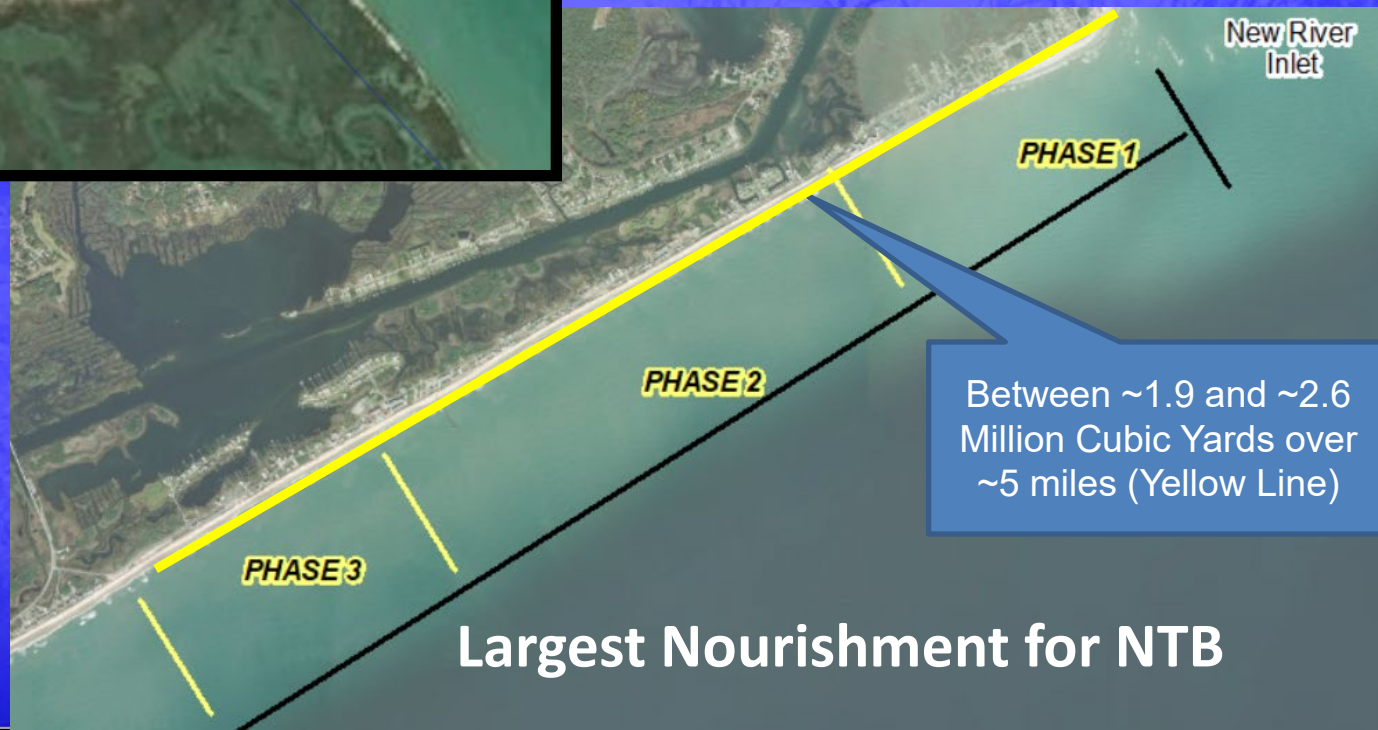

Between ~1.9 and ~2.6 Million Cubic Yards over ~5 miles (Yellow Line)

Largest Nourishment for NTB

Potential Tropical Cyclone (PTC) 8

DECLARED OCTOBER 19, 2024

SUMMARY

STATE: North Carolina
NUMBER: FEMA-4837-DR
INCIDENT: Potential Tropical Cyclone Eight
INCIDENT PERIOD: September 16-20, 2024
DATE REQUESTED BY GOVERNOR: October 16, 2024
FEDERAL COORDINATING OFFICER: E. Craig Levy, Sr.
National FCO Program

DESIGNATIONS AND TYPES OF ASSISTANCE:

INDIVIDUAL ASSISTANCE (Assistance to individuals and households):

Not Requested.

PUBLIC ASSISTANCE (Assistance for emergency work and the repair or replacement of disaster-damaged facilities):

Brunswick, Carteret, New Hanover, and Onslow Counties.

- Dune Restoration to Withstand 5-Year Storm
- FEMA Project Processing Continues
- No Additional FEMA Information Requests

Public Assistance (PA)

Provides grants to eligible state, local governments, EBCI and eligible private non-profits ("Applicants") to assist with the cost of responding to and recovering from disasters

Governing Laws, Regulations, and Policies

Stafford Act

Law

44 CFR

Program Regulations

2 CFR

Procurement Requirements


PA Program & Policy Guide (PAPPG)

Policy

FEDERAL EMERGENCY MANAGEMENT AGENCY (FEMA)
ENVIRONMENTAL PLANNING AND HISTORIC PRESER-
VATION (EHP) GREENSHEET FOR DR-4837-NC






PTC 8 Rainfall (Sept. 16, 2024)

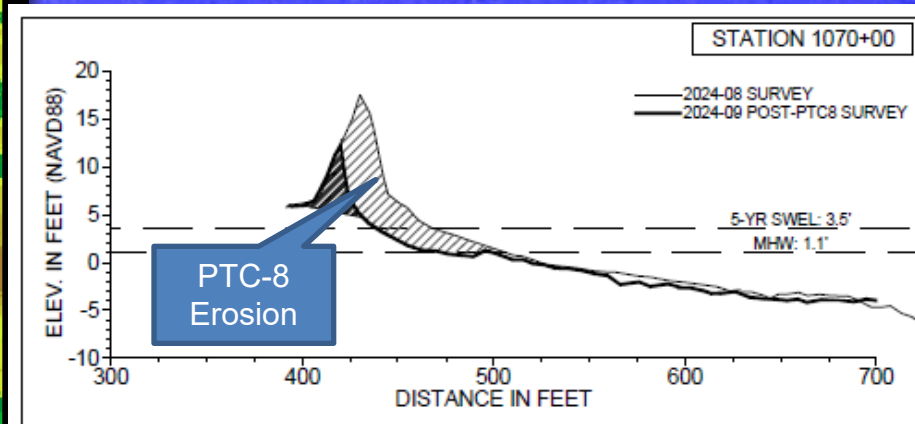

Critical Dune Restoration: ~8,000 cy in April/May

FEMA PTC-8 Mitigation

ST Wooten – Contractor

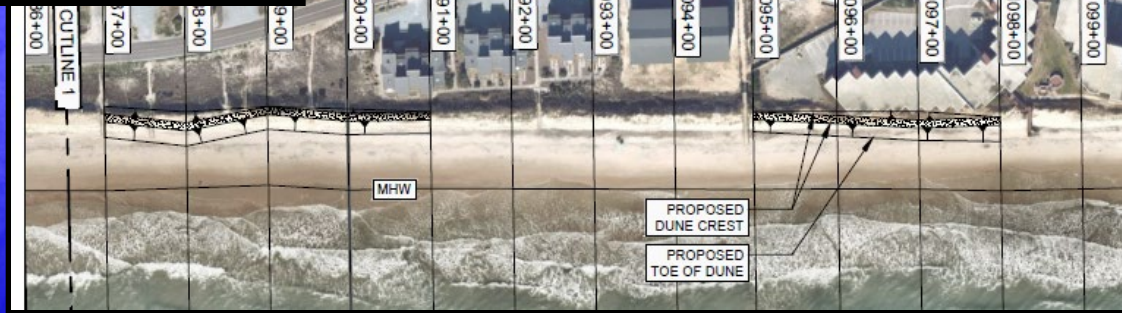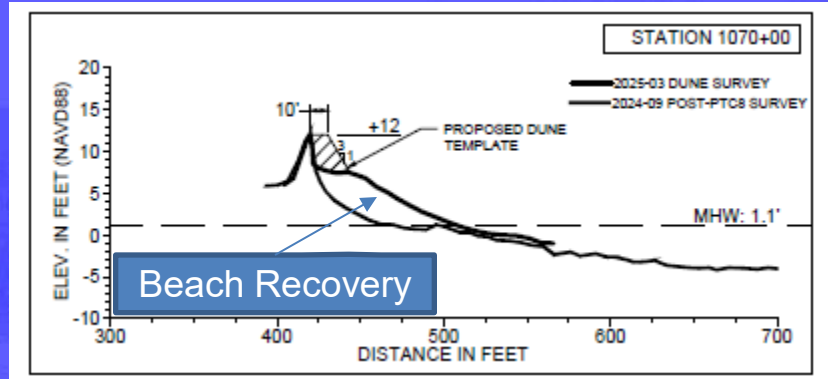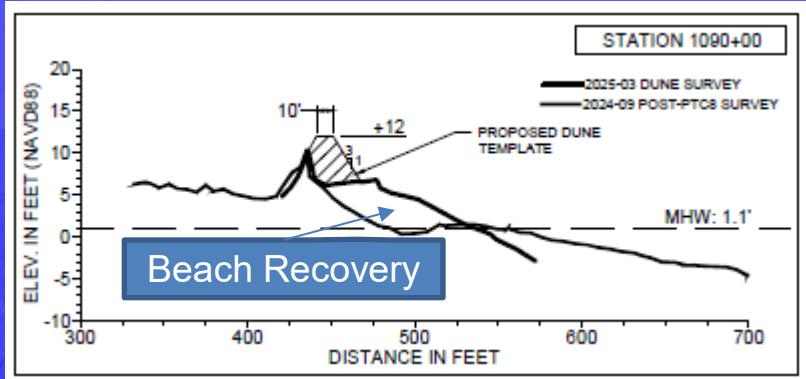


Northern Shoreline Dune Restoration (Phases 1 to 3 for 53,000 cy)

ST Wooten – Contractor – Approximately 2 Month Project

Planned to Start Monday, January 5

Contractor is Flexible on Order of Work

FEMA PTC-8 Mitigation

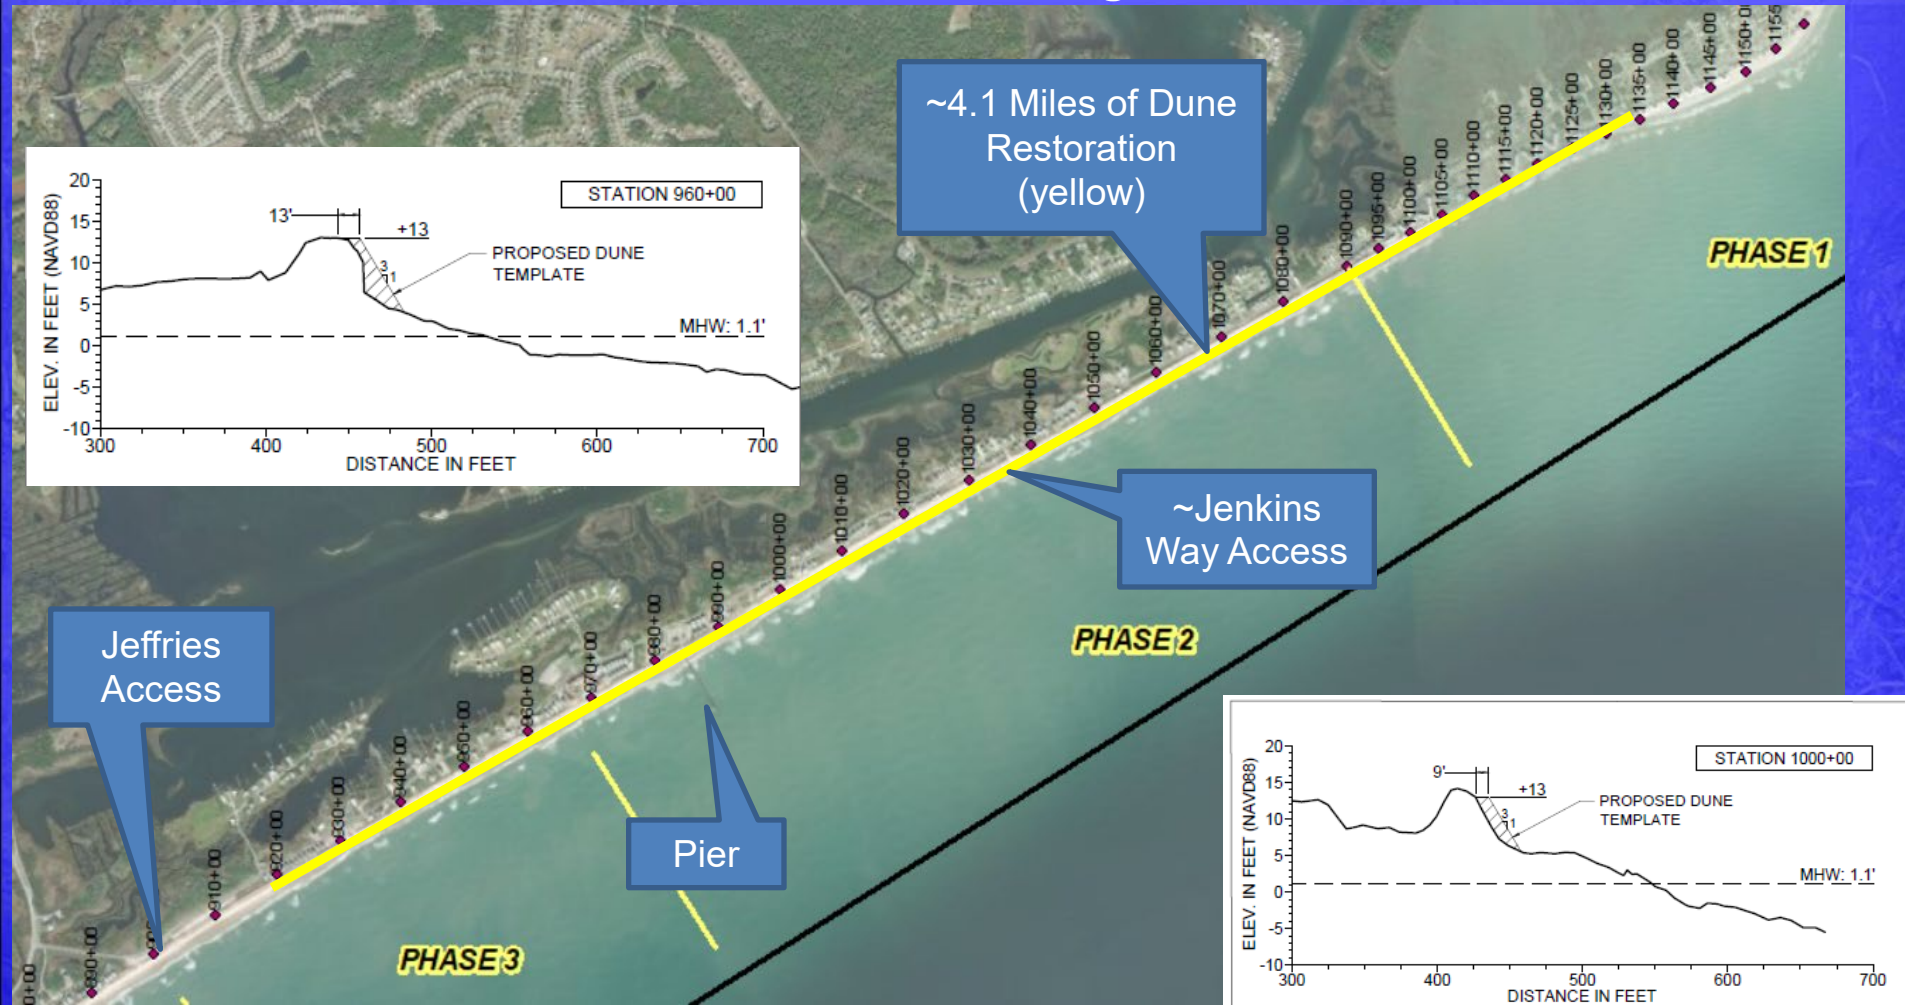

Town Beach Projects Updates

- Dune erosion occurred during Nor'easter on weekend of October 11-12 with +2.5 foot surge and large waves.
- New River Inlet Management Master Plan EIS: Draft EIS under several levels of USACE review. Higher level review ongoing. Shutdown has slowed this.
- Post Tropical Cyclone 8 FEMA/NCEM- No more additional FEMA requests and berm project processing is moving forward. 53,000 cy dune restoration (in addition to 8,000 cy in April) in Phases 1, 2 and 3 to occur January 5. ST Wooten is flexible on order of work.
- Disposal Area 143 Beneficial Reuse for Nourishment of Phases 1,2,3 of between ~1.9 and ~2.6 million cubic yards. Easement coordination on DA143 use ongoing with state agencies. Then final permit application submittal.
- Critical Dune restoration in Phases 1 and 2 COMPLETED.
- State Grant Nourishment - ~220,000 cy in Phase 4 COMPLETED.
- Phase 1 – Corps AIWW Project (~77,000 cy placed north of Topsail Reef condos) COMPLETED.
- Working with NTB Staff regarding funding, accounting and reimbursement for FEMA funded projects
- Permitting Coordination (all projects)

