




The Town of Warrenton
P.O. Box 341
Warrenton, VA 20188
P (540) 347-1101
F (540) 349-2414

April 2024 Road Conditions Report

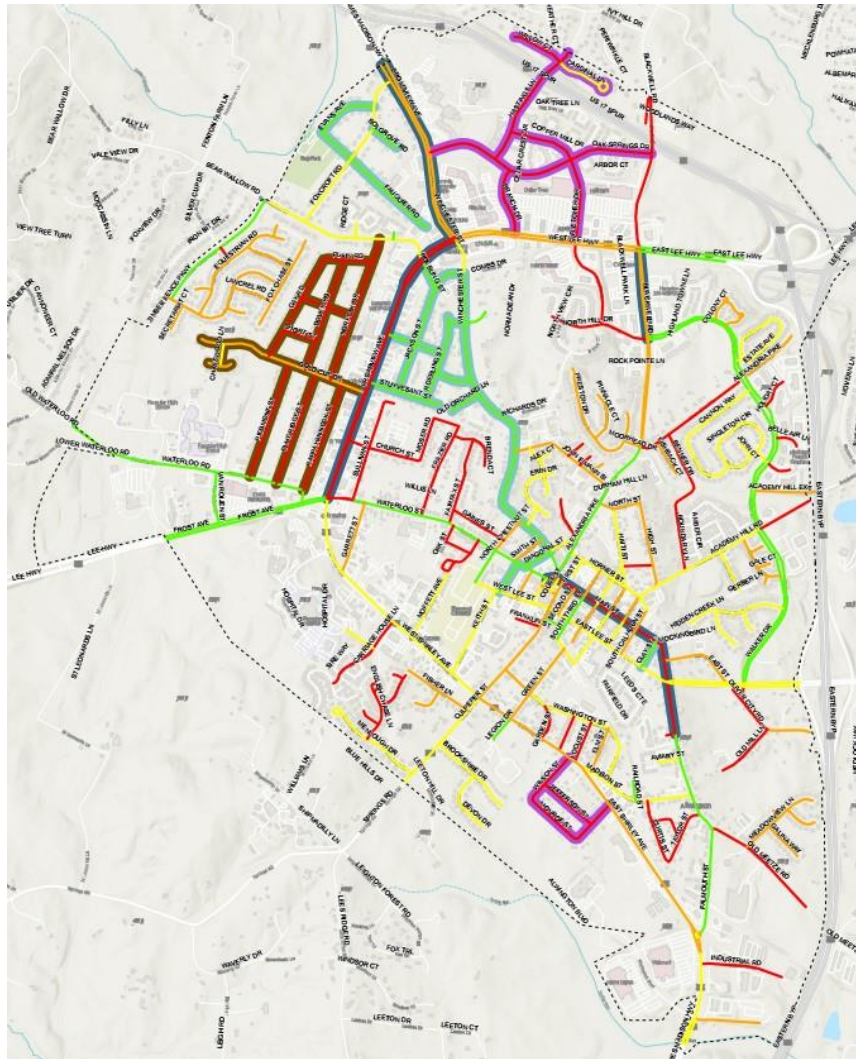

VDOT State of Good Repair

- **VDOT State of Good Repair Program- Local Pavement Program**
 - 100% funding from VDOT via FHWA
 - ADA Ramps upgraded to present standards
 - Mill and overlay deteriorated streets
- **SGR targets for October 2023 application**
 - Main Street- from Courthouse Square to Falmouth Street
 - Falmouth Street- from Main Street to Falmouth Court
 - Received \$911,778.00 of SGR Funds for FY-23
- **VDOT CTB Requirements**
 - CTB FY-2029 Goal
 - 82 % of Arterial Streets need a CCI score of 60 or greater
 - 75 % of Collector Streets need a CCI score of 60 or greater

Pavement Overlay and Sidewalk Replacement Plan

- **FY-24 Pavement Overlay Schedule- Completed**
 - Total Budget- \$600,000.00
 - Finished 8 months ahead of schedule
 - \$62,490.28 under budget
- **FY-25 Pavement Overlay Schedule**
 - Award PO July 2024
 - Collector Routes
 - Branch Drive
 - Cardinal Lane
 - Fletcher Drive
 - Oak Springs Drive
 - Hastings Lane
 - Willow Court
 - Wilson Street
 - Monroe Street
 - Cleveland Street
 - Jefferson Street

- Fix broken curbs and sidewalks on proposed routes
 - Estimate 35% to 40% replacement
- Sidewalk Repairs- Spring 2024
- Asphalt placement- Completed before July 1, 2025
- Estimated Funding Request- \$850,000.00

➤ **FY-26 Pavement Overlay Schedule**

- Award PO July 2025
- Collector Routes
 - Beacon Road
 - Blue Ridge Street
 - Dover Road
 - Norfolk Drive
 - Piedmont Street
 - Rappahannock Street
 - Short Street
- Fix broken curbs and sidewalks on proposed routes
 - Estimate 35% to 40% replacement
- Sidewalk Repairs- Spring 2025
- Asphalt placement- Completed before July 1, 2026
- Estimated Funding Request- \$450,000.00

➤ **Pavement Evaluation**

- Forecast future funding demands
- Spring 2024 evaluate Poor and Fair Roadways
- Start Planning for FY-27 Pavement Overlay and Sidewalk Replacement

➤ **Current Pavement Conditions**

- Town invested \$1,455,370.25 in Collector and Arterial Streets for FY-23 & FY-24

Current Road Conditions (1st Quarter 2024)						
Arterial Routes				Collector Routes		
Condition	Lane Miles	Percentage		Condition	Lane Miles	Percentage
Good	10.2	31.1%		Good	12.8	19.4%
Satisfactory	7.1	21.6%		Satisfactory	14.3	21.6%
Fair	9.6	29.3%		Fair	15.2	23.0%
Poor	5.9	18.0%		Poor	23.8	36.0%
Total Lane Miles	32.8			Total Lane Miles	66.1	

Sidewalk Construction

➤ Fauquier Road

- Started Preliminary Engineering on September 28, 2023
- Survey work completed by end of October 2023
- Concept Plan completed December 2023
- Public Comment
- 30% Design completed by Fall 2024
- Submit for VDOT funding in FY-25

➤ Washington Street

- Update existing plans
- Start construction by Fall 2024

➤ Future Sidewalks in planning stage

- Gay Road
- Foxcroft Road
- Academy Hill Road

Transportation & Safety Improvements

➤ Courthouse Square

- Conducted Traffic Study from March 18th to March 22nd
- Processing public comments
- Present results to Council in May 2024

➤ Waterloo Street

- Multi-phase approach is in effect.
- Speed trailers have been deployed.
- Future traffic calming measures
 - Speed table between Garrett Street and Middle School
 - Place chicane hardscape between Sullivan Street to Garrett Street
 - Bid by Summer 2024
