

Project Update

Engineering

FY 2025-26

1st Quarter Report


King's Gate Road Bridge Replacement Project



Site photo looking south

- ▶ **Let date:** August 2025.
- ▶ **Contractor:** Talbert Companies, LLC
- ▶ **Bid Total Amount:** \$1,536,598.58
- ▶ **Project Description:** The project consists of the removal and replacement of the King's Gate Road bridge over Clear Fork Trinity River. The project includes the approach roadways approximately 200' south of the bridge to the IH 20 frontage road and 100' north of the bridge.
- ▶ **Timeline:** Project is to be completed in 121 working days. Anticipated completion date is June 2026.
- ▶ **Project Update:** Construction continues to move forward steadily. The existing structure has been fully removed, and crews are actively completing various dirt work and excavation. The storm drainage line has also been removed and reinstalled with new 45-degree bends, resolving the conflict with the planned drill shaft foundation while preserving proper flow from the adjacent curb inlet. In addition, the contractor has finished extending the corrugated metal pipe at the west driveway of SiteOne Landscape Supply and has installed new concrete safety end treatments. The contractor has begun working on the drill shaft foundations.

Texas Department of Transportation's 2025 Transportation Alternatives (TA) Set-Aside Call for Projects

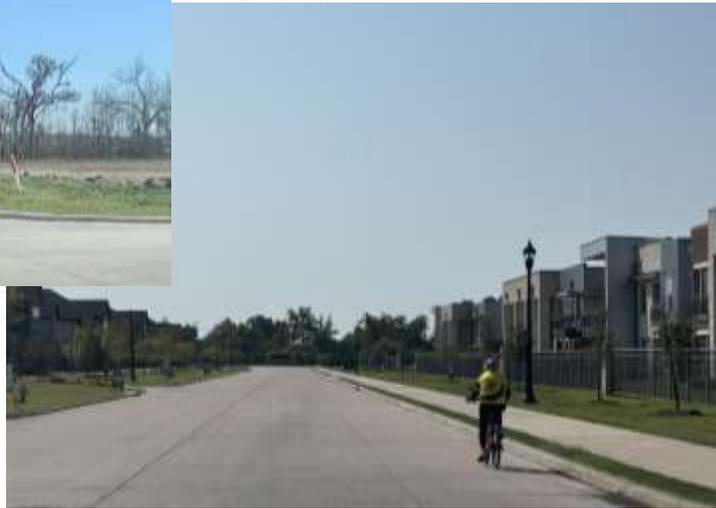


- ▶ The Texas Department of Transportation (TxDOT) issued a “Call for Projects” in January 2025 for communities to apply for funding assistance through the Transportation Alternatives Set-Aside (TA) Program.
- ▶ The TA program provides funding for development of preliminary engineering and construction of pedestrian and/or bicycle infrastructure.
- ▶ The City of Willow Park TA project was selected to receive federal funding (80% maximum for preliminary engineering and construction) by the Texas Transportation Commission.
- ▶ The Transportation Alternatives (TA) Set-Aside funding program is an 80/20 match, where the city would be responsible for 20% of the cost of the project. The city would also be responsible for all non-reimbursable costs and 100% of overruns, if any.

Texas Department of Transportation's 2025 Transportation Alternatives (TA) Set-Aside Call for Projects (cont.)

- ▶ **Phases of work included in award:** Design and Construction
 - ▶ **Federal Funding Amount:** \$552,800
 - ▶ **Local Match:** \$138,200
 - ▶ **Project Description:** The project will fill gaps, remove barriers, and expand connectivity in active transportation networks, while separating pedestrians and bicyclists from vehicle traffic. The project will construct 6-foot-wide bike lanes along Meadow Place Dr. from I-20 frontage road to W. Jockey and 6-foot-wide concrete sidewalks along the west side of Kings Gate Rd. between Meadow Place Dr. and Kings Gate Park. Bike lane pavement markings and bike parking racks will support these improvements. Meanwhile, the Kings Gate Rd./Meadow Place Dr. intersection will receive safety improvements including curb ramps, crosswalks, illumination, and advance crosswalk signage.
 - ▶ **Project Update:** A project initiation meeting was held on January 15th with the TxDOT District to discuss project scope, timeline, elements of the Advance Funding Agreement (AFA), consultant procurement, and other project details. The next step is to complete the required Project Information Form (PIF) and submit it to TxDOT so they can begin drafting the AFA.
-

Squaw Creek Road - Water Line Replacement and Street Improvements

- ▶ The project consists of water line replacement and street reconstruction of Squaw Creek, Yucca, Mesa, Cactus, Cactus Court, and Verde Roads.
- ▶ Town Hall meetings for the residents along Squaw Creek Road and side streets have been held.
- ▶ With the project plans at 90% completion, the engineer has identified conflicts with existing power poles within the construction limits. City staff is coordinating with Oncor on the utility relocations.
- ▶ One-on-one meetings with residents to discuss specific details about the project have been completed.
- ▶ At the December 9th City Council meeting, Council approved the publication of Notice of Intent for Certificate of Obligation (CO) bonds.
- ▶ **Project Update:** The next step is for City Council to pass an ordinance authorizing issuance of CO's.

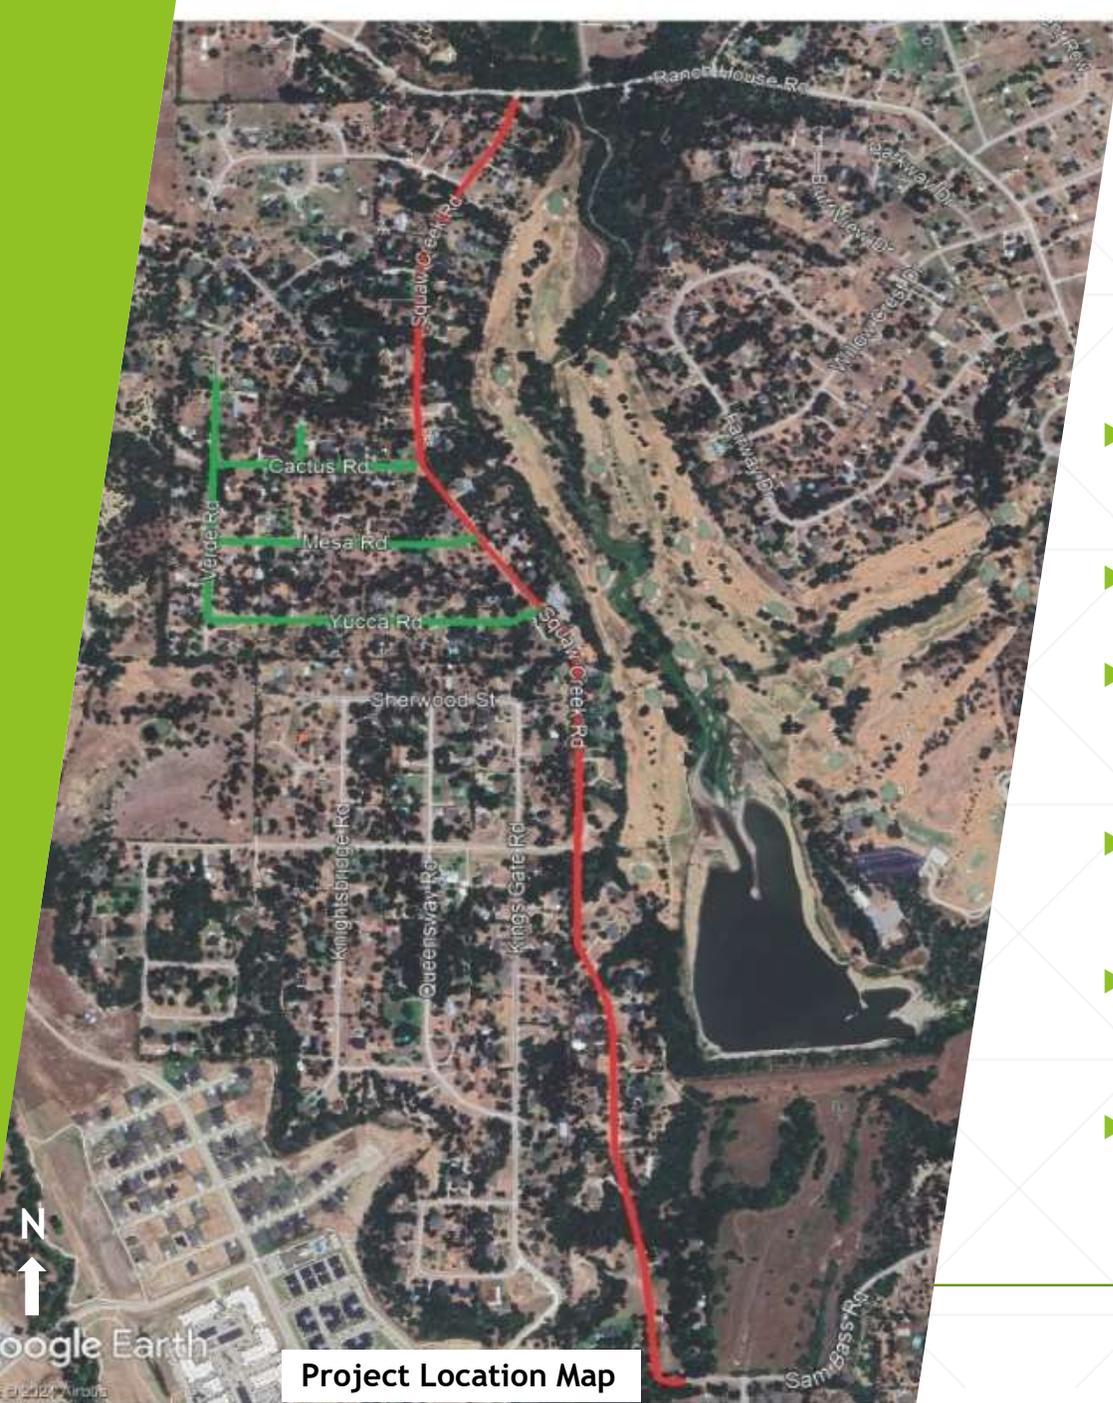

Project Location Map
