

**Willamette Water Supply Program
Wilsonville Area Pipeline Project
(PLM_1.3)
City Council Update**

April 1, 2024

Willamette Water Supply Program Update

- Project Update
 - Overview
 - SW Kinsman Road Restoration
 - SW 95th Construction
 - SW Boeckman Road/SW 95th Trenchless Crossing
 - SW Ridder Road (Future Work)
- Recent Public Outreach
- Question & Answer

**RWF_1.0 Pump Station,
Electrical Building,
Seismically Reinforced
Riverbank, and Pipeline
Project**

Under Construction

Estimated Completion: April 2025

PLM_1.1 Pipeline

Construction Complete

**PLM_2.0 Pipeline-Kinsman Rd
Partnership Project**

Construction Complete

**PLM_1.2 Pipeline-Garden
Acres Rd
Partnership Project**

Construction Complete

PLM_1.3 South Section

Under Construction

Estimated Completion: February 2025

PLM_1.3 North Section

Under Construction

Estimated Completion: February 2025

SW Garden Acres Rd

SW Kinsman Rd

SW Boeckman Rd

SW Ridder Rd

SW Wilsonville Rd

SW 95th Ave



Legend

- PLM_1.3 (Under Construction)
- RWF_1.0 (Under Construction)
- Completed Projects



Project Construction Update

Project Segment	Pipeline Complete	Street/Site Complete
SW Kinsman Rd. (Wilsonville Rd. to Barber St.)	100%*	Permanent (25%)*
SW 95 th Avenue (Hillman Ct. to Ridder Rd.)	95%	Temp Complete*
SW Boeckman Rd. (Private Property)	90%*	NA
SW 95 th Avenue (Boeckman Rd. to Hillman Ct.)	60%*	Future
SW Ridder Rd. (95 th Ave. to Peters Rd.)	Future	Future



SW 95th Avenue temporary paving

SW Kinsman Road Paving and Restoration




Pipeline Complete

Anticipating Pipeline Testing Complete by April 1

Future Restoration Work

Concrete Panel Installation (*ongoing through Summer 2024**)
Kinsman/Wilsonville Truck Turn Lane & Intersection Improvements (*TBD*)

SW 95th Avenue Paving and Restoration

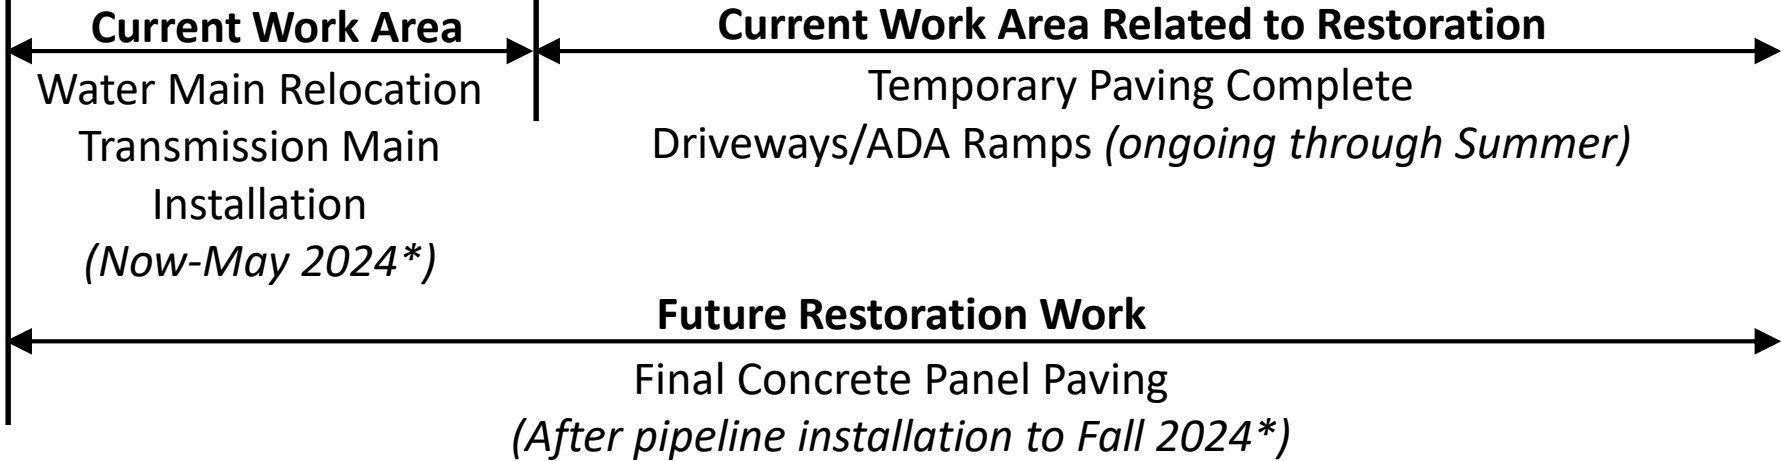

Trenchless Crossing SW Boeckman & SW 95th

- Trenchless crossing of SW Boeckman Road and the TriMet Westside Express Service (WES)
- When complete, it will connect to the 66" water pipeline being installed in SW 95th avenue
- 3rd trenchless crossing for project
- Anticipated completion: Spring 2024*



The trenchless crossing minimizes impacts on the environment, roadways, traveling public, and nearby businesses

SW Ridder Road (Future Work)



Future Work Area


Pipeline Installation and Road Restoration (*May – October 2024**)
Currently Coordinating with the BPA and Republic Services

**Based on the most recent contractor's schedule. Subject to change due to weather, utility conflicts, and other delays.*

Public Outreach History (Since 2019)

- ✓ Dedicated Project Webpage
- ✓ Monthly Project Update E-Newsletter
- ✓ Construction Notifications
- ✓ Boones Ferry Messenger Articles
- ✓ Wilsonville Spokesman Articles
- ✓ Postcard Mass Mailing
- ✓ Door Knocking
- ✓ Construction Access Surveys
- ✓ Open Houses/Meet the Contractor
- ✓ Easement Outreach and Coordination
- ✓ Project Briefings
- ✓ Trip Check
- ✓ Annual Program Updates Video

Recent Public Outreach

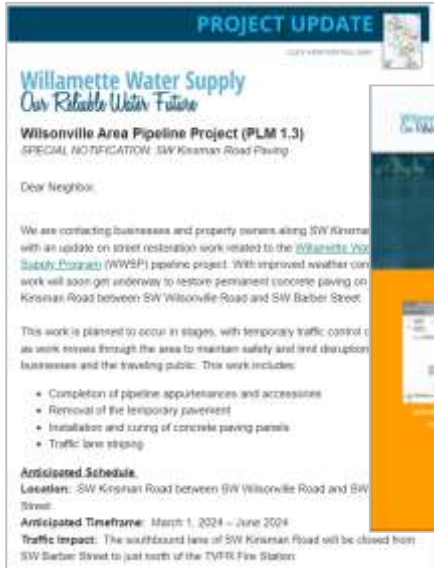

- ✓ Project Webpage
- ✓ Project E-newsletter
- ✓ Construction Notifications
- ✓ Detour Maps
- ✓ Business briefings, emails, 1:1 meetings
- ✓ Signage
- ✓ Trip Check

- ✓ City of Wilsonville Website
- ✓ Social Media
- ✓ Wilsonville Spokesman

Construction Outreach





**QUESTIONS?
THANK YOU!**

info@ourreliablewater.org

www.ourreliablewater.org
