


2022 ADA Improvements

Project Type: ADA (Streets)

Total Project Cost: \$88,774

Project Timeline: Jan 2022 – Aug 2022

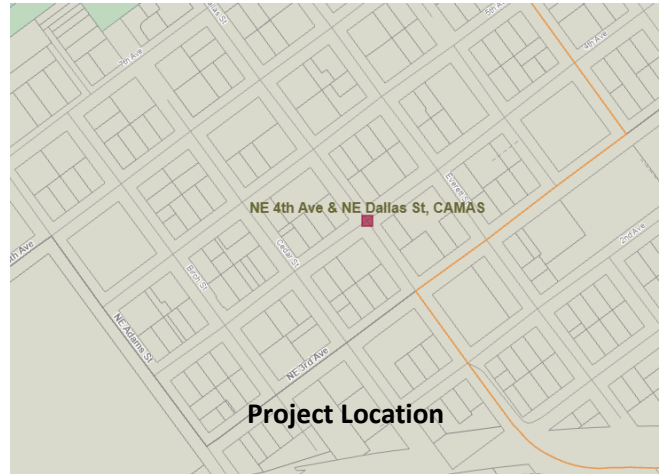

Project Description

The 2022 ADA project replaced 23 exposed aggregate panels that created tripping hazards and slippery conditions in the Downtown core area. These panels were the subject of multiple complaints from the elderly and those with mobility impairments.

Camas Downtown businesses had the option to work with awarded contractor to replace additional sidewalks. Attic Gallery and Lutz Hardware were able to improve sections of their frontages.

Project Details and Benefits

- Sidewalks sections had not been improved for at least 50 years
- New sidewalks benefit all pedestrians through the downtown area, especially those with mobility impairments
- Downtown Camas Association and businesses were pleased to have safer sidewalks in advance to Camas Days and before the first American Empress Riverboat tour

Project Funding

Project Phase	Year	ADA Budget	Omnibus	Total
Construction	2022	\$50,000	\$38,774	\$88,774
Total		\$50,00	\$39,260	\$88,774
Original Budget Estimate				\$85,000

