


Skate Park Improvements Project Summary

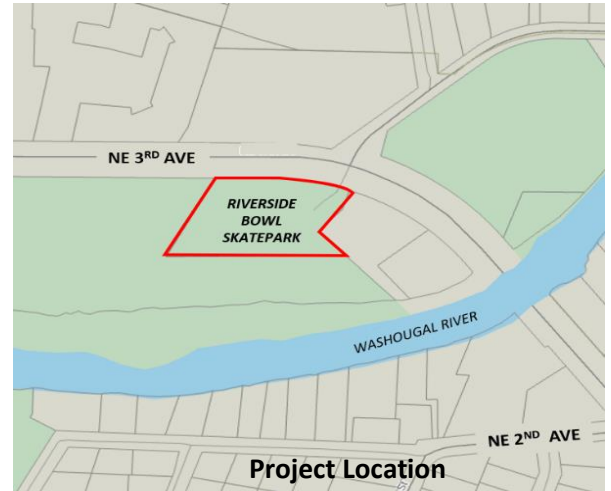

Project Type: Park Improvement
Total Project Cost: \$383,227
Project Timeline: June 2021 - July 2023

Project Description

The skate park improvements consisted of construction of new concrete features within the existing park footprint. New features included a quarter pipe section, fun box, entry pyramid, quarter pipe with deck, and a full bowl with tunnel wall entrance. The project was a great success and collaboration between involved citizens, fund-raising efforts and City contributions!

Project Details and Benefits

- Project was community driven with local citizens volunteering and engaged throughout the process.
- With 20 years of use, the condition and features of the park were outdated and not fit for all skill levels.
- New features can be enjoyed by all skill levels, age groups, and different wheeled recreational devices.
- Park improvements have been a start to area revitalization.

Project Funding

Project Phase	Year	Grants/Fundraising	Total
Design	2022-2023	\$0	\$10,000
Construction	2023	\$38,840	\$363,951
Testing	2023	\$0	\$9,276
Total		\$38,840	\$383,227
Original Budget Estimate	2022		\$75,000
2023 Omnibus	2023		\$315,000
Total			\$390,000



Before



After
