



CITY OF MEDINA

501 EVERGREEN POINT ROAD | PO BOX 144 | MEDINA WA 98039-0144
TELEPHONE 425-233-6400 | www.medina-wa.gov

Date: September 13, 2021
To: Honorable Mayor and City Council
Via: Michael Sauerwein, City Manager
From: Ryan Osada, Public Works Director
Subject: Public Works Monthly Report


1. CITY WIDE OVERLAY PROJECTS – Over the last few weeks, the city has seen several asphalt overlay projects being performed on our streets. Most recently NE 12th Street, Overlake Drive West and 77th Ave NE. These overlays are the restoration portion of the AC Watermain project that was completed by the City of Bellevue earlier this year. The overlay project for 84th Ave NE, between NE 12th Street & Overlake Drive West is currently scheduled to start at the end of September. This project will require a road closure which will have significant traffic impacts to the area.



2. NE 28TH ST BIKE TRAIL CROSSING – Earlier this year, the city received a complaint regarding the bollards located at the pedestrian/bike trail on NE 28th Street. There were two members of the Cascade Bike Club who had a near miss incident with the offset wood bollards that was originally installed by WSDOT. Over the course of 8 months, we were able to find an alternate design to remove the bollards and still provide a safe pedestrian/bike path for the community.




3. NE 12TH STREET UNDERGROUND PROJECT – The city is making progress with PSE to underground the utility lines located on NE 12th Street. An agreement has been signed to begin the design process to incorporate into the sidewalk project along this corridor. We are also coordinating the with the lighting team to install 15' concrete post-top LED Luminaires similar to the new section of 84th Ave NE.

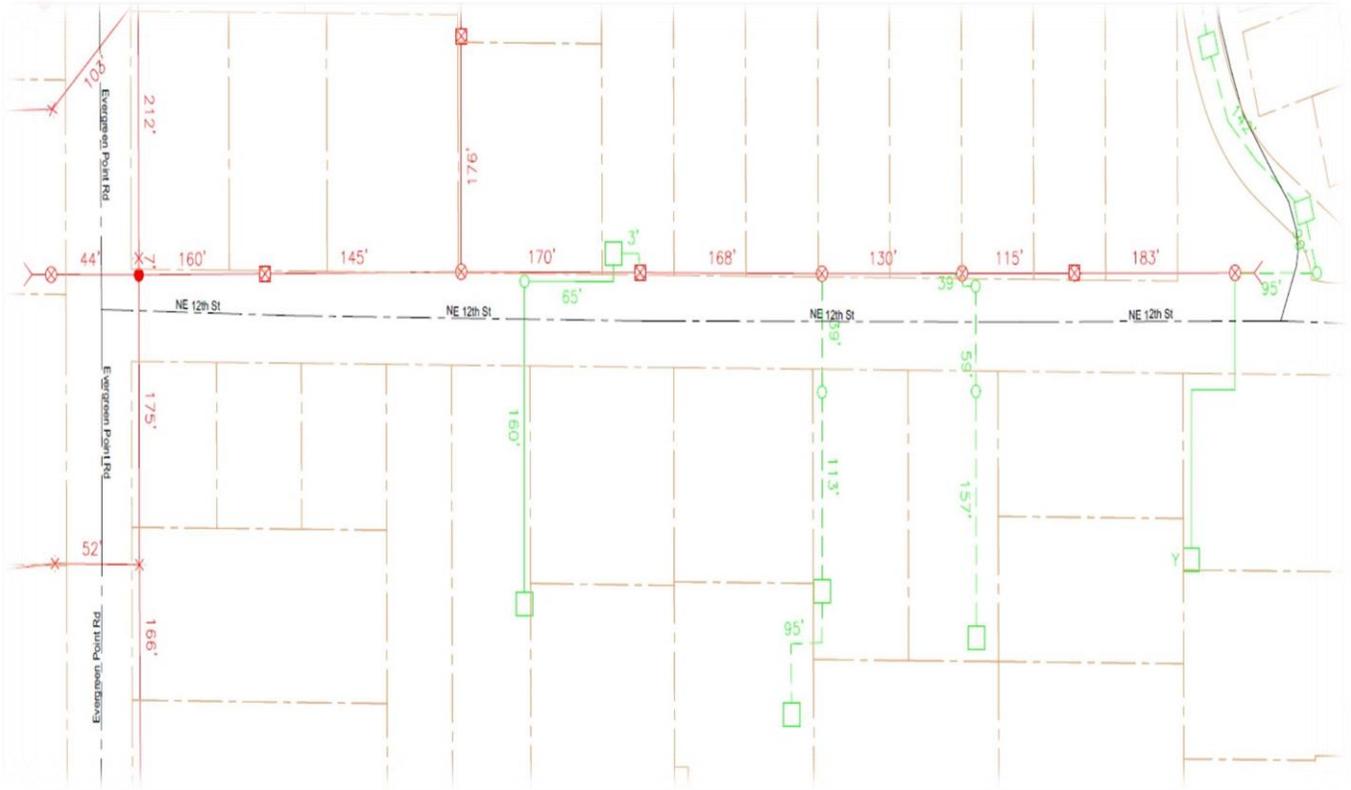

4. MAINTENANCE UPDATES – During the last two months, the Public Works Maintenance team has been busy with several projects including the Parking Lot Entrance revision. Watering has also been a priority during the summer drought. Garbage collection has become a large part of their daily routine due to the increase in park patrons during the pandemic. They also enjoyed working at the Medina Day event which was well attended and fun evening for the community.





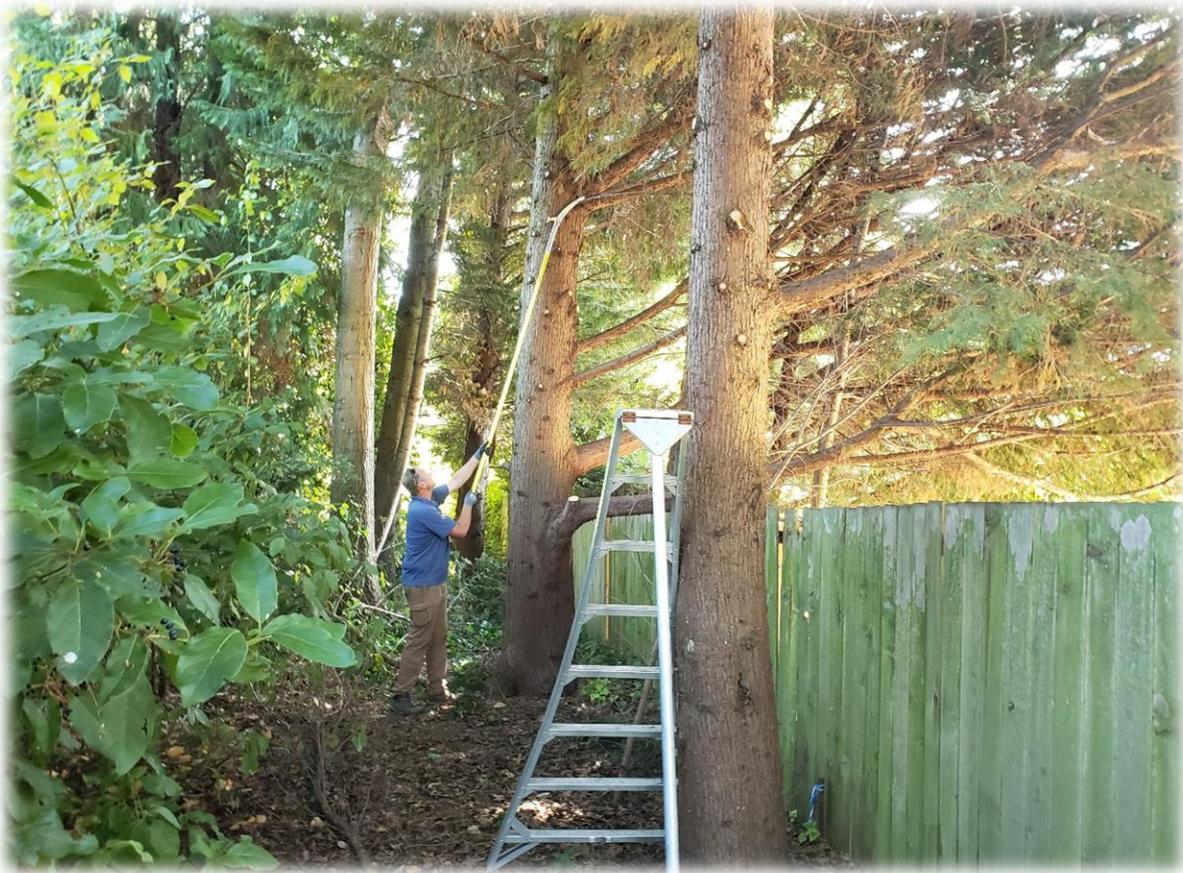

5. PROJECT UPDATES –

2015 Medina Park Stormwater Pond Imp. – Bravo Environmental has proposed vactoring to dredge the ponds. However, we are currently researching a method that will lessen the impact to the pond wildlife. In addition, recent estimates for material disposal are around \$900,000.00.

2017 Medina Beach Park Tree Replanting – Phase III tree planting.

TIB 84th Ave NE Overlay – NE 12th St to Overlake Drive – Scheduled for late September

2021 Overlay Program 77th Ave NE / NE 22nd St – completed

Medina Park Playground Improvements – The playground equipment is delayed and scheduled to arrive in November. This project has been rescheduled for Spring of 2022.

Post Office Floor Replacement – Planning schedule with the Post Office.

Citywide Stormwater System Mapping & Evaluation – G&O has completed most of the mapping. We are currently working on scoping and mapping the storm infrastructure that is located on several private properties.

2021 Hazardous Tree Removal – in review

NE 12th Street Sidewalk Improvements – Draft construction plans, and application has been submitted to PSE for undergrounding review.

Fairweather Tennis Court Resurfacing – completed early.
