

Project Update

Engineering/Public Works

FY 2025-26

2nd and 3rd Quarter Reports


King's Gate Road Bridge Replacement Project



Site photo looking northeast

- ▶ **Let date:** August 2025
- ▶ **Engineer:** Bartlett & West (Texas Department of Transportation's Consultant)
- ▶ **Contractor:** New contractor to be determined
- ▶ **Total Contract Amount:** \$1,536,598.58
- ▶ **Project Description:** The project consists of the removal and replacement of the King's Gate Road bridge over Clear Fork Trinity River. The project includes the approach roadways approximately 200' south of the bridge to the IH 20 frontage road and 100' north of the bridge.
- ▶ **Timeline:** To be determined.
- ▶ **Project Update:** Since the last project update the contractor working on the King's Gate bridge has gone out of business. The Surety has taken control of the project and is in the process of acquiring a new contractor to complete the work. TxDOT is waiting to hear from the Surety when they are ready to proceed. TxDOT is keeping an eye on the project site to ensure no site conditions change and that safety measures remain in place.


E. Bankhead Highway Utility Extensions, Phase 2

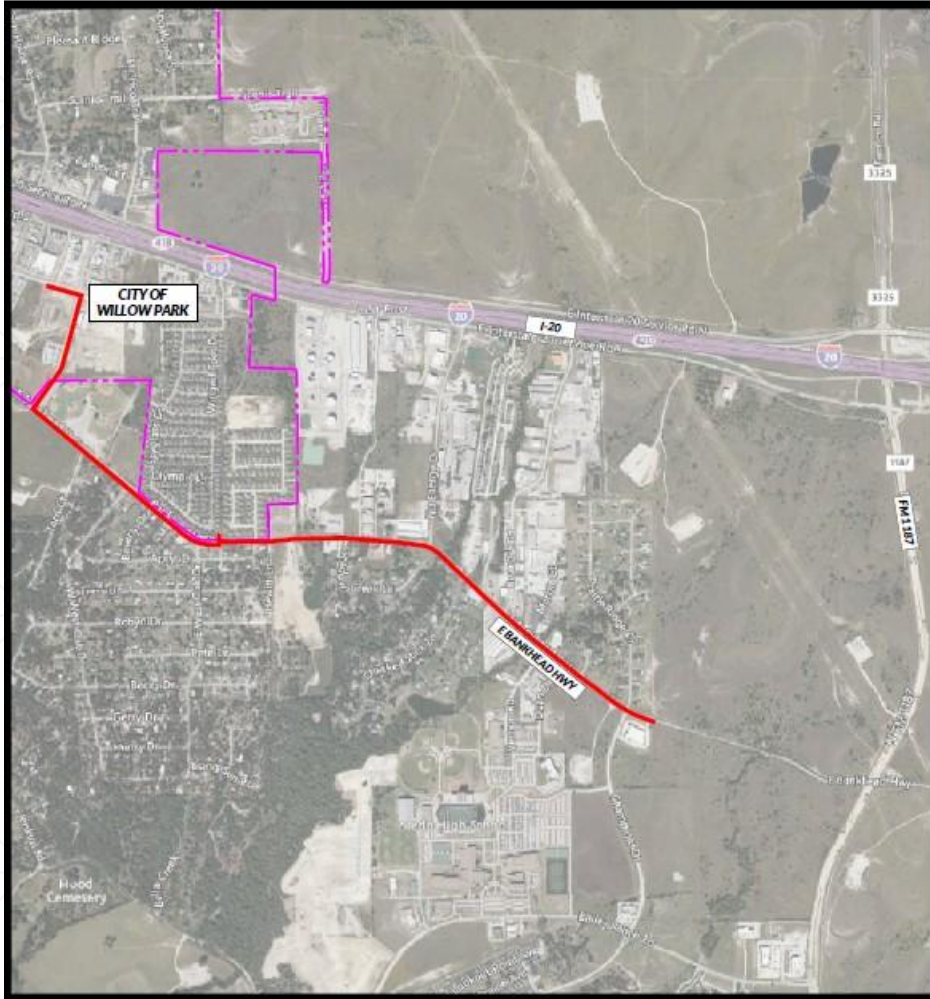

PROJECT LOCATIONS: ■

- ▶ **Engineer:** Jacob Martin, LLC
- ▶ **Contractor:** Skyblue Utilities, Inc.
- ▶ **Total Contract Amount:** \$4,122,003.40
- ▶ **Project Description:** The project consists of approximately 4,850 linear feet of 8" HDPE water line, 4,970 linear feet of 10" C-900 PVC sewer line, bores, valves, manholes and associated appurtenances.
- ▶ **Timeline:** 450 calendar days
- ▶ **Project Update:** City Council approved a construction contract with Skyblue Utilities on April 14th, 2026. Crews with BlueSky Utilities began work July 21st on the first phase of construction. Each section is expected to take 2-4 weeks to complete, weather permitting.
 - Section A (Cold Track Drive to Beverly Drive)
 - Section B (Cold Track Drive to Shadow Creek Lane)
 - Section C (Shadow Creek Lane to Nu Energy)

Texas Department of Transportation's 2025 Transportation Alternatives (TA) Set-Aside "Call for Projects"

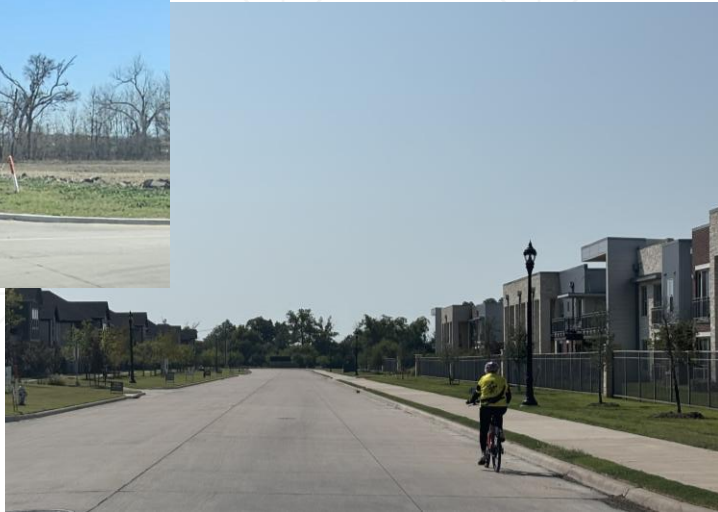

- ▶ The City of Willow Park Transportation Alternatives (TA) project was selected to receive federal funding for the construction of pedestrian and bicycle infrastructure.
- ▶ The City Council adopted a Resolution to enter into an Advance Funding Agreement (AFA) with the Texas Department of Transportation (TxDOT) for the design and construction of sidewalks, corner clips, crosswalks and bike lanes on Kings Gate and Meadow Place Drive.
- ▶ Awaiting Authorization of the Project
 - TxDOT must have an executed Federal Project Authorization and Agreement (FPAA) from the Federal Government, and
 - Local Government must have State Letter of Authority (SLOA)
 - Prior to Professional Services Procurement (RFQ)
 - Prior to Preliminary Engineering

Bankhead West Water Line Project



- ▶ **Engineer:** Jacob Martin, LLC
- ▶ **Contractor:** Contractor to be determined
- ▶ **Project Description:** The project consists of approximately 3,100 linear feet of 8" water line and river crossing with all associated appurtenances.
- ▶ **Project Update:** The City Council approved a water line loop along the I-20 service road and East Bankhead Highway. This water loop project has been in the City's Capital Improvement Plan since 2017. This project will improve water capacities and level out system pressures along the I-20 corridor, along with removing a dead-end main that requires monthly flushing. The 90% plans have been submitted to the city for review. The estimated project cost is \$647,300. The source of funding is from Impact Fees. The next step is to advertise for bids.

Water Supply and Infrastructure Grant (WSIG)

Eligible Projects. The grant must address at least one:

- **Water Loss**
- **TCEQ violation**
- **Provide additional water supply**

- ▶ House Bill 500, passed during the 89th Texas Legislative Session, appropriated a one-time \$1.038 billion in general revenue to the Texas Water Development Board (TWDB) for water supply and infrastructure projects and grants.
- ▶ City Council approved a Resolution authorizing the preparation and submission of a grant application to the TWDB.
- ▶ Jacob Martin Engineers are assisting staff with the application process.
- ▶ Application deadline is July 30th, 2026.

Removal of Existing Wastewater Treatment Plant

- ▶ **Engineer:** Jacob Martin, LLC
- ▶ **Bid Opening:** July 28th, 2026
- ▶ **Contractor:** TBD
- ▶ **Project Description:** This project consists of removal, demolition, and storage of an existing 0.495 MGD municipal wastewater treatment plant, including all associated equipment and appurtenances. Work includes decommissioning, cleaning, disinfection, sludge removal and dewatering, disposal of materials, protection of stored equipment, and site restoration.
- ▶ **Timeline:** 30 calendar days
