


Town of Century

Projects Update

May 6th, 2025

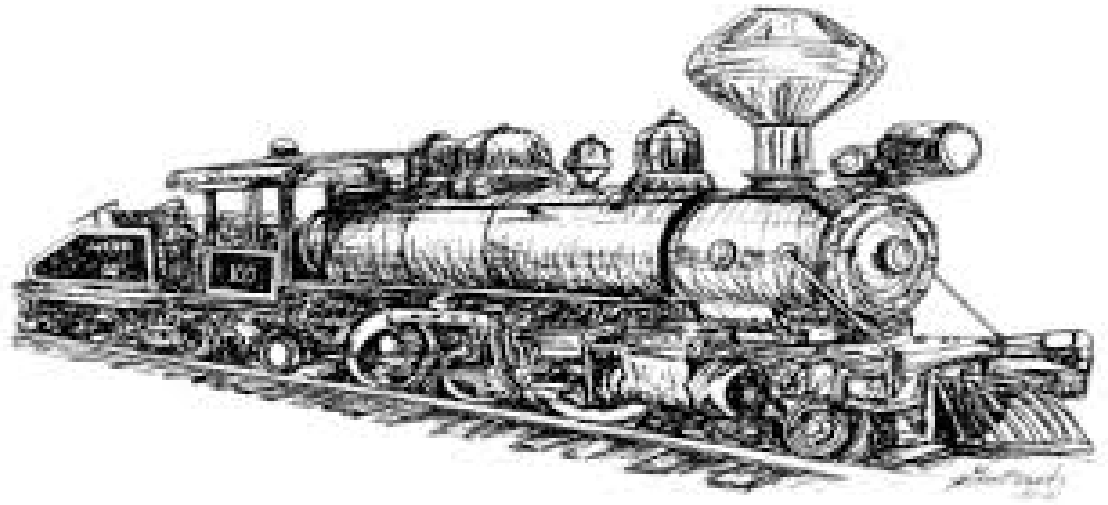

Purpose of Today's Presentation

- Status update of current projects.
 - Scope
 - Funding
 - Project Schedule
 - Current Status
- Status update of existing grants and new applications.
- Feedback and questions from Council.

Summary of Grants & Loans (1)

- FDEP Wastewater State Revolving Fund Loan (WW170301)
 - \$8,865,336 (90% PF & 10% Loan)
 - Miscellaneous Wastewater Improvements – Phase II
 - Lift Station Rehabs & WWTF Improvements
- State Legislative Appropriation Grant (LPA0150)
 - \$468,453 (100% grant)
 - Wells No. 1, 2, and 3 Rehabilitation
- State Legislative Appropriation Grant (LPA0284)
 - \$1,301,892 (100% grant)
 - Water Meter and Service Replacements.
 - Grant Managed by Escambia County.

Summary of Grants & Loans (2)

- State Legislative Appropriation Grant (G2P32)
 - \$1,297,000 (100% grant)
 - Freedom Road Bridge
- State Legislative Appropriation Grant (LPA0484)
 - \$628,500 (100% grant)
 - Well #3 Replacement
- FDEP Water State Revolving Fund Planning & Design Loan (DW17034)
 - \$150,000 (50% PF & 50% Loan)
 - Booster Pump Station Replacement
 - Well No. 1, 2, and 3 Improvements
 - Service Renewals.
 - Utility Billing Software.
- FDEP Pilot Grants
 - \$40,000 Well No. 2 Lime Feed System
 - \$1,360,500 Well No. 3 Replacement and Well Building Rehab

Overall: \$14 million in funding!

Well #3 Replacement



- **Scope:** Construction of new well at the prison water plant.
- **Funding:**
 - FDEP Grant LPA0484
 - SRF Loan DW17034
 - FDEP Pilot Grant
- **Status:** Bids received in November were higher than expected (\$1.2 million).
- **Next Step:** Final funding step in August 2025.
- **Completion:** 2026 (contingent on funding).



Next Meeting: Council update in June.

Freedom Road Bridge

- **Scope:** Bridge Replacement
- **Budget:** \$1,297,000
- **Funding:** FDOT Grant G2P32
- **Status:** Design & Permitting. Project On-Budget and On-Schedule.
- **Next Steps:**
 - 1) Receive US Army Core Permit (Under Review)
 - 2) Design & Permitting is 99% Complete
 - 3) Bidding (August 2025)
 - 4) Begin Construction (December 2025)
- **Completion:** October 2026



Lift Stations Rehabilitation

- **Scope:** Rehab Lift Stations

Prison LS #1

Century Woods LS #5

Highway 4 West LS #8

Jefferson Ave. LS #16

Pond and Jefferson LS #20


- **Budget:** \$3,365,175

- **Funding:** SRF Loan WW170301

- **Contractor:** Talcon Group.

- **Status:** Under construction. Delivery of equipment May/June.

- **Completion:** December 27th, 2025

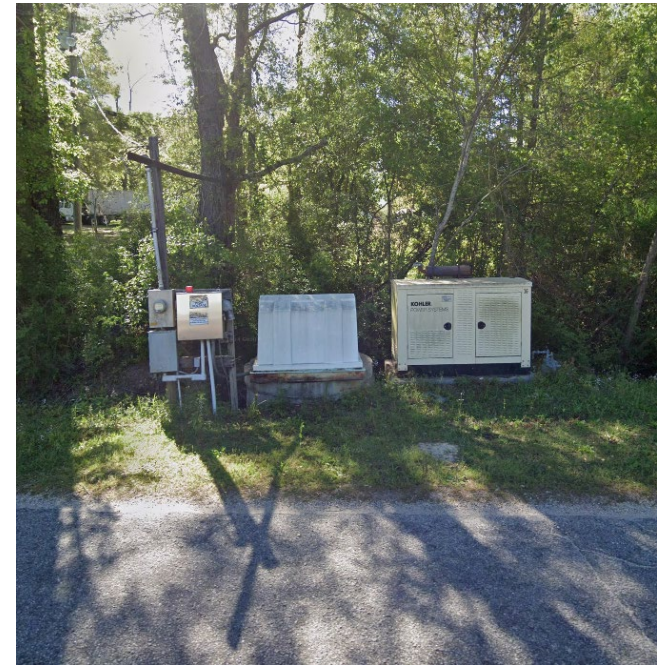

*Next Meeting:
Construction Progress Meeting
End of June 2025*

Wastewater Treatment Plant Improvements

- **Scope:** Miscellaneous Improvements

Sludge Screw Press.

Filter repair.

Automatic Transfer Switch.

Air line replacement.

EQ pump replacements.

Tank repairs.

Coatings

Etc.

- **Budget:** \$5,129,476

- **Funding:** SRF Loan WW170301

- **Status:** Project awarded (\$5,359,446). Initial tank repair activities have started.

- **Next Steps:** Continue construction.

- **Completion:** May 7th, 2026.



*Next Meeting:
Pre-Construction Progress Meeting
End of June 2025*

Wells No. 1, 2 and 3 Rehabilitations

Overall Budget: \$468,453

Funding: FDEP Grant LPA0150

- **Scope:** Well #2 - Electrical
 - **Status:** Awarded to Dunaway Electrical Services, Inc.
 - **Cost:** \$264,877
 - **Next Step:** Start construction in February 2025. Waiting on delivery of materials.
 - **Completion:**
~~December 2025~~ March 2026
- **Scope:** Well #2 - Building & Site
 - **Status:** Awarded to Evans Contracting, Inc.
 - **Cost:** \$334,707
 - **Next Step:** Start construction in February 2025.
 - **Completion:**
~~December 2025~~ March 2026

Next Meeting:
Construction Progress Meeting
June 2025

Next Meeting:
Construction Progress Meeting
June 2025

Well No. 1 & 3 improvements are currently unfunded.

Water Meter & Service Replacement

- **Scope:** Replacement of water service lines and meters throughout the distribution system.
- **Budget:** \$1.3 million
- **Funding:** FDEP Grant LPA0284
- **Status:** Awarded.
- **Next Steps:** Begin construction.
- **Completion:** December 2025

Next Meeting:

Pre-construction Meeting May 8th, 2025 at Town Hall

Future Projects

Known Needs

- Additional Well #1, #2, and #3 Improvements.
 - SRF is pending, and Pilot grant has been awarded.
- Tedder Rd. water booster pump station rehab ~\$500,000.
 - SRF is pending.

Future Needs

- Water service replacements → Applied for WMD Grant & Legislative appropriation, but unlikely to be funded. Apply through SRF program.
- SCADA system → Applied for Legislative appropriation (\$2 million).
- Motor Control Center replacement at WWTF (not funded).
- Remaining lift station rehabs (not funded).
- Develop a formal CIP & Master Plan (not funded).

Next Steps

- Continue advancing current projects.
Significant construction activities in 2025 & 2026 !
- Continue grant application efforts.
- Schedule an update to the Council (July 2025)?

Questions?

Daniel Magro, P.E.

Aclus Engineering, LLC

daniel.magro@acluseng.com
