



Monthly Status Report August 2026

City of LaBelle, FL



woodardcurran.com
COMMITMENT & INTEGRITY DRIVE RESULTS

Prepared for
Mayor Vince Ross

September 30,
2026

TABLE OF CONTENTS

SECTION	PAGE NO.
EXECUTIVE SUMMARY	ES-1
1. SAFETY	1-1
1.1 Monthly Safety Training	1-1
1.2 Safety Audit Update	1-1
2. FOG PROGRAM UPDATES	2-1
3. ENVIRONMENTAL COMPLIANCE ACTIVITY	3-1
3.1 Environmental Compliance Activity	3-1
3.2 Upcoming Compliance Events	3-1
4. CONSTRUCTION/REPAIRS/UPGRADES.....	4-1
4.2 Sentry Probe Events.....	3-1
5. WASTEWATER TREATMENT	5-4
5.1 Biosolids	5-4
6. WATER TREATMENT	6-1
7. CORRECTIVE AND PREVENTATIVE WORK ORDERS.....	7-1
8. PROJECT FINANCIALS	8-1
9. STAFFING	9-1

TABLES

Table ES1-1:	Vendors
Table 5-1:	WWTP Flows and Loads
Table 6-1:	City of LaBelle Water Production and Distribution
Table 8-1:	Project Financials
Table 9-1:	Project Staffing
Table 9-2:	Corporate Support

FIGURES

Figure 5-1	Effluent Flow vs Rainfall in Inches
Figure 5-2	Effluent Flow vs Influent Flow (MGD)
Figure 5-3	Effluent Biochemical Oxygen Demand (BOD)
Figure 5-4	Effluent Total Suspended Solids (TSS)
Figure 6-1	Deep Injection Well Volume
Figure 6-2	Finished Water Flow
Figure 6-3	Finished Water Chlorine Residual
Figure 7-1	Corrective and Preventative Work Order History Report

EXECUTIVE SUMMARY

This Monthly Status Report covers the reporting period from August 1st, 2026, through August 31st, 2026. August 2026 was another successful month of operations at the City of LaBelle's Water and Wastewater Project. "SAFETY" is always the number one priority at Woodard & Curran and as of August 31st, W&C staff have worked a total of 1763 days without lost time or recordable incident. In August, all the required monthly safety training was completed on time.

Woodard & Curran Regional Office

Woodard & Curran's local office location:
1511 N Westshore Blvd.
Tampa, FL 33607

Meetings

W&C project staff meet at the Water Plant every Monday and Friday mornings in person and every Tuesday through Thursday mornings remotely to discuss and plan the operational events of the day and discuss a daily tailgate safety topic. Other meetings held:

- 08/04/26: Water and Wastewater Scada Meeting
- 08/05/26: City, County, and W&C staff attended a "Lift Station Control Panel" training course
- 08/06/26: 1st Thursday Engineering and O&M Meeting
- 08/07/26: Biweekly Lift Station Rehab Meeting
- 08/20/26: 3rd Thursday Engineering and O&M Meeting
- 08/21/26: Biweekly Lift Station Rehab Meeting
- 08/25/26: WWTP Consent Order Discussion
- 08/28/26: Lift Station Rehab Budget Review

Vendors

W&C continues to reach out to potential project vendors to continue the Independent Contractor Agreement (ICA) and Purchase Order (PO) process. As invoices are received from the city, W&C starts the application process to create POs for each vendor. As of August 2026, the following vendors have been added to a W&C PO and/or (ICA) Independent Contractor Agreement.

TABLE ES1-1: VENDORS

Vendor Name and Address
PSI Technologies, Jeremy Fisher, 239-645-2698 3520 Investment Lane Unit 33 Riviera Beach FL 33404
Calusa Environmental, Trina Moore, 863-465-7155 PO Box 1347 LaBelle, FL 33975
Miller Septic North Environmental Inc. Lydia Billips 386-673-5550 19420 Doris Ln North Fort Myers, FL 33917
Restoration & Protective Solutions LLC. Peter Giustina II 941-575-1255 12705 Tamiami Trail Punta Gorda, FL 33955
Advanced Lift station services, Brett 239-292-6406, 1-888-993-5438

Vendor Name and Address
1871 Pine Ave Alva FL 33920
Pittsburg Tank & Tower Group Maintenance Division, Dennis Paquet dpaquet@pttg.com P: 270-826-9000 Ext: 4604 F: 270-215-5713 PO Box 1849 Henderson, KY 42419
CEC Controls Mark Bilbrey MBilbrey@cecccontrols.com (Cell 615-207-2409) 5306 4th Ave. Cir. E. Bradenton FL 34208
DM Integration Solutions, LLC Emily Dunn edunn@dmintegrationsolutions.com (Cell 207-899-5814) 10716 Bridegate Heights Loop San Antonio, FL 33576
Porterfield Oil Company Inc. 863-675-0565 1397 SR 29 South LaBelle FL 33935
Security Fence of SWFL, Pam Pletcher ((239) 369-5551 office), ((239) 340-6682 cell).
Indusco Environmental, Mike Thompson 251-621-2338 sales@induscoenviro.com 30914 Jay Drive, Spanish Fort AL. 36527
Hands Free Security, Service Department Service@handsfreellc.com (239-351-2871) 6063 Janes Lane Naples FL 34109
Trinova Inc., 4485 Laughlin Dr South Mobile AL 36693 2401 Draine Field Rd Lakeland FL 33811 (863-682-4500)
Southwest Ag Environmental LLC Tifton Holt 6755 State Road 80 LaBelle FL, 33935. (863) 885-4993 tkh@sw-env.com
MEEKS Plumbing Inc. 5555 US Highway 1 Suite 1, Vero Beach, FL 32967
Kyle Meeks PHONE: (772) 569-2285 FAX: (772) 569-7647
Florida Utility Solutions, LLC; Mitch Gilbert; 239-513-0445 15275 Collier Blvd. Suite 201, Naples, Fl. 34119
Wilbanks Mechanical LLC; Mike Wilbanks; (863) 269-3199; wilbanksmechanical@yahoo.com 25069 Marine Avenue Sebring, Fl. 33875
BAR Environmental, Inc.; Darien Rorabeck; (615)-373-0788; drorabeck@barenviro.com 100 Winners Circle Brentwood, TN. 37027

1. SAFETY

1.1 Monthly Safety Training

Woodard & Curran provides monthly safety training for all employees. Upon being hired, all new LaBelle employees receive an extensive array of health & safety training topics to get them fully up to speed on health and safety requirements. The safety topic for August 2026 was "Emergency Eyewash and Deluge Stations". Additionally, Woodard & Curran staff members hold regular safety meetings. Each workday a brief general safety topic will be discussed as well as any unusual conditions existing at the plants and any additional safety concerns that should be considered given those conditions.



All Woodard & Curran personnel assigned to the LaBelle project are participating in the (SPARKS) program. Employees who stay current on their monthly safety training, participate in monthly safety meetings, and who do not incur lost time from a work-related accident, are eligible to receive a SPARKS bonus at the end of the year. This bonus begins at \$200.00 and can reach \$500.00 based on five successive years of meeting SPARKS' goals.

Monthly Safety training completed by W&C staff in August consisted of:

- W&C Health & Safety Misc. Topics Daily Orientation (Tailgate).
- In August, W&C staff participated in a spark's safety meeting on Emergency Eyewash and Deluge Shower Stations.
- In August, there were no "Lost Time" accidents reported at the water or wastewater plant.
- In August, there were no "Lost Time" accidents reported at any of the city lift stations.

1.2 Safety Audit Update

"SAFETY" is always the number one priority at W&C. On October 22nd, 2025, a safety audit was performed at the City of LaBelle's Water and Wastewater Facilities which recorded 35 findings that yielded a total of 81 action items to be corrected. W&C's goal was to correct all action items in a timely manner, except items that require funding from Capital.


All safety audit action items have been corrected and completed.

2. FOG PROGRAM UPDATES FOR AUGUST 2026

Sewer Use Ordinance, Fats, Oil and Grease Program (FOG)

- Inspection and Compliance Summary
- Inspections Conducted: 0
 - Failed Inspections: 0
- Stores Out of Compliance: 16
 - Breakdown:
 - 16 stores have delayed submission of cleaning records.
- Remediation Efforts:
 - Actively coordinating with FSEs and cleaning companies to ensure timely report submissions and resolution of compliance issues.
- FSE Status Overview
- Total FSEs: 75
- Cleaning in Progress:
 - 14 FSEs are actively undergoing cleaning procedures.
- Pending Re-inspection:
 - 0 FSEs are out of compliance and awaiting re-inspection.

Successful Inspections: 1

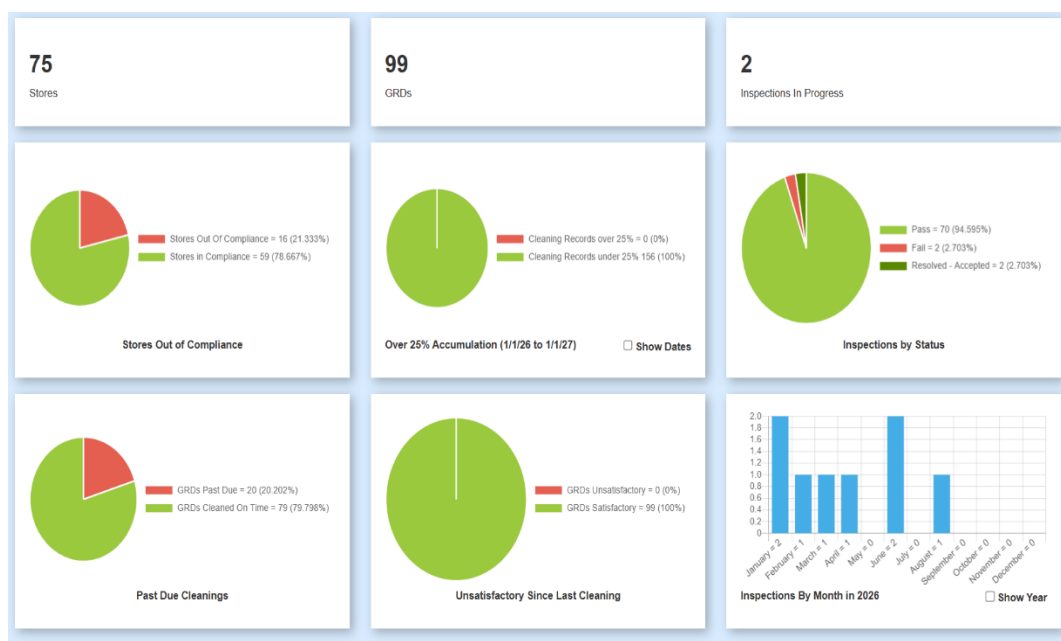

3. ENVIRONMENTAL COMPLIANCE ACTIVITY

3.1 Environmental Compliance Activity

Woodard & Curran strive for 100% compliance at both treatment plants. Below is a summary of the compliance activity for the month of August 2026.

- FDEP and SWFMD Regulatory Monthly Reporting
- Submitted both the Monthly Operating Report for Public Water System (PWS #5250050) and the Discharge Monitoring Report for the wastewater treatment plant to the Florida Department of Environmental Protection (DEP).
- Submitted the Deep Injection Well Discharge Monitoring Report in accordance with UIC Permit #329487-004-UO/1X to the DEP.
- Sampling & Laboratory Coordination:
- Collected wastewater composite, fecal, and bacteriological samples, and coordinated monthly compliance sampling with Eurofins Labs for the upper and lower monitor wells and deep injection well (Permit #98493 329487-004).
- Conducted additional wastewater composite and fecal sampling in accordance with DEP Permit #FLA014283-007.
- Collected the drinking and raw water bacteriological samples as required by 62-555, Florida Administrative Code (FAC)
- Operational Testing:
 - Weekly generator tests and monthly inspections were conducted, in compliance with 62-555.320(4)(a) FAC.

3.2 Upcoming Compliance Events

- PFAS the forever chemicals, the first quarterly testing will be performed by the end of this year (2026) on 6 PFAS variations.

4. CONSTRUCTION/REPAIRS/UPGRADES


- During the month of August 2026, W&C staff pressure washed, prepped, and painted both Concentrate Pumps, piping and concrete pump stands.



- Painted the High Service Pump pad caution yellow.



- Wilbanks Mechanical replaced a faulty pressure sensor on the CO2 system at the water plant and conducted annual maintenance on the system.

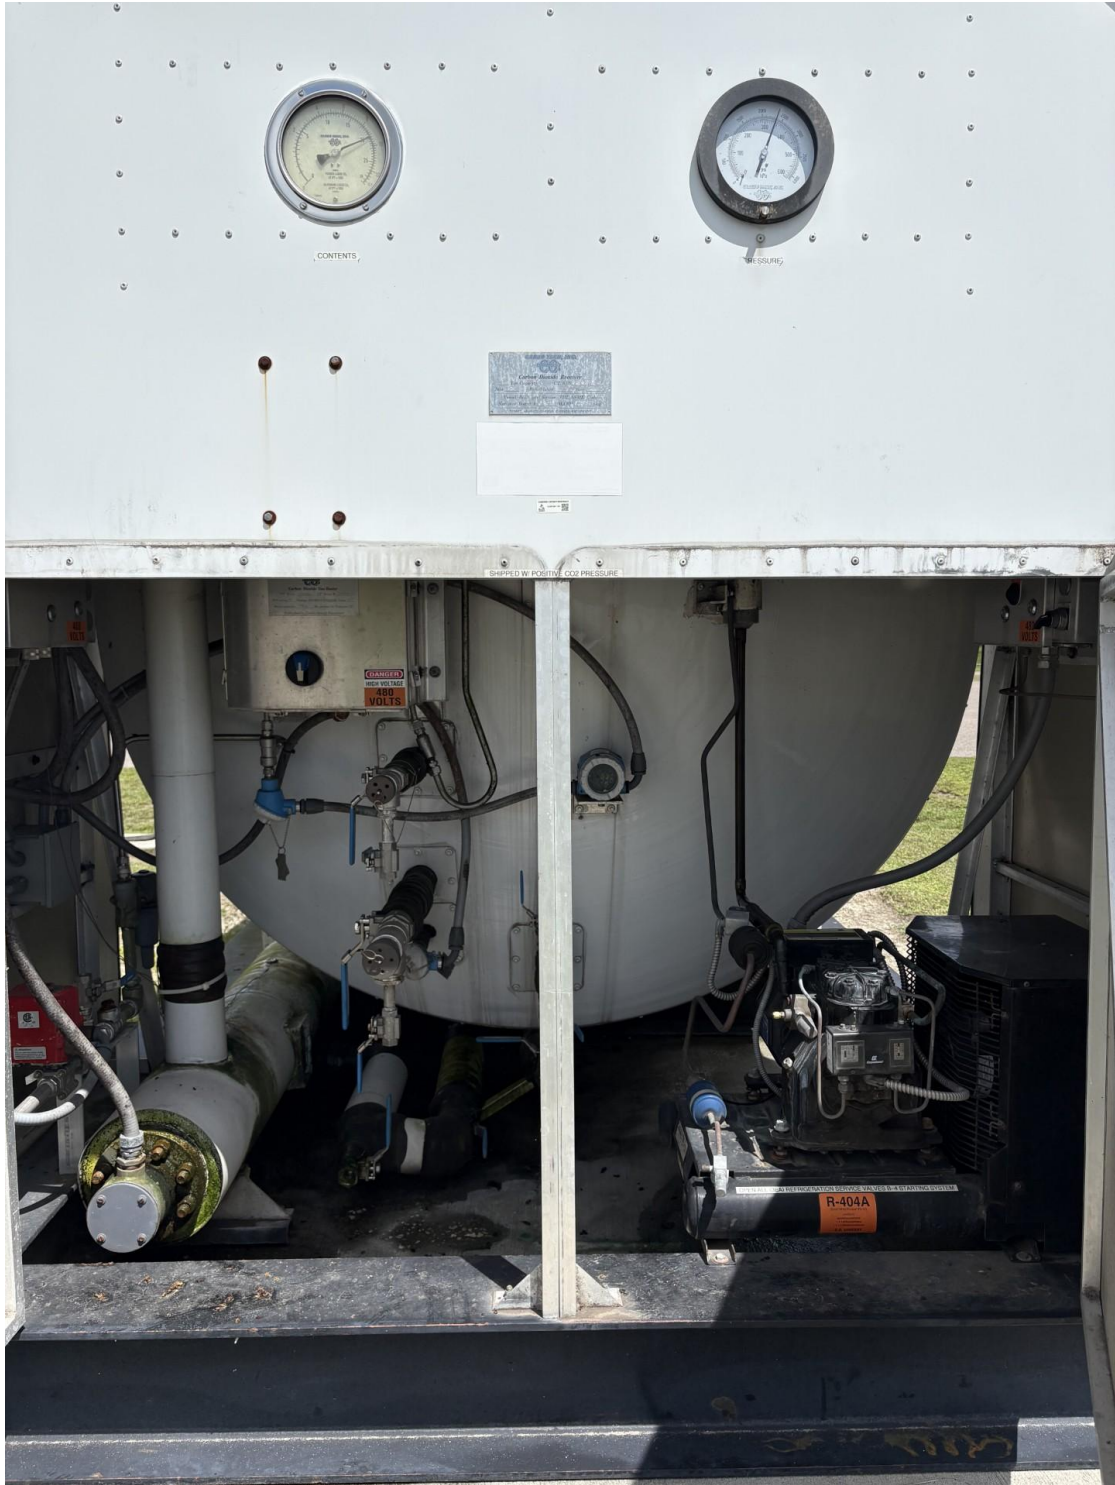

- On the night of 08/24/2026 the water plant experienced a direct lightning strike that caused numerous equipment failures. W&C staff responded immediately and began assessing the situation. It was discovered that 3 out of 4 high service pumps VFDs had been damaged and several other items around the plant had lost communication to VTScada. Some instrumentation was able to be restored quickly.
- On the morning of 08/25/2026 it was determined that the water plant could only run and produce water in manual mode (hand). Staff was able to produce water throughout the day to last through the following night. During this time W&C reached out to numerous vendors to source needed replacement equipment.
- On the morning of 08/26/2026 W&C located a spare VFD at their Bradenton project that could be utilized. W&C staff from Bradenton delivered and installed the VFD to restore redundancy to the distribution pumping station to ensure that residents of the city would not go without water. W&C Instrumentation Technicians arrived onsite and began troubleshooting and correcting VTScada communication issues.
- On 08/27/2026 W&C was able to order 3 permanent replacement VFDs with a PO provided by the city. W&C IT continued to correct communication issues.
- Mid-morning on 08/27/2026 the new VFDs were delivered, and replacement work began. By the end of the day, 3 of the 4 high service pumps were repairs and back in operation. W&C IT corrected most communication issues and ordered needed replacement parts.
- Follow-up work and repairs continued into September.



5. WASTEWATER TREATMENT

In August, WWTP had another successful month of operation. In accordance with the FDEP permit, W&C staff collected various compliance samples throughout the month. Summarized in Table 5-1 are the total flows for the influent and effluent as well as key permit constituents. The flows are displayed in Million Gallons per Day (MGD) Table 6-1 below, displays a one-year rolling average.

TABLE 5-1: WWTP FLOWS AND LOADS

Month	Influent Flow MGD	Influent BOD mg/L	Influent TSS mg/L	Effluent Flow MGD	Effluent BOD mg/L	Effluent TSS mg/L	Total Biosolids Transferred Dry Ton	Effluent Fecal Coliform Nor/100ml	Effluent Flow Quarterly Average MGD	Plant % Capacity %
Sep 2025	0.436	161	136	0.643	4.75	4.15	0.00	1,151.59	0.547	72.96
Oct 2025	0.373	267	134	0.571	5.00	8.35	0.00	2.44	0.578	77.00
Nov 2025	0.321	253	275	0.543	6.00	5.93	14.84	0.94	0.586	78.12
Dec 2025	0.303	274	179	0.515	7.40	5.50	0.00	2.29	0.543	72.40
Jan 2026	0.403	352	287	0.512	4.25	19.13	23.02	2.05	0.523	69.77
Feb 2026	0.476	401	493	0.480	3.25	8.55	8.84	54.89	0.502	66.97
Mar 2026	0.478	396	378	0.495	7.00	8.33	17.75	4.66	0.496	66.08
Apr 2026	0.474	328	289	0.507	3.50	3.55	0.00	2.18	0.494	65.88
May 2026	0.456	336	426	0.522	3.50	2.30	25.13	3.22	0.508	67.72
Jun 2026	0.421	327	347	0.511	4.80	4.24	0.00	170.11	0.513	68.43
Jul 2026	0.370	287	213	0.469	5.25	1.40	16.73	6.51	0.501	66.74
Aug 2026	0.387	260	259	0.576	4.68	1.96	0.00	4.43	0.518	69.13
Minimum	0.303	161	134	0.469	3.25	1.40	0.00	0.94	0.494	65.88
Maximum	0.478	401	493	0.643	7.40	19.13	25.13	1,152	0.586	78.12
Total	4.897	3,641	3,416	6.344	59.38	73.37	106.32	1,405	6.309	841.20
Average	0.408	303.50	285	0.529	4.95	6.12	8.86	117.11	0.526	70.10

5.1 Biosolids

- In August, 0.00 dry tons of biosolids were processed by SynaGro.

FIGURE 5-1 EFFLUENT FLOW VS RAINFALL IN INCHES

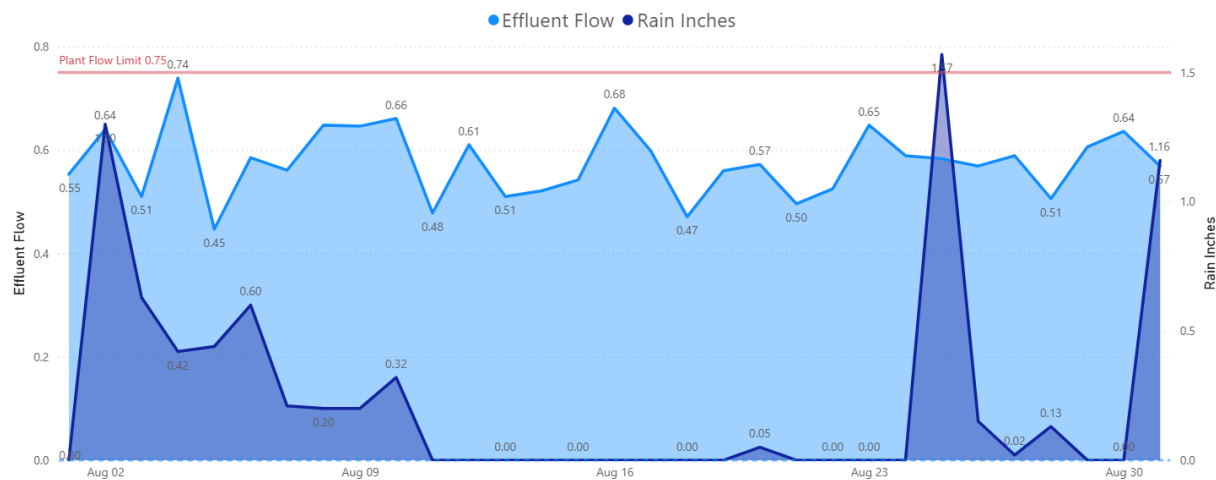


FIGURE 5-2 EFFLUENT FLOW VS INFLUENT FLOW (MGD)

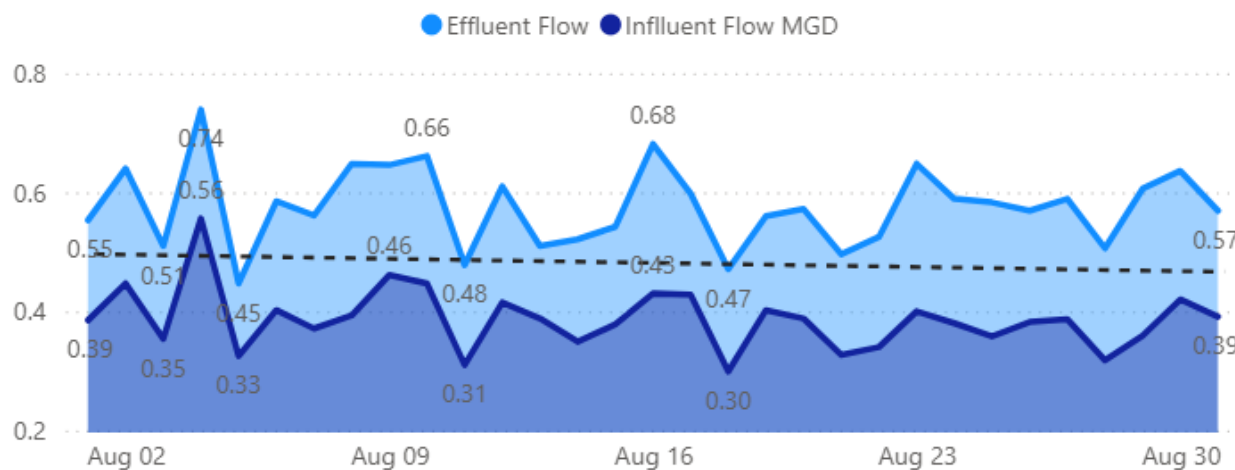


FIGURE 5-3 EFFLUENT BIOCHEMICAL OXYGEN DEMAND (BOD)


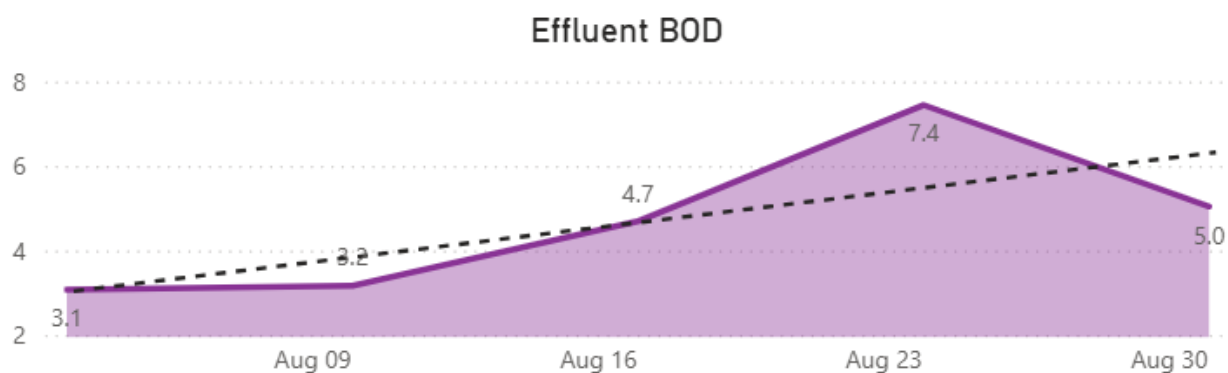


FIGURE 5-4 EFFLUENT TOTAL SUSPENDED SOLIDS (TSS)

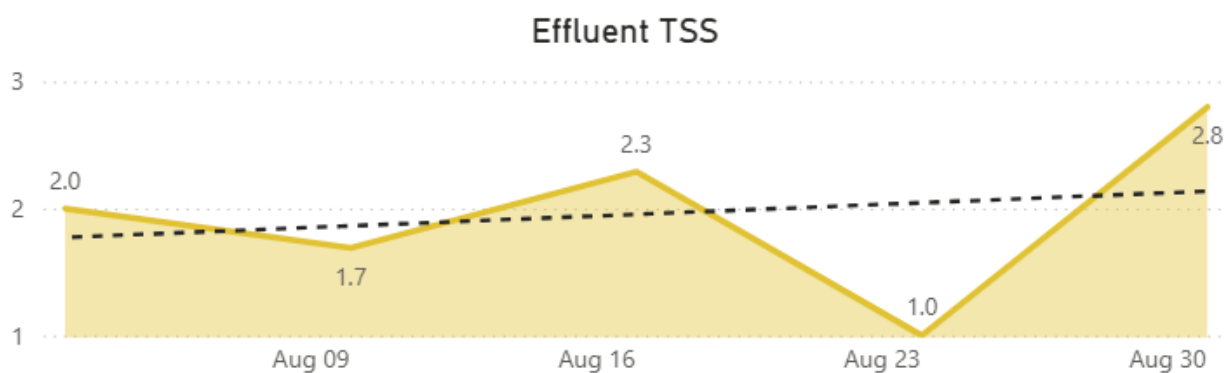

6. WATER TREATMENT

Below is a table representing the average MGD of water pumped from the groundwater supply wells and finished treated water leaving the plant. The water loss data derives from the delta between the total treated water leaving the plant and the metered customer usage and is represented in the percentage of water loss. Table 6-1 represents a 12-month rolling average of the data.

TABLE 6-1: CITY OF LABELLE WATER PRODCUTION AND DISTRIBUTION

Month	Well 102 Total Flow MGD	Well 103 Total Flow MGD	Total Volume Withdrawn MGD	Finished Water Treated MGD	Total Injection Well Volume MG	Line 11 Water Loss %
Sep 2025	0.371	0.693	0.995	0.776	0.236	31.76
Oct 2025	0.805	0.802	1.011	0.725	0.259	22.96
Nov 2025	0.001	1.008	1.008	0.809	0.248	31.02
Dec 2025	0.000	0.977	0.977	0.751	0.234	27.28
Jan 2026	0.633	0.535	0.932	0.764	0.216	6.37
Feb 2026	0.853	0.118	0.929	0.766	0.219	28.13
Mar 2026	0.816	0.660	1.424	0.747	0.206	28.47
Apr 2026	0.276	0.574	0.850	0.724	0.195	16.02
May 2026	0.353	0.596	0.930	0.782	0.225	26.76
Jun 2026	0.280	0.546	0.826	0.692	0.232	15.00
Jul 2026	0.649	0.529	0.938	0.616	0.215	15.27
Aug 2026	0.361	0.425	0.772	1.187	0.219	100.00
Minimum	0.000	0.118	0.772	0.616	0.195	6.37
Maximum	0.853	1.008	1.424	1.187	0.259	100.00
Total	5.399	7.462	11.592	9.339	2.702	349.05
Average	0.450	0.622	0.966	0.778	0.225	29.09

FIGURE 6-1 DEEP INJECTION WELL VOLUME

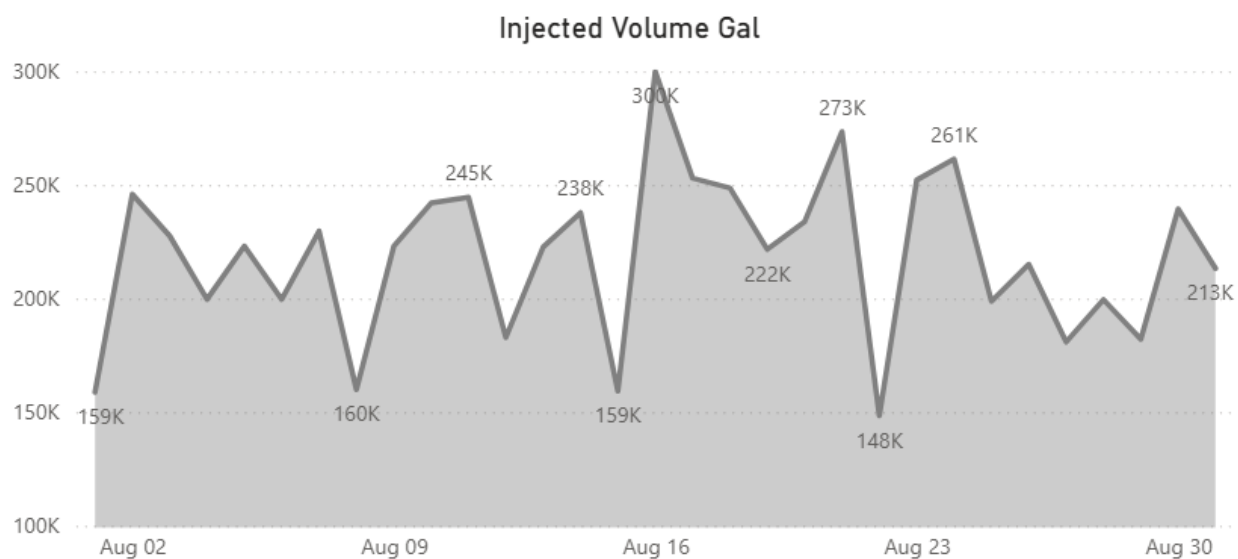


FIGURE 6-2 FINISHED WATER FLOW


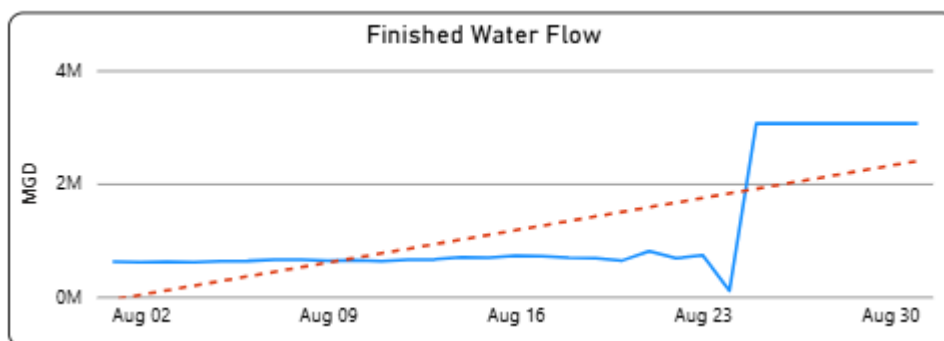


FIGURE 6-3 FINISHED WATER CHLORINE RESIDUAL

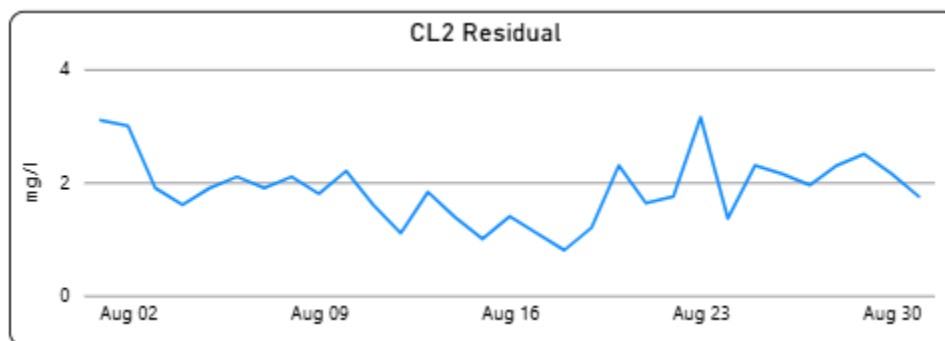

7. CORRECTIVE AND PREVENTATIVE MAINTENANCE WORK ORDERS

FIGURE 7-1 CORRECTIVE AND PREVENTATIVE MAINTENANCE WORK ORDER HISTORY REPORT


Maintenance History Report

Labelle, Florida



Report Start: 8/1/2026
Report End: 8/31/2026

Work Orders by Type	Total
Corrective Maintenance	207
Preventative Maintenance	124
Inspections	20
Total	351

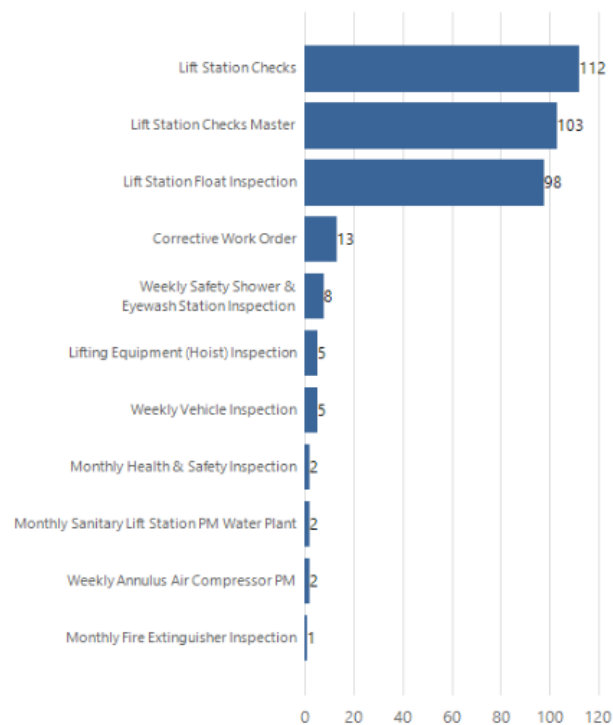

Top Work Orders by Description

8. PROJECT FINANCIALS FOR AUGUST 2026

TABLE 8-1: PROJECT FINANCIALS FOR AUGUST 2026 (YEAR 5)

- Due to W&C transitioning into a new finance system/software, we are unable to provide the financials for the month of August 2026 currently. As soon as the financials can be calculated, they will be sent to the city via email. The financial details below are from July 2026.

Budget Category	Month Actual	Month Budget	YTD Actual	YTD Budget	Annual Budget	over (under)	% of budget
Labor (D.L. + FB)	\$46,667	\$58,828	\$581,564	\$588,279	\$705,935	(\$6,716)	82%
Utilities	\$159	\$925	\$8,130	\$9,250	\$11,100	(\$1,120)	73%
Chemicals Costs	\$17,642	\$20,554	\$140,882	\$205,542	\$246,650	(\$64,660)	57%
Maintenance and Repair Costs	\$5,518	\$16,144	\$241,904	\$161,438	\$193,726	\$80,466	125%
Sludge Disposal Costs	\$0	\$7,500	\$130,436	\$75,000	\$90,000	\$55,436	145%
Lab Supplies & Equipment	\$1,462	\$5,863	\$85,595	\$58,630	\$70,356	\$26,965	122%
Office Supplies	\$0	\$283	\$6,302	\$2,833	\$3,400	\$3,469	185%
Miscellaneous Expenses	\$18,731	\$6,876	\$117,725	\$68,758	\$82,510	\$48,967	143%
Overhead (G&A of D.L.)	\$12,444	\$15,687	\$155,084	\$156,874	\$188,249	(\$1,791)	82%
Subtotal of Costs for Contract Year	\$102,623	\$132,661	\$1,467,621	\$1,326,605	\$1,591,926	\$141,016	92%
Fixed Fee for Contract Year 2	\$8,210	\$10,613	\$117,410	\$106,128	\$127,354	\$11,281	92%
Total	\$110,833	\$143,273	\$1,585,031	\$1,432,733	\$1,719,280	\$152,297	92%

9. STAFFING

TABLE 9-1: PROJECT STAFFING

Name	Title	Certifications
Robert Archer	Project Manager	FDEP B Wastewater License
Salvador Mora	Assistant Project Manager	- FDEP B Water License - TREEO/AWWA Backflow Tester/Repair Certified
Doug Denning	Operator I	FDEP C Wastewater License
Denis Ortega	Part Time: Operator II	- FDEP C Wastewater License - FDEP A Water License
John Smith	Operator II	- FDEP A Wastewater License - FDEP C Water License
Ubaldo Guzman	Maintenance Technician II	- FDEP Level 1 Distribution License - Backflow Tester/Repair Certified

TABLE 9-2: CORPORATE SUPPORT

Name	Title	Support Provided
Alyson Watson	CEO	Management Support
Brian Bzdawka	Senior Vice President O&M Business Center Manager	Management Support
Marc Thomas	National Operations Leader	Management Support
Bri Morales	O&M Operations Leader	Management Support
Fred Rogers	Area Manager	Management Support
Shannon Eyler	Director of Health & Safety	Health & Safety
Steve Lindeman	Health and Safety Manager	Health & Safety
Renea Shields	Health and Safety Coordinator	Health & Safety
Ron Harrison	SCADA Technician	SCADA and Technical Services
Alan Fabiano	IT Coordinator	Utility Cloud (Computerized Maintenance Management System), HACH WIMS (Laboratory Information

Name	Title	Support Provided
		Management System), Tablets & Technology
Jeannie Dubois	MIS Support Specialist	Computer and Network set-up and support
Celina Bland	O&M Specialist	Hach WIMs, Utility Cloud and Power BI programming and support
Jackie Smith	Senior Project Assistant	Project Support Specialist
Sarah Coen	Human Resources – Benefits Administrator	Employee Benefits
Linsay McAuliffe	Senior Talent Management Partner- HR & Compliance	Human Resources
Beth Sweitzer	Senior Talent Management & Acquisition Manager	Human Resources
Vanessa Luberto	Talent Management Partner	
Lizzie Dovich	Technical Recruiter	Human Resources
Wendy Foreman	Health & Safety Administrator	Health & Safety Support
Sam Stanley	O&M Specialist	O&M Project Support
Justin DeMello	Project Manager II	Engineering Support
Tami Ray	Funding Specialist	Engineering Support
Troy Kepley	Operations Specialist	Operations and Management

A large, light blue, stylized 'A' watermark is positioned in the background of the lower half of the page. It is composed of several overlapping, curved lines that form a triangular shape.

woodardcurran.com
