


**FIBER AND HH PLACED
ON PROJECT A05BVSE**

**PLACE GROUND FIELD
AT EXIST HH FOR SPLICE**

**PLACE HH NEAR POWER
PEDS FOR UNIFORMITY**


**PULL FIBER TAIL BACK THROUGH
IPP TO BE PLACED ON PROJECT
A05BVSE 200' -BORE UNDER CADOTTE
3-5' DEEP THEN 1-3' OFF EDGE OF RD IN
GREENBELT APPROX 200' -PLACE NEW HH
AND CORE INTO BASEMENT UTILITY ROOM
-CUSTOMER TO PROVIDE BB, POWER AND
GROUND -SITE CONTACT ANDY RYNBERG
906-440-6618 -ALL RESTORAL MUST BE TO
THE SATISFACTION OF MACKINAW ISLAND
MUNICIPALITY, RESIDENTS AND BUSINESS
OWNERS -CITY CONTACT IS DAVE LIPOVSKY
906-847-4035**

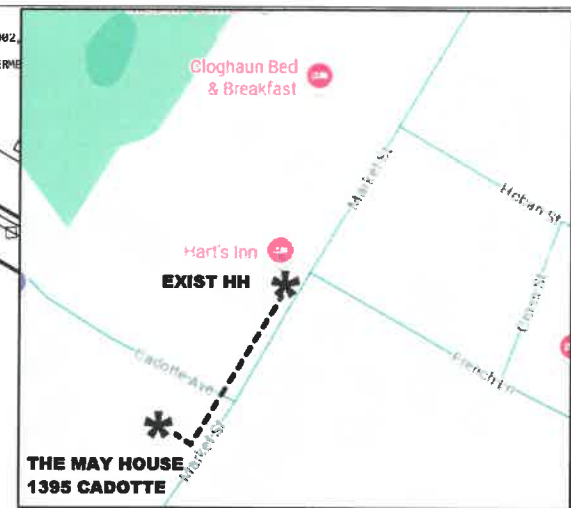

**MACKINAW ISLAND
MACKINAC COUNTY**

PROJECT # A05CCQH		DATE SVC REQ'D 05/12/2026	
NPANNX 906847	GEO LOC M29921	CLL mcismimn	
PRIMARY ENGR.: COLLARD, JEFFREY			
ENGR. ID: JC7632		PERMIT REQ'D.	N
PHONE #: 5867648260		PRINT 1 OF 2	

4

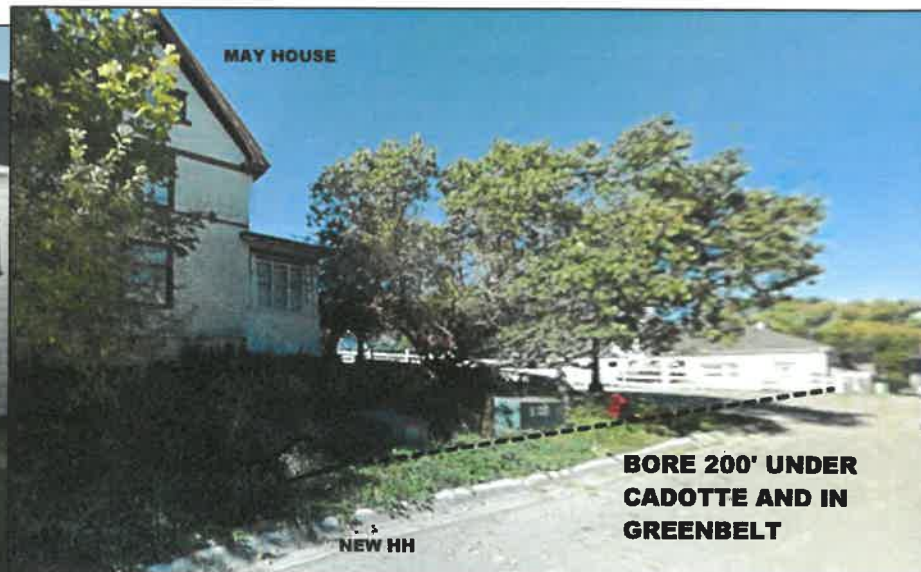

NO PICTURE OF UTILITY ROOM DUE TO IT BEING UNDER CONSTRUCTION AT THE TIME OF SITE SURVEY -CUSTOMER TO PLACE BB, POWER SOURCE AND GROUND

PROJECT #		DATE SVC REQ'D
A05CCQH		05/12/2026
NPANNX	GEO LOC	CLLI
906847	M29921	mcismmn
PRIMARY ENGR.: COLLARD, JEFFREY		
ENGR. ID: JC7632	PERMIT REQ'D:	N
PHONE #: 5867648260	PRINT 2	OF 2
