



CITY OF MEDINA

501 EVERGREEN POINT ROAD | PO BOX 144 | MEDINA WA 98039-0144
TELEPHONE 425-233-6400 | www.medina-wa.gov

Date: March 13, 2023
To: Honorable Mayor and City Council
Via: Stephen R. Burns, City Manager
From: Ryan Osada, Public Works Director
Subject: Public Works Monthly Report

- 1. BELLEVUE AC WATERMAIN RESTORATION** – Bellevue Water is currently replacing the AC Main at 79th Place NE which is the last location for the FY2021 project. The contractor is also finalizing restoration and asphalt patching along NE 14th Street and Evergreen Point Road. Bellevue's Transportation Department reached out regarding schedule to overlay the road surfaces this summer.



2. **2023 PHASE 2 AC WATERMAIN REPLACEMENT_BELLEVUE** – As briefly discussed at a previous council meeting, Bellevue Water is planning to replace the AC Watermain along NE 18th Street, Rambling Lane and 73rd Ave NE. This corridor has several challenges for the contractor since the street is narrow with several sharp turns. Bellevue Water and their contractor will need to propose a viable plan to provide adequate ingress and egress for the residents and emergency vehicles. This section is anticipated to take three months to complete.

NOTICE OF UPCOMING WORK in Your Neighborhood in 2023-2025

The City of Bellevue Utilities Department is designing a new ductile iron water main that will replace existing asbestos-cement (AC) water main along your street or a street nearby in your neighborhood. This is part of the city's annual water main replacement program. The program entails replacing small diameter AC pipe that does not meet current fire flow standards.

Surveying and design field work will occur in 2023 and 2024. Construction in your area is expected to occur sometime during the years 2024 to 2025. Once a contractor is selected for the project, additional notification will be sent prior to the start of construction in your neighborhood.

For questions contact:
Paige Young, Consultant Project Manager, 425-452-2067 or
pyoung@bellevuewa.gov.


Thank you for your cooperation.




For alternate formats, interpreters, or reasonable accommodation requests please phone at least 48 hours in advance 425-452-2067 (voice) or email pyoung@bellevuewa.gov. For complaints regarding accommodations, contact City of Bellevue ADA/Title VI Administrator at 425-452-6168 (voice) or email ADATitleVI@bellevuewa.gov. If you are deaf or hard of hearing dial 711. All meetings are wheelchair accessible.

정보 Information 情報
Información معلومات
సమాచారం
اطلاعات
सूचना 425-452-6800 資料

3. LAKE WASHINGTON LAKE LINE MANAGEMENT – Bellevue Sewer is in the early stages of developing a Lake Line Management Plan. As stated in a recent meeting, the plan will help minimize risk of failures, provide reliable service and identify potential improvement projects or strategies. Bellevue’s project goals will include phasing future repairs and operations. The final management plan is schedule for review early 2024.

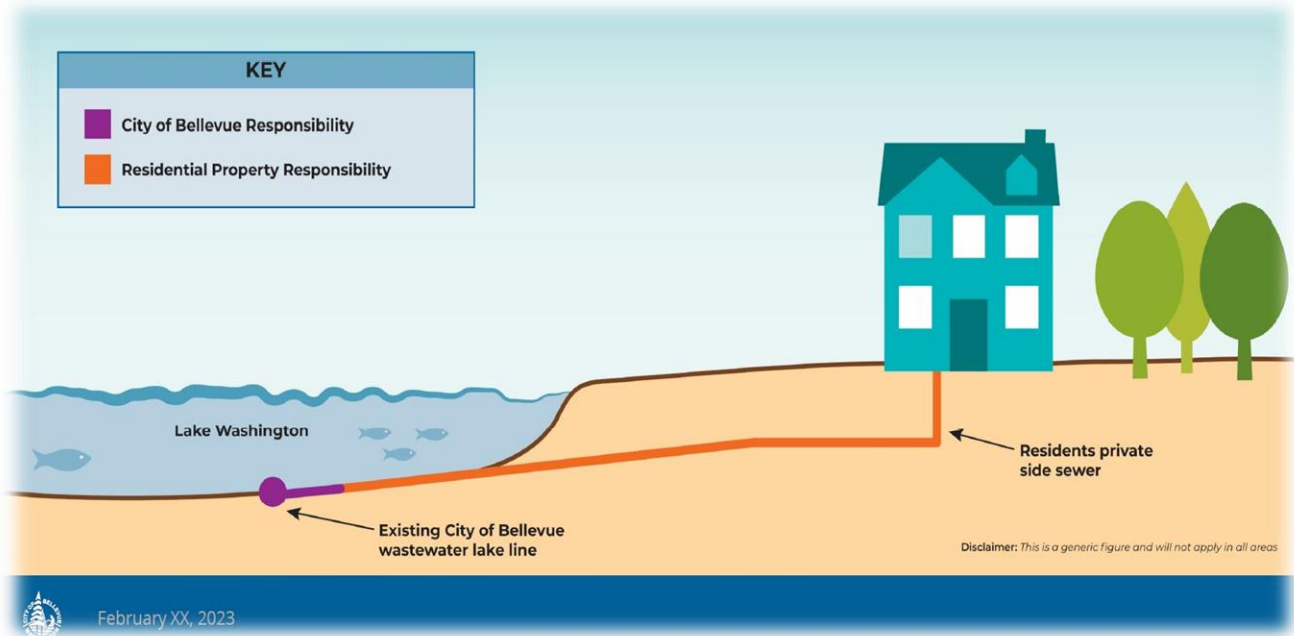

- 4. MAINTENANCE** – For the last three years, the month of February has been the busiest in terms of weather-related events. The Public Works Staff were on-call more in February than any of the other months. In addition to the de-icing and plowing, we have also scheduled improvements to the Post Office Floor. As the weather gets warmer, we will transition into springtime tasks with more concentration in our beautiful parks.

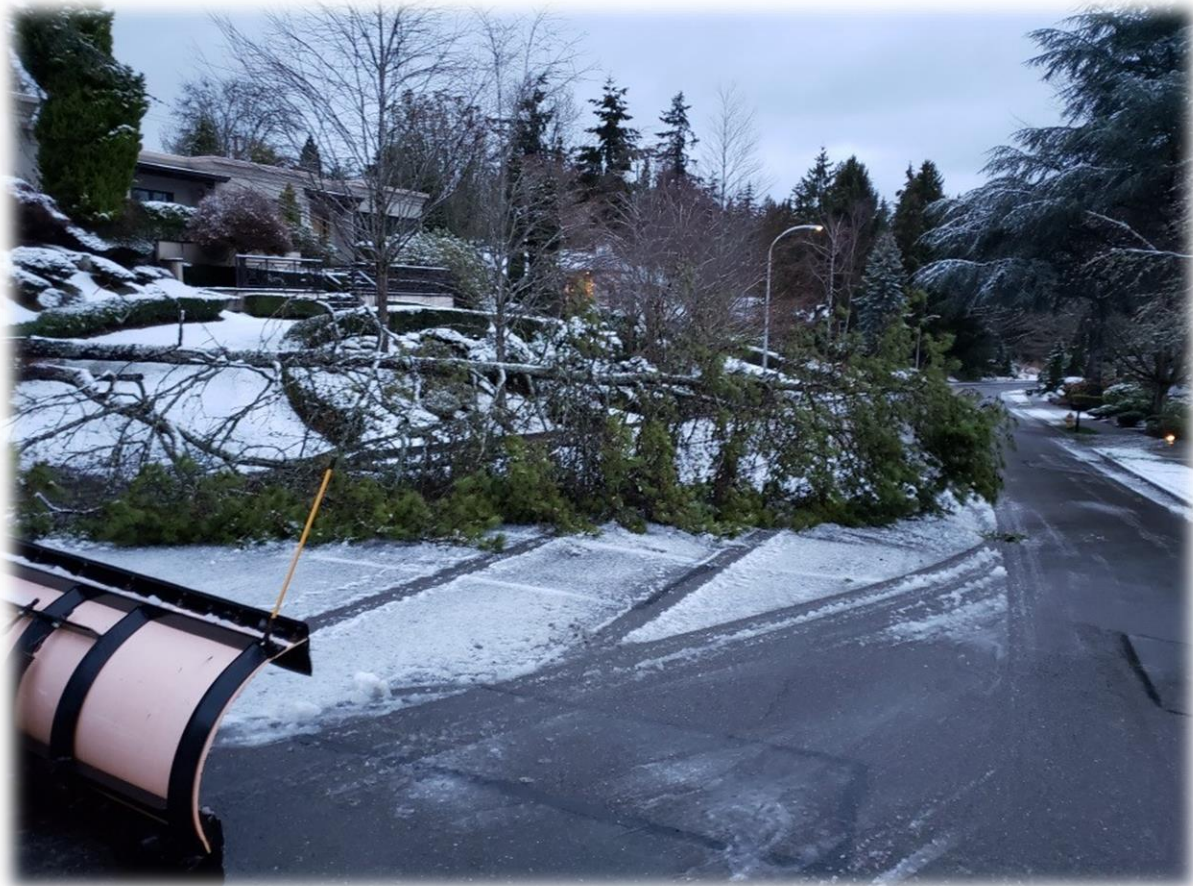

5. PROJECT UPDATES -

Upland Road Overlay – in design with KCDOT

86th Ave NE Overlay – in design with KCDOT

2023 Crack Seal – reviewing specs, go out for bid March

Medina Elementary Sidewalks_81st Ave NE – design

Medina Park Irrigation & Pathway Improvements_West – go out for bid March

2023 Upland Road Stormwater Improvements – in design

City Hall Carpet Replacement – soliciting bids

Post Office Floor Replacement – Public Works Staff in March

2023 Hazardous Tree Removal – summer

Citywide Stormwater System Mapping & Evaluation – G&O has completed most of the mapping. We are currently working on scoping and mapping the storm infrastructure that is located on several private properties.

NE 12th Street Sidewalk Improvements & Undergrounding – Final construction drawings are complete. Waiting approval by Intolight, Lumen and Comcast. Scheduled to Bid May, construct early summer.

2022 City Hall Repairs – Miscellaneous – Balcony – design

77TH Ave NE Sidewalk & Curb Ramp Imp. – reevaluating scope of work

2017 Medina Beach Park Tree Replanting – Phase III tree planting.

2015 Medina Park Stormwater Pond Imp. – Dredging is tentatively planned for summer of 2024
